

Office of Active and Abandoned Mine Operations

# SKIDMORE BED CROPFALL SUBSIDENCES Abandoned Mine Reclamation Project Contract No. OSM 22(0458)101.1 EMER

Bureau of Abandoned Mine Reclamation 2 Public Square, 5<sup>th</sup> Floor Wilkes-Barre, PA 18701-1915

## DEPARTMENT OF ENVIRONMENTAL PROTECTION OFFICE OF ACTIVE AND ABANDONED MINE OPERATIONS BUREAU OF ABANDONED MINE RECLAMATION

#### SKIDMORE BED CROPFALL SUBSIDENCES ABANDONED MINE RECLAMATION PROJECT CONTRACT NO. OSM 22(0458)101.1 EMER

#### **FACT SHEET**

**Location:** The project is located on Pennsylvania State Game Lands No. 264,

Bear Valley Road, Williams Township, Dauphin County.

Watershed: West Branch Rausch Creek

Official Start Date: January 13, 2022

**Contract Completion Date:** February 7, 2022

**Contractor:** Morgan's Excavating, LLC of Mount Union, PA

**Property Owner:** Pennsylvania Game Commission

**Project Cost:** \$39,879.50 (Final Amount)

\$46,444.00 (Bid Amount)

**Project Area:** 0.5 acre

**Purpose:** To eliminate public health and safety hazards by backfilling two

crop fall mine subsidences on PA State Game Lands.

**Description:** Two mine subsidences on PA State Game Lands in Williams

Township, Dauphin County were reclaimed as an emergency project. The openings measured approximately 30-35 feet in diameter. The project work consisted of establishing an access road to the openings, a work safety zone around the subsidences, installing erosion and sedimentation controls, clearing and grubbing and backfilling the subsidences. There were 0.3 acres of land cleared and grubbed and over 1,200 cubic yards of on-site material was used to fill the subsidences. The disturbed areas were

then graded and seeded.


**Funding:** Abandoned Mine Land Program

**Project Management:** Bureau of Abandoned Mine Reclamation

Wilkes-Barre District Office (Contact: 570.826.2371)

### SKIDMORE BED CROPFALL SUBSIDENCES CONTRACT NO. OSM 22(0458)101.1 EMER

### Location Map

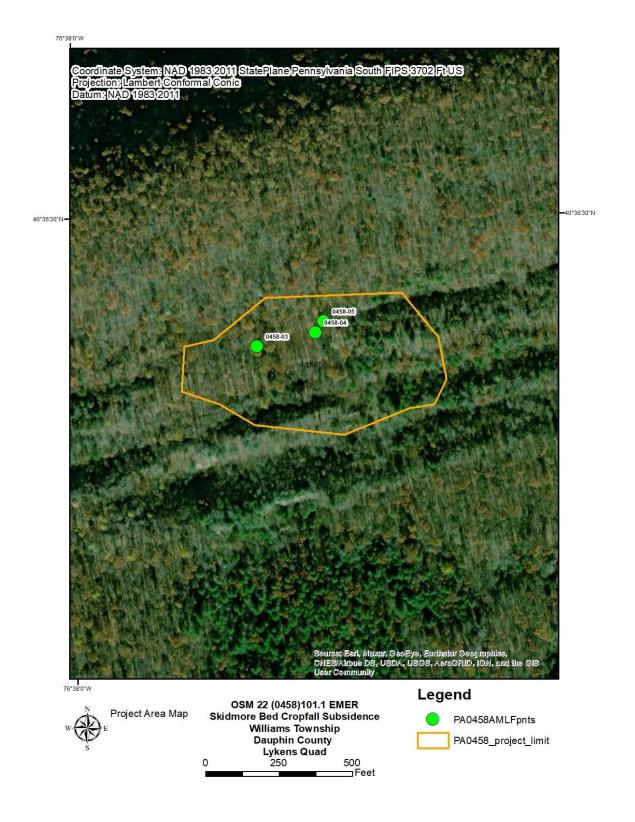

### SKIDMORE BED CROPFALL SUBSIDENCES CONTRACT NO. OSM 22(0458)101.1 EMER

#### **Pre-Construction**



AMLF 0458-03 (VO): vertical opening measuring approximately 30 feet in diameter.



AMLF 0458-04 (VO): vertical opening measuring approximately 35 feet in diameter.

#### SKIDMORE BED CROPFALL SUBSIDENCES CONTRACT NO. OSM 22(0458)101.1 EMER

**During Construction** 





AMLF 0458-04 (VO) after being backfilled

### SKIDMORE BED CROPFALL SUBSIDENCES CONTRACT NO. OSM 22(0458)101.1 EMER

### Post Construction



AMLF 0458-03 (VO) after seeding



AMLF 0458-04 (VO) after seeding
