Water Supply Assessment, Preparedness, Prevention and Contingency Plan

Pennsylvania Pipeline Project

Prepared for:
Sunoco Pipeline L.P.
535 Friztown Road
Sinking Spring, PA 19608

Prepared by:
Tetra Tech, Inc.
661 Anderson Drive
Pittsburgh, Pennsylvania 15220
(412) 921-7090
Fax (412) 921-4040

December 2, 2016
Revised February 6, 2017

TABLE OF CONTENTS

Section			Page
1.0	PROJECT DESCRIPTION		1
2.0	SURFACE AND GROUNDWATER PROTECTION PLANS		1
3.0	WATER SUPPLY PLAN PURPOSE		1
4.0	EXISTING ENVIRONMENT		2
	4.1	PRIVATE GROUNDWATER WELLS	2
	4.2	PUBLIC WATER SUPPLY WELLS AND INTAKES	2
5.0	RISK ASSESSMENT		3
	5.1	DESCRIPTION OF RISKS	3
		5.1.1 Hazardous Material Spill and Encounters	3
		5.1.2 Conventional Auger Bore and HDD Installation Methods	3
		5.1.3 Hydrostatic Testing	4
	5.2	RISKS TO WATER SUPPLIES	5
		5.2.1 Private Groundwater Wells	5
		5.2.2 Public Water Supply Wells	6
		5.2.3 Public Water Supply Surface Water Intakes	6
6.0	PREVENTION, PREPAREDNESS, AND CONTINGENCIES		7
	6.1	PUBLIC AND PRIVATE OWNER CONSULTATIONS	7
	6.2	HAZARDOUS MATERIAL SPILLS AND ENCOUNTERS	8
	6.3	RELEASES FROM HDDS	10
	6.4	NOTIFICATIONS	11

APPENDICES

A	Water Supplier Consultations
B	Well Test Plan
C	Hydrogeologic Review and Aquifer Summary
D	Master Water Supplier Index

1.0 PROJECT DESCRIPTION

Sunoco Pipeline, L.P. (SPLP) proposes to construct and operate the Pennsylvania Pipeline Project (Project or PPP) that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way (ROW) from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the ROW from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same ROW. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles. For a detailed Project Description see Attachment 9 of the Project's Chapter 105 Joint Application for Permit.

2.0 SURFACE AND GROUNDWATER PROTECTION PLANS

SPLP has developed four plans that accompany the Erosion & Sedimentation Plan (E&S Plan). These plans assess the potential impacts and provide for the protection of surface and groundwater due to unanticipated Project activities. The overarching PPC Plan addresses spill prevention, countermeasures, and response in general. Potential impacts to surface waters and public and private water supplies in particular have been analyzed and addressed within two supplemental plans to the PPC Plan: this Water Supply Assessment, Preparedness, Prevention and Contingency Plan (Water Supply Plan); and a HDD Inadvertent Return Assessment, Preparedness, Prevention and Contingency Plan (IR Plan). This Water Supply Plan provides for the assessment of the existing public and private water supplies in or along the project, as well as identifies prevention and preparedness measures to be implemented to protect those supplies. The IR Plan outlines the preconstruction activities implemented to ensure sound geological features are included in the HDD profile, the measures to prevent impact, and the plan to be implemented if an impact were to occur. In addition, a Void Mitigation Plan for Karst Terrain and Underground Mining (Karst Plan) is provided as part of the E&S Plan and assesses the potential impacts and avoidance and mitigation measures during open-cut and drilling procedures. The purpose of these plans is to protect surface and groundwater resources Project-wide. The PPC Plan is provided as Attachment 12A of the Project's Chapter 105 Joint Application for Permit, this Water Supply Plan is provided as Attachment 12B, the IR Plan is provided as Attachment 12C, and the Karst Plan as Attachment 12D. These four plans also accompany every E&S Plan developed for the Project under the Chapter 102 regulations.

3.0 WATER SUPPLY PLAN PURPOSE

Private and public water supply sources are located along and/or downstream of proposed work areas. This plan describes the methodology used to identify those water supplies (i.e., private groundwater wells, public groundwater wells, and private water supply intakes) in relation to the Project areas and presents a summary of the existing environment in regards to these supplies. Next, this plan provides an evaluation of the risks to the types of supplies and outlines the

prevention, preparedness, and contingencies in regards to the potential impacts to those supplies.

4.0 EXISTING ENVIRONMENT

A variety of sources were used to identify the existing environment in regards to private and public water supplies in the vicinity of the Project areas. The methods of identification and summary of the results are provided in each of the following subsections.

The data acquired included:(1) Public Water Supply (PWS) areas identified by accessing the Pennsylvania Department of Environmental Protection's (PADEP's) eMapPA platform (http://www.depgis.state.pa.us/eMapPA/)to locate both "Groundwater Wells" and "Surface Water Intakes", this included Public Water Systems as well; (2) private water wells identified using the Pennsylvania Department of Conservation and Natural Resources' (DCNRs') Pennsylvania Groundwater Information System (PaGWIS); and (3) water supply data acquired from landowners during the pipeline easement negotiations.

4.1 PRIVATE GROUNDWATER WELLS

Representatives from SPLP spoke with all landowners directly affected by the Project's workspaces in regards to the presence and location of any waters supply wells. Landowner consultations and plat preparation associated with the acquisition process provided the best available data in regards to the presence and location of groundwater wells. SPLP has avoided all direct impacts to all private water wells. In addition to the information gained from the landowners, SPLP utilized the PAGWIS data to identify 22 approximate water well locations within 150 feet of all HDD alignments, including parcels that would be adjacent to, but not directly crossed by, the Project. The distance of 150 feet was used based on Federal Energy Regulatory Commission guidelines for identification of water wells in the vicinity of their authorized Projects. The locations of these wells are kept within the Project files and are not displayed here to protect the rights of the individual owners. Although the PAGWIS data is made available to the public, the accuracy as stated within the metadata is not reliable and what SPLP has or will obtain represents exact well locations.

4.2 PUBLIC WATER SUPPLY WELLS AND INTAKES

Public water suppliers within one mile of wetlands and waterbodies impacted by the Project were obtained from PADEP's eMapPA platform. Public Community Water Systems within 1 mile of the proposed workspaces were identified as well. In each query, both groundwater wells and surface water intakes were identified. The analysis resulted in the identification of 146 PWS as potentially occurring within the 1.0 mile buffer of the Project areas. Project notification letters and maps were sent to all identified PWS authorities and are provided in Attachment A. In these correspondences, SPLP requested the locations of the authority's PWS groundwater well and/or surface intakes as well as an assessment of potential impacts. Many authorities did not provide intake locations, but did inform SPLP that impacts were not anticipated. If a ground water well location was provided, the location was analyzed for potential impacts. When higher risk situations or concerns are raised, SPLP has or will consult with the supplier in regards to well locations, depths, and additional PPC activities.

Contact reports outlining all PWS authority consultations can be found in Appendix A and master list of these suppliers is provide in Appendix D.

5.0 RISK ASSESSMENT

The project involves the installation 306.8 miles of 20-inch pipeline and 255.8 miles of 16-inch pipeline and supporting aboveground block valve (53) and pump station (8) facilities. The pipeline installation will involve open trenching the majority of the mileage to a depth adequate enough to provide a minimum of 4 feet-of-cover to the top of the pipe in all areas except stream crossings where it will be a minimum of 5-feet-of-cover. The project also involves 132 HDDs for the 20-inch pipeline and 105 HDDs for the 16-inch pipeline and 304 auger bores for the 20-inch pipeline and 250 for the 16-inch pipeline.

Private and public water supplies may be impacted by hazardous material spills during any of the project activities including, open trenching, HDD and auger bore installation, and block valve and pump station construction and installation, and hydrostatic testing. Open trenching and grading activities have the potential to encounter karst areas/openings that may lead to groundwater sources. Unanticipated encounters with contaminated soil may also threaten water resources and supplies. Additional risks to private and public water supplies may result from the activities associated with the HDD method of pipeline installation, specifically, the use of drilling fluids during the drill process. Hydrostatic testing may require the use of and discharge to public water supply surface waters.

5.1 DESCRIPTION OF RISKS

5.1.1 HAZARDOUS MATERIAL SPILL AND ENCOUNTERS

The materials anticipated to be stored on site during this pipeline construction include diesel fuel, lubricating oil, bentonite clay, and welding gasses (oxygen and acetylene). Of these materials, the material stored in the largest volume and with the highest potential adverse impact to private / public water supply wells and public water supply surface water intakes is diesel fuel.

Encounters with karst terrain or openings during open trenching or grading activities offer a possible pathway for contaminants to migrate to groundwater resources. However, the threat to groundwater sources is limited to sedimentation from on-site run-off into the opening. A diesel fuel spill in the same location as an encountered karst area would be an unlikely event. SPLP has also developed a karst terrain plan that provides procedures for mitigating encounters with subsurface openings. The plan is provided in Attachment 12D of the Project's Chapter 105 Joint Application for Permit. There is the potential to encounter an unanticipated petroleum-based impacted soil during Project construction. The threat of such an encounter to surface or groundwater would depend on the location and extent of the impacted condition and is covered within the Project's overarching PPC Plan.

5.1.2 CONVENTIONAL AUGER BORE AND HDD INSTALLATION METHODS

Conventional auger boring (CAB) or jack and bore is a dry trenchless method of installing a relatively shallow underground steel pipe, from an excavated entry pit to an excavated exit pit, beneath an avoidance obstacle (such as a road). Specifically, a specialized track machine pushes the product pipe into and through the ground while simultaneously auger boring to remove the spoil from within the pipe. This push and clean-out process is repeated for each pipe segment until the desired

total installation length is achieved. The technique has been utilized extensively in the United States for numerous decades, primarily for road and railroad crossings. A more detailed description of the CAB process is presented in Section SPLPs' *Trenchless Feasibility Analysis* (TFA) included with the Alternatives Analysis provided with the Project's Chapter 105 Joint Application for Permit.

Horizontal directional drilling (HDD) is a steerable trenchless method of installing underground pipe, conduit, or cable in a shallow arc along a prescribed bore path by using a surface-launched drilling rig, with minimal to no impact along the bore path. The easiest forms of HDD emerged in the 1960s and have since been advanced and are typically utilized when conventional trenching techniques are not desirable or practicable. It is suitable for a variety of soil and bedrock conditions and primarily intended for obstacle avoidance including, but not limited to, stream crossings, roads, and protected environmental features systems. A more detailed description of the HDD process is presented in SPLPs *Trenchless Feasibility Analysis* (TFA) included with the Alternatives Analysis provided with the Project's Chapter 105 Joint Application for Permit.

Throughout the HDD process, a pressurized drilling fluid comprised primarily of water and bentonite clay is pumped into and circulates back out of the bore hole. The principal functions of drilling fluid in HDD pipeline installation are listed below.

- Transportation of spoil
- Cooling and cleaning of cutters
- Reduction of friction
- Hole stabilization
- Transmission of hydraulic power
- Hydraulic excavation
- Soil modification

5.1.3 HYDROSTATIC TESTING

Hydrostatic testing involves filling a pipeline segment with water and performing a pressure test. SPLP utilizes hydrostatic tests for a variety of applications, such as strength testing prior to commissioning a newly constructed pipeline, testing pipeline replacement sections before being tied into the main pipeline, as a periodic pipeline reassessment method after a pipeline has been in operation, or to establish a new maximum operating pressure. The hydrostatic tests are used to ensure that the pipeline is suitable for service prior to commissioning. SPLP will be installing new pipe to complete the Project.

A combination of approved surface water sources and public water sources will be used to provide the water required for HDD, hydrostatic testing of pipeline segments installed by HDD, and hydrostatic testing of the main pipeline. The pipeline will be tested hydrostatically in accordance with DOT regulations, 49 C.F.R. Part 192. The pipeline will be filled with water and maintained at a test pressure and duration in compliance with SPLP's engineering standards and applicable federal regulations. After completion of a satisfactory test, the water will be discharged to the ground or a directly to a surface water in accordance with in obtained permits or trucked to an offsite facility. HDD segments will be hydrostatically tested individually after the installation process. Subsequently, once the entire pipeline has been installed within a construction spread, the full pipeline will be hydrostatically tested.

5.2 RISKS TO WATER SUPPLIES

5.2.1 PRIVATE GROUNDWATER WELLS

Private groundwater wells are constructed by one of three types as follows:

- Drilled wells are constructed by either a cable tool (percussion) or rotary-drill machines. Well depths typically range between 50 and 500 feet, while some reach depths over 1,000 feet. Drilled wells are the most common type. Drilled wells typically have 20 to 40 feet of casing set at the surface to protect against shallow sources of contamination but the casings are rarely grouted in place, so the protection in limited.
- Driven wells are constructed by driving a small-diameter pipe into shallow water-bearing sand or gravel. Hand-driven wells usually are only about 30 feet deep, while machine-driven wells can be 50 feet or more.
- Dug wells are of a historical nature and constructed by hand shoveling a shaft down below the water table. The sides are usually lined with stones, bricks, or other material to prevent collapse and the top may be capped when not utilized. Dug wells usually do not exceed 25 feet in depth.

Potential Hazardous Material Spill and Encounter Impacts

Given appropriate material handling practices and limited quantities of the hazardous materials on site at given moment, hazardous materials spills and unanticipated contaminate soil encounters occurring in Project areas pose a minimal threat to private groundwater wells.

Potential CAB Impacts

CAB is a relatively shallow construction process that must occur in a dry environment. CAB areas with a high groundwater table are dewatered by various methods to temporarily dry the area to facilitate construction. Given the depth (not more than 20 feet) of CAB and adjacency with only the high groundwater table, threats to significantly deeper groundwater tables used for private wells are considered to be minimal.

Potential HDD Impacts

HDD for pipelines usually occur at depths less than 100 feet, which could include the crossing of shallow aquifers. The primary potential impact to groundwater is the migration of drilling fluid away from the HDD drill path. Specifically, drilling fluid expended downhole will flow in the path of least resistance. While the path of least resistance is typically the bore hole itself, it may instead be an existing fracture, fissure, or formation opening in the soil or rock substrate. When this happens, circulation can be lost or reduced and drilling fluid could enter the groundwater table that could be used by private groundwater wells.

Hydrostatic Testing

SPLP will use new pipe in the installation of the pipelines and therefore contamination of the water used for hydrostatic testing is not expected. Therefore, discharge of the water whether it be to upland areas or direct discharge to a surface water would not introduce contaminates into public or private groundwater or surface water supplies. To ensure the water being discharged is free of contaminates, a PAG-10 permit is obtained for all hydrostatic test locations and requires pre-test and discharge testing of the water.

5.2.2 PUBLIC WATER SUPPLY WELLS

Public water supply wells are typically drilled wells constructed by either a cable tool (percussion) or rotary-drill machines. Well depths are similar to private wells. Drilled wells typically have 40 feet or more of grouted casing set at the surface which effectively protects against shallow sources of contamination.

Potential Hazardous Material Spill and Encounter Impacts

Given appropriate material handling practices, casing requirements for public water supply wells and limited quantities of the hazardous materials on site at given moment, hazardous materials spills and unanticipated contaminate soil encounters occurring in Project areas pose a minimal threat to public water supply wells.

Potential CAB Impacts

As described in Section 5.2.1 above, CAB construction process is not expected to affect these deep public water supply wells.

Potential HDD Impacts

As stated earlier drilled wells typically have 40 feet or more of grouted casing set at the surface which effectively protects against shallow sources of contamination. HDD for pipelines usually occur at depths greater than 40 feet, which could include the crossing of shallow aquifers. The primary potential impact to groundwater is the migration of drilling fluid away from the HDD drill path. Specifically, drilling fluid expended downhole will flow in the path of least resistance. While the path of least resistance is typically the bore hole itself, it may instead be an existing fracture, fissure, or formation opening in the soil or rock substrate. When this happens, circulation can be lost or reduced and drilling fluid could enter the groundwater table that could be used by private groundwater wells.

Hydrostatic Testing

As noted in Section 5.2.1, SPLP will use new pipe in the installation of the pipelines and therefore contamination of the water used for hydrostatic testing is not expected. To ensure the water being discharged is free of contaminates, a PAG-10 permit is obtained for all hydrostatic test locations and requires pre-test and discharge testing of the water.

5.2.3 PUBLIC WATER SUPPLY SURFACE WATER INTAKES

Potential Hazardous Material Spill and Encounter Impacts

Hazardous material spills and encounters with unanticipated contaminated soil has a potential to impact surface waters that may be upstream and in or along a surface water with a public water supply intake. Work with diesel run equipment is often carried out adjacent to, and within wetlands, waterways, and floodways. A spill could result in a direct and immediate impact.

Potential CAB Impacts

Because the CAB construction process is conducted in a dry environment, no interaction with surface waters is anticipated. The risk to surface water intakes is considerably low.

Potential HDD Impacts

HDD fluid follows the path of least resistance and may leave the bore hole through a variety of geologic features. The environment may be impacted if the fluid

inadvertently returns to the surface at a location on a waterway's banks or within a waterway or wetland. If the fluid cannot be adequately contained, it can mix with surface water, dramatically increasing turbidity, and flow downstream. If this turbid flow reaches a surface water intake, then the public water supply could be adversely affected.

Hydrostatic Testing

As noted in Section 5.2.1, SPLP will use new pipe in the installation of the pipelines and therefore contamination of the water used for hydrostatic testing is not expected. To ensure the water being discharged is free of contaminates, a PAG-10 permit is obtained for all hydrostatic test locations and requires pre-test and discharge testing of the water.

6.0 PREVENTION, PREPAREDNESS, AND CONTINGENCIES

Identification and description of the existing environment (see Section 4.0) in regards to public and private water supplies and the risks and threats (see Section 5.0) to these supplies in regards to Project actions, allowed SPLP to develop prevention, preparedness, and contingencies as outlined within the following subsections.

6.1 PUBLIC AND PRIVATE OWNER CONSULTATIONS

Attachment A provides the status of SPLP's efforts to consult with PWS authorities within the vicinity of the Project. The majority of the PWS authorities identified have responded with no issue or concern and/or provided the requested location. Several have not responded, and those that did not respond were contacted by telephone to ensure receipt and consideration of the correspondence. Some PWS authorities requested additional information, which SPLP has provided. Some consultations with PWS authorities are on-going and will be resolved to ensure that public water supplies are not put at risk from the Project. Identification of the PWS intakes and concerns raised by the authorities has allowed SPLP to better prevent and prepare contingencies for potential impacts to these resources.

When location data is made available by the public water supplier as a result of consultation efforts, SPLP will identify those wells within 150 feet of HDD alignments. For these wells, the drill path will be compared to the well depth and geology of the area. Those wells in geologies with potentially significant interconnected secondary porosity (solution openings and structural features) will be considered for monitoring during HDD installs depending on specific individual water supplier requirements. All public water suppliers with known wells within 150 feet of HDDs, will be notified at least 72 hours prior to initiation of the drilling phase of the HDD construction activity.

Once the project is fully permitted and construction begins, SPLP will field verify the location of all private drinking water wells within 150 feet of HDDs previously identified through PaGWIS data and landowner consultation. With landowner approval, and if well conditions permit, SPLP will test the wells for water quality and quantity before, during, and after the drill operation in accordance with SPLP's water supply testing plan (Appendix B). Also if any landowner outside of the HDD areas requested pre- and post-construction testing of the wells, that testing will also occur in accordance with SPLP's water supply testing plan. To-date 120 landowners have requested such testing. All identified private wells within 150 feet of HDDs, will be notified at least 72 hours prior to initiation of the drilling phase of the HDD construction activity.

PADEP will be notified within 24 hours of receipt of any water supply complaints. This data will be utilized as a baseline for comparison to post-inadvertent return and/or post-construction sampling results to evaluate potential impacts and mitigation measures, if necessary.

6.2 HAZARDOUS MATERIAL SPILLS AND ENCOUNTERS

Emergency response protocol for material spills is the same as the protocol documented in SPLP's PPC Plan. The PPC Plan provides the following:

- List of emergency response coordinators
- Duties and responsibilities of the emergency response coordinator
- Chain of command
- Countermeasures to be undertaken by facility
- Countermeasures to be taken by contractors
- Internal and external communications and alarm systems
- Evacuation plan for installation personnel
- Emergency equipment available for response

To ensure site personnel are adequately prepared so they can respond effectively to an emergency, a material spill training program has been generated. SPLP's PPC Plan provides documentation of this program. To mitigate the risk of fuel spillage, all fuel shall be stored in code compliant double-contained vessels. In addition, all fuels will be stored in accordance with the setbacks from aquatic resources as identified within the Project's E&S Plan. To comply with the regulatory requirements set forth in 25 Pa. Code Section 78, SPLP has developed a PPC Plan for effective action to minimize and abate hazards to human health and the environment from fire, explosion, emission or discharge of pollutants to air, soil, surface water, or groundwater. Although hazardous materials (other than diesel fuel) are not planned for use on the Project, SPLP's PPC Plan describes the actions that SPLP or contractor personnel will take regarding hazardous materials if encountered.

Specific Spill Clean Up Procedures:

In the event of a release of hazardous materials during construction activities or if impacted soils identified by visual or olfactory methods are encountered during construction, the following procedures will be followed:

1. Work is stopped immediately in the area if an apparent worker safety concern is identified.
2. Upon discovery, SPLP's Environmental Compliance Coordinator (ECC) will be contacted.
3. If the ECC determines that impacted soils may be present, the ECC representative will notify an SPLP approved Rapid Response contractor. Additionally, if the ECC determines that current conditions cause or threaten pollution to surface or groundwater, then the ECC will immediately notify PADEP of the condition in accordance with 25 Pa. Code §91.33.
4. The Rapid Response contractor dispatches the appropriate personnel and equipment to further assess the site.
5. Rapid Response personnel examine the soil and screen it with a photoionization detector to determine the presence/absence of volatile and semi-volatile organic compounds.

6. If the Rapid Response personnel determine there are no impacted soils in the area, then the soil is considered cleared and can be used as backfill.
7. Upon positive identification of impacted soils, Rapid Response personnel will document site conditions, the estimated extent of the condition, and any potential threats to health, safety, and the environment. If at this or any other point of the response process, the ECC in consultation with the Rapid Response personnel concludes that there is a threat of or actual pollution to surface water or groundwater, and PADEP has not been previously notified of the incident, then the ECC will immediately notify PADEP of the condition in accordance with 25 Pa. Code §91.33.
8. Rapid Response personnel will then excavate and segregate any impacted soils, placing an impervious cover over and under the impacted soils.
9. After the impacted soils have been excavated and segregated, Rapid Response personnel collect representative samples of the impacted soils and analyze the soil samples for organics in accordance with PADEP's Management of Fill Policy.
10. If the results of the sampling do not exceed the numeric standards in Table GP-1a of the General Permit for Beneficial Use of Regulated Fill, then the soils may be reused in the area as backfill. If the results of the sampling exceed the numeric standards in Table GP-1a of the General Permit for Beneficial Use of Regulated Fill, then the impacted soils shall be disposed at a properly permitted offsite disposal facility.
11. Construction may continue unless the ECC, in consultation with the Rapid Response personnel, determines that proceeding with construction poses a threat to health, safety, or the environment.

Petroleum and Petroleum Related Materials: In dealing with a petroleum spill, the immediate response action is to attempt to eliminate the source of the spill as soon as possible. In the event of an accidental spill, emergency measures will be implemented by SPLP to isolate the spilled material and prevent the release from entering surface water or groundwater. Berms may be constructed to contain the spill, and/or excavation equipment may be used to promptly remove impacted soils, concrete, or asphalt. Stormwater collection structures will be either blocked or pumped, if appropriate, to prevent the release to surface water.

Soil that is impacted as a result of an accidental spill or release will be containerized for subsequent disposal. The typical clean up procedure for the spilled oil is as follows:

- Remove sources of ignition (ignition sources are not to be within 50' of any storage tanks)
- Contain the spill using whatever equipment and material are available. Petroleum captured within secondary containment should be recycled to the extent possible. In water, booms should be used to limit the spread of oil along the surface. On land, absorbent materials such as Oil Dri, straw, sawdust, or soil should be used to soak up any free or flowing oil and limit its spread. The most important thing is to act quickly to limit the extent of the spill.
- Remove the petroleum soaked materials using the most effective means, whether it is by hand using shovels or heavy earth moving equipment. Caution must be exercised in using construction equipment in and around streams to minimize the disturbance to the watercourse. It may be

necessary to provide clean fill to reconstruct the affected areas after removal of the petroleum contaminated soils.

6.3 RELEASES FROM HDDS

A separate IR PPC Plan has been created for the Project and is supplemental to this PPC. Like this plan, the IR Plan is to be included with all permitting documents provided to the contractor (see Attachment 12C of the Chapter 105 Joint Application for Permit). The IR Plan addresses 25 Pa. Code §78a.68a: Horizontal Directional drilling for oil and gas pipelines. The immediate response actions in dealing with an inadvertent return of drilling fluids (primarily bentonite and water) from a horizontal direction drill include discontinuing drilling operations, identifying the area of the inadvertent return, and isolating the inadvertent return.

As identified in Section 5.3 the risks to water supplies associated with use of the CAB installation method are considerably low. However, HDD methods do present some risk. To ensure the highest probability of success on the proposed HDD installations, SPLP has assembled a technical team which includes engineers and consultants having expertise in HDD design, construction, and environmental issues. Groundwater & Environmental Services, Inc. (GES) reviewed certain information described in Appendix C to identify potential Inadvertent Return (IR) problem areas. GES assembled information related to certain parameters associated with aquifers to assess the relative risk of IRs at HDDs. Of the 17 counties that the proposed PPP crosses, GES reviewed HDD profiles and supplemental information for nine of the counties where geologies representative of all HDD crossings were evaluated. SPLP's IR Plan provides documentation of the methodologies the team employs to eliminate / minimize inadvertent releases of drilling fluids. These protocols include:

- Design criteria and geotechnical sampling
- Site feasibility analysis and inadvertent release risk assessments
- Drinking water source protection protocols

The most effective way to minimize environmental impact associated with HDD installations, and specifically with drilling fluids, is to maintain drilling fluid circulation to the extent practicable. To help facilitate this goal, SPLP's IR Plan provides documentation of the planned HDD implementation procedures and inadvertent returns preparedness measures. These protocols include:

- Drilling fluid control
- Environmental / geologic inspection
- HDD alignment monitoring and inadvertent return protocols

In the event an inadvertent release or return occurs, the fast and appropriate response by all Project parties is essential to minimize adverse impacts. These actions will depend on the location and time of release or return, site specific geologic conditions, and the volume of the release or return.

In the event an inadvertent release occurs to surface waters that could potentially affect a downstream water supply intake point, an SPLP representative will notify the owner / manager of the water supply to provide ample warning so that intake can be temporarily discontinued until the turbidity plume passes.

Should an inadvertent return adversely affect a groundwater or surface water supply source, the following actions shall occur:

- Clean drinking water shall be supplied to affected users until the situation is resolved.
- Water quality and quantity re-sampling shall be conducted to determine the extent of impact and help determine remedial actions, if any.

SPLP's IR Plan provides the details of planned response to inadvertent returns. These protocols address:

- Inadvertent returns in uplands
- Inadvertent returns in wetland(s) / stream(s)
- Containment and clean-up materials and equipment
- Notifications

6.4 NOTIFICATIONS

All identified public water suppliers with known wells within 150 feet of HDDs, will be notified at least 72 hours prior to initiation of the drilling phase of the HDD construction activity.

All identified private wells within 150 feet of HDDs, will be notified at least 72 hours prior to initiation of the drilling phase of the HDD construction activity.

PADEP will be notified at least 24 hours prior to initiation of the drilling phase of the HDD construction activity. This notification will be made through PADEP's online Oil and Gas Reporting Electronic (OGRE) application. The OGRE application is accessed via the DEP Greenport login in system at https://www.depgreenport.state.pa.us .

PADEP will be notified within 2 hours of receipt of any water supply complaints. This notification will be made through PADEP's online Oil and Gas Reporting Electronic (OGRE) application. The OGRE application is accessed via the DEP Greenport login in system at https://www.depgreenport.state.pa.us .

The Project's IR Plan contains additional notifications regarding inadvertent returns.

The Pennsylvania Clean Streams Law regulations require that when any pollutant discharged into surface or groundwater, including sewers, drains and ditches, the person spilling the substance or the person owning the premises from which the substance is spilled must notify PADEP immediately. The following notifications will be made to PADEP immediately following an occurrence:

- PADEP Southwest Regional Office: 412-442-4000
- PADEP Southcentral Regional Office: 866-825-0208
- PADEP Southeast Regional Office: 484-250-5900
- PA Fish and Boat Commission Bureau of Law Enforcement: 717-705-7861
  SWRO: 814-445-8974, SCRO: 717-486-7087, SERO: 717-626-0228
- Other agencies that will be notified:
  - U.S. Army Corps of Engineers
    Pittsburgh District: 412-395-7155
    Baltimore District: 410-962-3670

Philadelphia District: 215-656-6728

- Local agencies and municipalities who are downstream users of water, as applicable (see Water Supply Plan supplied with the Project's E&S Plan)

Appendix A
Water Supplier Consultations

List of Contacted Public Supply Sources

PWS ID	PWS Name	Date Sent	Response	Phone
PA4070008	ALTOONA CITY AUTH. WATER DEPT.	9/20/2016	In consultation	814-949-2222
PA1460073	AQUA PA MAIN DIVISION	9/20/2016	In consultation	610-645-1082
PA1150035	AQUA PA UWCHLAN	9/20/2016	No response	610-645-1164
PA4070054	AUTUMN EST	9/20/2016	No response	814-695-0536
PA4070011	BLAIR TWP WATER & SEWER AUTH	9/20/2016	Responded – No Issue	814-695-6300
PA5320006	BLAIRSVILLE MUNI AUTH	9/20/2016	No response	724-459-9100
PA3060052	CAERNARVON TWP AUTH	9/20/2016	No response	610-286-1017
NA	CAMP HILL STATE CORRECTIONAL INST	9/20/2016	Responded – No Issue	
PA1230004	CHESTER WATER AUTHORITY	9/20/2016	Responded – No Issue	610-876-8185
PA7380007	CORNWALL BORO MUNI AUTH	9/20/2016	Responded – No Issue	717-274-5441
PA7210065	COUNTRY VIEW EST	9/21/2016	Responded – No Issue	717-776-7109
PA7210001	CREEK VIEW MOBILE HOME COMMUN	9/20/2016	No response	717-245-2100
PA4110030	CRESSON BORO WATER SYS	9/20/2016	No response	814-886-2139
PA4110038	CRESSON TWP MUNI AUTH	9/20/2016	No response	814-886-2793
PA4110299	CROYLE TWP WATER AUTH	9/21/2016	No response	814-495-9009
PA1150037	DEVEREUX FOUNDATION BRANDYWINE	9/20/2016	No response	610-942-5900
PA4070012	DUNCANSVILLE MUNI WATER AUTH	9/20/2016	No response	814-695-1497
PA4110009	EBENSBURG BORO MUNI AUTH	9/20/2016	Responded – No Issue	814-472-8780
PA1150191	ELVERSON WATER COMPANY	9/20/2016	Responded – No Issue	610-286-5115
PA4070034	FREEDOM TWP WATER & SEWER	9/20/2016	Responded – No Issue	814-695-8051
PA4070013	GREENDOWN ACRES MHP	9/20/2016	No response	814-695-1464
PA4110014*	GREATER JOHNSTOWN WATER AUTH-SALTLICK	2/4/2017	No response	814-533-4300
PA7210003	HARMONY ESTATES MHP	9/20/2016	No response	717-730-4141

PWS ID	PWS Name	Date Sent	Response	Phone
PA7380033	HEIDELBERG TWP MUNI AUTH	9/21/2016	Responded – No Issue	717-949-6977
PA4110017	HIGHLAND S & W AUTH BEAVERDAM	9/20/2016	Responded – No Issue	814-266-3146
PA4110015	HIGHLAND S & W AUTH LLOYDELL	9/20/2016	Responded – No Issue	814-266-3146
PA4110016	HIGHLAND S&W AUTH NORTHERN END	9/20/2016	Responded – No Issue	814-266-3146
PA5650069	HIGHRIDGE WATER AUTH	9/20/2016	Responded – No Issue	888-557-4343
PA7210022	HILLSIDE MHP	9/20/2016	No response	717-576-3155
PA4070017	HOLLIDAYSBURG MUNI AUTH	9/20/2016	Responded – No Issue	814-695-7543
PA4110021	JACKSON TWP WATER AUTH	9/20/2016	Responded – No Issue	814-322-1262
PA7380010	LEBANON WATER AUTH	9/20/2016	Responded – No Issue	717-865-2191
PA5650012	LITTLE ACRES MHP	9/20/2016	No response	724-863-1388
PA1150030	LOAGS CORNER MOBILE HOME PARK	9/21/2016	No response	610-286-5183
PA7670024	MEADOWBROOK MHP	9/20/2016	No response	717-774-8887
PA7210063	MIDDLESEX TWP MUNI AUTH	9/20/2016	No response	717-243-0674
PA7220038	MIDDLETOWN BORO WATER AUTH	9/20/2016	No response	717-948-3055
PA5020025*	MUN AUTH OF WESTMORELAND COUNTY – MCKEESPORT	2/4/2017	No response	412-678-6065
PA7210049	N MIDDLETON WATER AUTH	9/20/2016	No response	717-243-8269
PA7220017	PA AMER WATER CO	9/20/2016	No response	717-533-5627
PA5020039	PA AMER WATER CO-PITTSBURGH	9/20/2016	No response	724-437-0102
PA7210029	PA AMERICAN WATER CO WEST	9/20/2016	No response	717-774-7460
PA5320025	PA AMERICAN WATER CO-INDIANA D	9/20/2016	No response	724-465-6600
PA1230886	PATHWAYS	9/20/2016	No response	610-459-9177
PA5650026	PINE GARDEN APARTMENTS	9/20/2016	No response	724-875-0882
PA7380031	QUENTIN WATER CO	9/20/2016	No response	717-274-5514
PA3060067	SHILLINGTON MUNI AUTH	9/20/2016	No response	610-777-1338
PA7220036	STEELTON BORO WATER AUTH	9/20/2016	No response	717-939-0425

PWS ID	PWS Name	Date Sent	Response	Phone
PA7220015	SUEZ WATER	9/20/2016	No response	717-561-1103
PA7210028	UNITED WATER PA MECHANICSBURG	9/20/2016	No response	717-561-1103
PA3060076	WERNERSVILLE MUNI WATER AUTH	9/20/2016	Responded – No Issue	610-678-4711
PA7360141	WEST COCALICO TWP WATER AUTH	9/20/2016	Responded – No Issue	717-336-8720
PA5650034	WESTMORELAND MA-TRUXALL SYS	9/20/2016	No response	724-727-2300
PA3060127	ABRAXAS ACADEMY	1/18/2017	No response	(610)913-8000
PA7220935	ADVENTURE SPORTS IN HERSHEY	1/18/2017	In consultation	717-533-7479
PA3061101	ALLEGHENY EVAN LUTH CH	1/18/2017	No response	(610)777-2520
PA3061055	AMER HOUSE OF FRITZTOWN	1/18/2017	No response	(610)678-0609
PA3060403	AMERICAN LEGION POST 537	1/18/2017	No response	(610)286-5920
PA7220949	ANALYTICAL LABORATORY SVCS	1/18/2017	In consultation	717-944-5541
PA7671020	ASSN OF BAPTIST FOR WORLD EVNG	1/18/2017	No response	(717)774-4400
PA4070313	AVIATION INN	1/18/2017	No response	(814)932-0595
PA3061231	BASIL PIZZERIA	1/18/2017	No response	(484)509-2066
PA3061194	BC MONTESSORI COUNTRY DAY SCH	1/18/2017	No response	(610)777-3080
PA3061154	BIG BERTHAS GRILL	1/18/2017	No response	(610)670-4540
PA4310850	BRANCH CPGRD	1/18/2017	No response	814-643-0485
PA3061100	BRECKNOCK ACADEMY	1/18/2017	No response	(610)777-2980
PA3060846	BRECKNOCK TWP FIRE COMPANY	1/18/2017	No response	(610)777-9575
PA5650902	BUSH RECREATION AREA	1/18/2017	No response	(729)639-9013
PA3060417	CAMP ADAHI & ADAHI KIDS	1/18/2017	No response	(610)856-7250
PA5630431	CANONSBURG SPORTSMEN ASSOCIATN	1/18/2017	No response	(724)745-0527
PA1150310	CAR SENSE UWCHLAND	1/18/2017	No response	(610)458-3700
PA7210982	CARLISLE YS MENS CLUB	1/18/2017	No response	717-243-1892
PA3061213	CATERING BY JOHN LOWE	1/18/2017	No response	(610)873-7229
PA7360836	COCALICO CREEK CPGRD	1/18/2017	In consultation	717-336-2014
PA3060633	COMMUNITY FIRE CO OF FRITZTOWN	1/18/2017	No response	(610)678-0502
PA7671148	CULHANES STEAK HOUSE	1/18/2017	No response	(717)938-0930
PA3061150	CUSHION PEAK ROD & GUN CLUB	1/18/2017	Responded – No Issue	(610)670-9558

PWS ID	PWS Name	Date Sent	Response	Phone
PA7210832	DOGWOOD ACRES REC AREA	1/18/2017	In consultation	717-776-5203
PA7210321	ECONOLODGE	1/18/2017	No response	717-766-4728
PA7671289	FAIRVIEW ELEM SCH	1/18/2017	No response	(717)938-9577
PA7381039	FAIRVIEW GC	1/18/2017	No response	(717)273-3411
PA7670980	FAIRVIEW TWP BLDG	1/18/2017	No response	(717)901-5261
PA7500808	FOWLERS HOLLOW ST PARK	1/18/2017	No response	717-776-5272
PA3060638	GALEN HALL CC INC	1/18/2017	No response	(610)678-8011
PA4070346	GEESEYTOWN VOL FIRE CO	1/18/2017	No response	(814)695-8003
PA3060438	GOUGLERSVILLE FIRE CO	1/18/2017	No response	(610)777-2449
PA3060347	GOV MIFFLIN BRECKNOCK ELEM SCH	1/18/2017	No response	(610)775-5079
PA7361081	GRACE BRETHREN RETREAT CENTER	1/18/2017	No response	717-336-2541
PA1230820	GRADYVILLE FOODS COUNTRY DELI	1/18/2017	No response	(610)558-3354
PA7670890	GUY SHELLY AMER LEGION 974	1/18/2017	No response	(717)774-3149
PA4310841	HAPPY TRAILS CAMPGROUND	1/18/2017	No response	(814)458-3101
PA7220044	HARRISBURG INTL AIRPORT	1/18/2017	No response	717-948-3900
PA7220964	HISTORIC ACRES OF HERSHEY	1/18/2017	No response	570-298-6340
PA5630338	HOUSTON SUNOCO	1/18/2017	No response	(724)745-1214
PA3060640	HUIES GRAY FOX INN	1/18/2017	No response	717-484-2625
PA3061243	JOANNA FURNACE	1/18/2017	No response	(610)286-0388
PA3061019	JOANNA STORE	1/18/2017	No response	(610)286-5197
PA3060989	KEN GRILL RECREATION ASSN	1/18/2017	No response	(610)777-9322
PA4110837	KEYSTONE RESTAURANT	1/18/2017	No response	(814)886-4533
PA7360835	KINGDOM HALL MOUNT JOY	1/18/2017	Responded – No Issue	(717)653-8501
PA3060401	LA CANTINA ITALIAN RESTAURANT	1/18/2017	No response	(610)777-5646
PA1230852	LA PORTA RISTORANTE	1/18/2017	No response	(610)358-5104
PA7210943	LANE ENTERPRISES	1/18/2017	No response	717-249-8342
PA7381059	LEBANON VAL BIBLE CHURCH	1/18/2017	No response	(717)867-4403
PA4110046	LILLY MUNI WATER WORKS	1/18/2017	No response	(814)886-7227
PA7220400	MANGIA MANGIA	1/18/2017	No response	570-689-3794
PA3060515	MANOR GC	1/18/2017	No response	(610)678-9597

PWS ID	PWS Name	Date Sent	Response	Phone
PA3060439	MAPLE GROVE PARK	1/18/2017	No response	(610)856-7200
PA1150818	MARSH CREEK STATE PARK	1/18/2017	No response	(610)458-5180
PA7360325	MIDDLECREEK WILDLIFE MGMT AREA	1/18/2017	No response	(717)733-1512
PA3060881	MOHNTON FISH & GAME ASSN	1/18/2017	No response	(610)775-3470
PA3060803	MORGANTOWN PROP	1/18/2017	No response	(610)913-7516
PA3061184	MOUNTAIN VIEW APARTMENTS	1/18/2017	Responded – No Issue	717-484-0973
PA3060821	NOLDE ENVIRONMENTAL ED CTR	1/18/2017	No response	(610)796-3699
PA7360382	NORTH LANC CO GAME & FISH ASSN	1/18/2017	No response	717-336-7280
PA3060069	PAW PENN DISTRICT	1/18/2017	No response	(610)404-1540
PA1150616	PETER J. CAMIEL SERVICE PLAZA	1/18/2017	No response	(610)286-0255
PA7670870	PHAT ALBERTS	1/18/2017	No response	(717)938-4790
PA5320838	PINE RIDGE COUNTY PARK	1/18/2017	No response	724-463-8636
PA7380426	PLAINS LPG SERVICES LP	1/18/2017	No response	(717)949-3469
PA4310800	RAYSTOWN LAKE ARMY CORPS ENG	1/18/2017	No response	(814)658-3405
PA4310855	RAYSTOWN LAKE CORP 7 PTS PLANT	1/18/2017	No response	(814)658-3405
PA7220420	RUTTERS FARM STORE #20	1/18/2017	No response	717-771-5970
PA4310856	SEVEN POINTS BAIT & GROCERY	1/18/2017	No response	(814)658-3718
PA3061175	SGL CARBON GROUP LLC	1/18/2017	No response	(610)670-4095
PA3061099	SINKING SPRING FAMILY YMCA	1/18/2017	No response	(610)678-0484
PA3060625	SLEEPY HOLLOW ATHLETIC CLUB	1/18/2017	No response	(610)856-7516
PA3060969	SLEEPY HOLLOW POOL	1/18/2017	No response	(610)856-1418
PA4310867	SMITTY S EATS N TREATS	1/18/2017	No response	(814)644-3791
PA3060432	SOUTH MOUNTAIN YMCA	1/18/2017	No response	(610)670-2267
PA7670937	SPEEDWAY 6760	1/18/2017	No response	(717)938-1428
PA3060922	ST BENEDICT CH	1/18/2017	No response	(610)856-1006
PA3061130	STEELCO	1/18/2017	No response	(610)678-6411
PA3061205	STEELCO WELL #2	1/18/2017	No response	(610)678-6411
PA7220916	STEVE HEINS GROCERY STORE	1/18/2017	No response	717-533-5222
PA3061018	SUNOCO FOOD SHOP	1/18/2017	No response	(610)678-3550
PA1230939	SWEETWATER FARM B AND B	1/18/2017	No response	(610)459-4711

PWS ID	PWS Name	Date Sent	Response	Phone
PA5650498	THE PINES	1/18/2017	No response	(724)468-9923
PA7381005	THOUSAND TRAILS	1/18/2017	No response	(717)867-5515
PA7210918	TRADING POST MARKET	1/18/2017	No response	717-776-3082
PA3060943	TURKEY HILL MINI MKT 115	1/18/2017	Responded – No Issue	(717)299-8908
PA3060362	TWIN VALLEY FIELD HOUSE	1/18/2017	No response	(610)286-8652
PA3061021	TWIN VALLEY MIDDLE SCHOOL	1/18/2017	No response	(610)286-8679
PA3060360	TWIN VALLEY SENIOR HIGH SCHOOL	1/18/2017	No response	(610)286-8679
PA4070391	VFW POST NO 8724	1/18/2017	In consultation	(814)695-9703
PA3060658	VINEMONT COMM LUTH CH	1/18/2017	No response	(610)670-1141
PA7500369	WILDWOOD FAMILY CG	1/18/2017	Responded – No Issue	717-734-3656
PA4110340	WOODLAND PARK CAMPGROUND	1/18/2017	No response	(814)472-9857

*PWS is located greater than 1 mile from Project impacted aquatic resource, however PADEP guidance requested this PWS be included.

TETRA TECH

Contact Report

To:	Abraxas Academy	Telephone: 610-913-8000
Contact name:	Daniel Stringfellow	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Daniel Stringfellow at Abraxas Academy on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 23, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7767

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

MORGANTOWN, PA 19543

OFFICIAL USE

Certified Mail Fee	$3.30
$	$0.00
Extra Services & Fees *(check box, add fee as appropriate)*	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
$	
Total Postage and Fees	$4.87
$	

ELLICOTT STATION 0205 21

Postmark Here

01/19/2017

Sent To ABRAXAS ACADEMY
Street and c/o DANIEL STRINGFELLOW
City, State, P.O. BOX 645
MORGANTOWN, PA 19543

PS Form 38 ...ons

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237767

On Time
Updated Delivery Day: Monday, January 23, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 23, 2017 , 10:57 am	**Delivered**	**MORGANTOWN, PA 19543**
Your item was delivered at 10:57 am on January 23, 2017 in MORGANTOWN, PA 19543.		
January 23, 2017 , 8:25 am	Available for Pickup	MORGANTOWN, PA 19543
January 23, 2017 , 8:06 am	Arrived at Unit	MORGANTOWN, PA 19543
January 22, 2017 , 9:20 pm	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:54 am	In Transit to Destination	
January 21, 2017 , 8:54 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

HELPFUL LINKS
Contact Us
Site Index
FAQs

ON ABOUT.USPS.COM
About USPS Home
Newsroom
USPS Service Updates
Forms & Publications
Government Services
Careers

OTHER USPS SITES
Business Customer Gateway
Postal Inspectors
Inspector General
Postal Explorer
National Postal Museum
Resources for Developers

LEGAL INFORMATION
Privacy Policy
Terms of Use
FOIA
No FEAR Act EEO Data

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

January 18th, 2017

ABRAXAS ACADEMY
c/o Daniel Stringfellow, Director
P.O. Box 645
Morgantown, PA 19543

Reference: Sunoco Pipeline L.P. – Pennsylvania Pipeline Project
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Adventure Sports in Hershey	Telephone: 717-533-7479
Contact name:	Janet Hill	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Janet Hill at Adventure Sports in Hershey on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Greg Hill (ghill@keystonecustomhome.com) (with cc to Dale Archenbach – daa@cplx.net) emailed Josh Baird on January 25, 2017 identifying concern with the Project's proximity to their on-site well source and has the potential to require an immediate shutdown of their business. They are requiring documentation assessment of the risk exposure to their public water supply by SPLP, including potential of leakage and the geotechnical study of the impact on the water supply. They request definition of " will be co-located in or adjacent to existing utility corridors " mean specifically as it relates to their facility. They would like to know if they now need to test their PWS for potential Natural gas liquid contamination.

They requested information by February 15, 2017 or they will deem the project is not in good standing as it relates to their PWS.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:29 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206125040 Delivered

Your package has been delivered

Tracking # 778206125040

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:28 am

c/o Janet Hill
Adventure Sports In Hershey
2905 Church Road
ELIZABETHTOWN, PA 17022
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206125040
Status:	Delivered: 01/19/2017 09:28 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	ELIZABETHTOWN, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:29 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ADVENTURE SPORTS IN HERSHEY
c/o Janet Hill
2905 Church Road
Elizabethtown, PA 17022

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Allegheny Evan Luth Church	Telephone: 610-777-2520
Contact name:	Property Committee Chairman	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to the Property Committee Chairman at Allegheny Evan Luth Church on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:06 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204430240 Delivered

Your package has been delivered

Tracking # 778204430240

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:03 am

c/o Property Committee Chairman
Allegheny Evan Luth Ch
1324 Alleghenyville Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204430240
Status:	Delivered: 01/19/2017 10:03 AM Signed for By: T.ORMSBEE
Reference:	112IC05958, 16
Signed for by:	T.ORMSBEE
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1

Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:05 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ALLEGHENY EVAN LUTH CH
c/o Property Committee Chairman
1327 Alleghenyville Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Altoona City Auth. Water Dept.	Telephone: 814-949-2222
Contact name:	William Cochran	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to William Cochran at the Altoona City Auth. Water Dept. on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016. Phone conversation with Mike Sinisi of Altoona Water Authority on 10/28/2016, he requested shapefiles of the pipeline in the vicinity of the authority's watershed – shapefile sent on 10/28/2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Thursday, September 22, 2016 2:57 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275189468 Delivered

Your package has been delivered

Tracking # 777275189468

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 9/22/2016 2:52 pm

William Cochran
Altoona City Auth. Water Dept.
20 Greenwood Road
ALTOONA, PA 16602
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275189468
Status:	Delivered: 09/22/2016 2:52 PM Signed for By: D.BECK
Reference:	112IC05958, 16
Signed for by:	D.BECK
Delivery location:	ALTOONA, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:57 PM CDT on 09/22/2016.


All weights are estimated.


To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

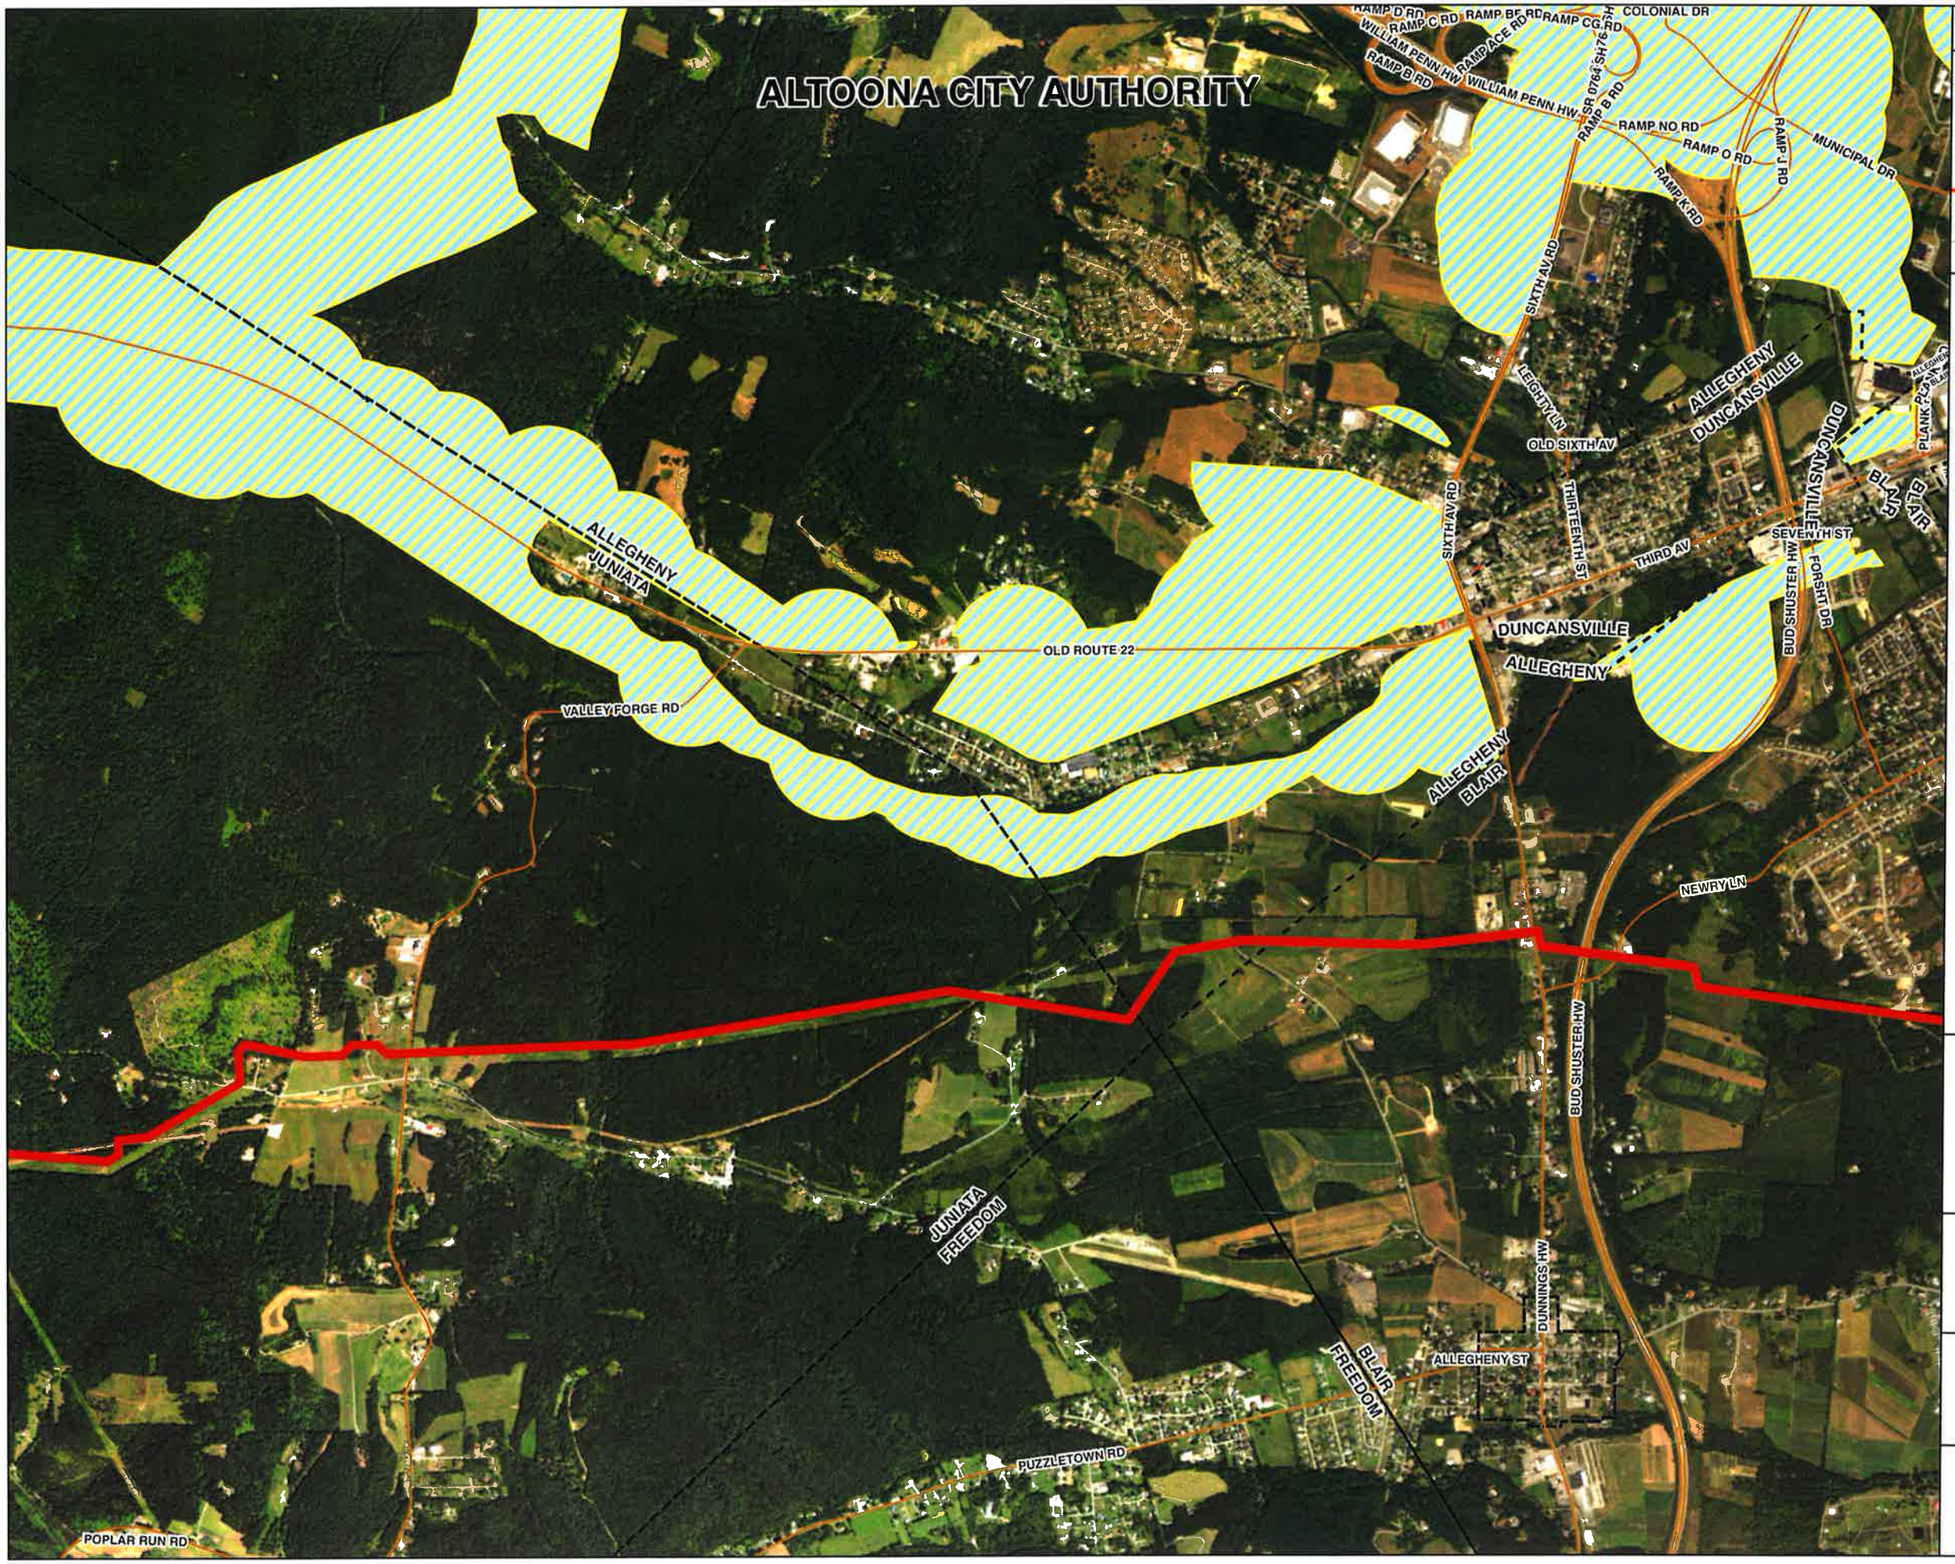



Legend

- Proposed Pipeline
- PA State Roads
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Amer House of Fritztown	Telephone: 610-678-0609
Contact name:	Craig J Lutz	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Craig J Lutz at Amer House of Fritztown on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:31 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204494035 Delivered

Your package has been delivered

Tracking # 778204494035

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:27 am

c/o Craig J. Lutz
Amer House of Fritztown
737 Fritztown Road
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204494035
Status:	Delivered: 01/19/2017 09:27 AM Signed for By: M.A
Reference:	112IC05958, 16
Signed for by:	M.A
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:30 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

AMER HOUSE OF FRITZTOWN
c/o Craig J Lutz
737 Fritztown Rd
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	American Legion Post 537 Telephone: 610-286-5920
Contact name:	Roger Jacobs, Post Commander
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Roger Jacobs at American Legion Post 537 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:47 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204516320 Delivered

Your package has been delivered

Tracking # 778204516320

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:42 am

c/o Roger Jacobs (Post Commander)
American Legion Post 537
4499 Twin Valley Road
MORGANTOWN, PA 19543
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204516320
Status:	Delivered: 01/19/2017 10:42 AM Signed for By: L.CREITZ
Reference:	112IC05958, 16
Signed for by:	L.CREITZ
Delivery location:	MORGANTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:47 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

AMERICAN LEGION POST 537
c/o Roger Jacobs, Post Commander
4499 Twin Valley Road
Morgantown, PA 19543

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Analytical Laboratory Svcs	Telephone: 717-944-5541
Contact name:	Peter Frick	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Peter Frick at Analytical Laboratory Svcs on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Mike Farling sent an email on January 25, 2017 (msf208@aol.com) requesting the map be sent to him. He was forwarded the letter only from Scott Brunk (Scott.Brunk@ALSGlobal.com). Mike is the owner of the building at 34 Dogwood Lane and stated that occupants of the building are on well water and it is used as an environmental laboratory. Josh Baird followed up with reqested map on January 26, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:23 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206145579 Delivered

Your package has been delivered

Tracking # 778206145579

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:14 am

c/o Peter Frick
Analytical Laboratory Svcs
34 Dogwood Lance
MIDDLETOWN, PA 17057
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206145579
Status:	Delivered: 01/19/2017 09:14 AM Signed for By: B.SCHAEFFER
Reference:	112IC05958, 16
Signed for by:	B.SCHAEFFER
Delivery location:	MIDDLETOWN, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:22 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ANALYTICAL LABORATORY SVCS
c/o Peter Frick
34 Dogwood Lance
Middletown, PA 17057

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Aqua PA Main Division	Telephone: 610-645-1082
Contact name:	Curt Steffy	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Curt Steffy at Aqua PA Main Division on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received voicemail and email from Craig Marleton, requesting digital AR site plans to aid in his review. Site plans were sent via FTP on 9/26/16; received an email on 9/27/16 inquiring about the Swedesford Road resource he saw on the Chester AR site plans. Advised that it is not part of the project anymore; sent an email with HDD plans and KMZ of the HDD in the area of their intake; received and email request for additional HDD drawings on 10/7/2016 and drawing was sent on 10/7/16. Extension was granted until 10/20/16. Letter received on 10/20/16 from AquaAmerica requesting meeting to discuss their concerns regarding potential impacts. Sunoco and AquaAmerica have been in coordination. On February 1, 2017 AquaAmerica sent a letter to PADEP indicating the ongoing investigations that Sunoco is performing on AquaAmerica's hillside wells. Per this letter, AquaAmerica expressed the assurance of cooperation between Sunoco and AquaAmerica.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:09 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275246803 Delivered

Your package has been delivered

Tracking # 777275246803

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 10:03 am

Curt Steffy
Aqua PA Main Division
762 Lancaster Avenue
BRYN MAWR, PA 19010
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275246803
Status:	Delivered: 09/21/2016 10:03 AM Signed for By: A.AUSTIN
Reference:	112IC05958, 16
Signed for by:	A.AUSTIN
Delivery location:	BRYN MAWR, PA
Delivered to:	Mailroom
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:09 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.





Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 10,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Aqua PA Uwchlan	Telephone: 610-645-1164
Contact name:	Curt Steffy	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Curt Steffy at Aqua PA Uwchlan on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 9:36 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470507716 Delivered

Your package has been delivered

Tracking # 777470507716

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Mon, 10/17/2016 9:34 am

Aqua PA Uwchlan
762 W Lancaster Avenue
BRYN MAWR, PA 19010
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470507716
Status:	Delivered: 10/17/2016 09:34 AM Signed for By: A.ALSTON
Reference:	112IC05958, 16
Signed for by:	A.ALSTON
Delivery location:	BRYN MAWR, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Adult Signature Required

	Deliver Weekday
Standard transit:	10/17/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:36 AM CDT on 10/17/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.





Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:
Sunoco Pipeline L.P.

Prepared By:
TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Assn of Baptist for World Evng	Telephone: 717-774-4400
Contact name:	Bruce Santos	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Bruce Santos at Assn of Baptist for World Evng on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:10 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206945033 Delivered

Your package has been delivered

Tracking # 778206945033

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:03 am

c/o Bruce Santos
Assn Of Baptist For Wold Evng
522 Lewisberry Road
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206945033
Status:	Delivered: 01/19/2017 10:03 AM Signed for By: T.PEQUIGNOT
Reference:	112IC05958, 16
Signed for by:	T.PEQUIGNOT
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Mailroom
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:09 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ASSN OF BAPTIST FOR WORLD EVNG
c/o Bruce Santos
522 Lewisberry Road
New Cumberland, PA 17070

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Autumn Est	Telephone: 814-695-0536
Contact name:	Matt Fowler	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Matt Fowler at Autumn Est on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:40 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275287755 Delivered

Your package has been delivered

Tracking # 777275287755

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 11:34 am

Matt Fowler
Autumn Est
117 Shaffer Lane
HOLLIDAYSBURG, PA 16648
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275287755
Status:	Delivered: 09/21/2016 11:34 AM Signed for By: B.SOLLENBERGER
Reference:	112IC05958, 16
Signed for by:	B.SOLLENBERGER
Delivery location:	HOLLIDAYSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:40 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

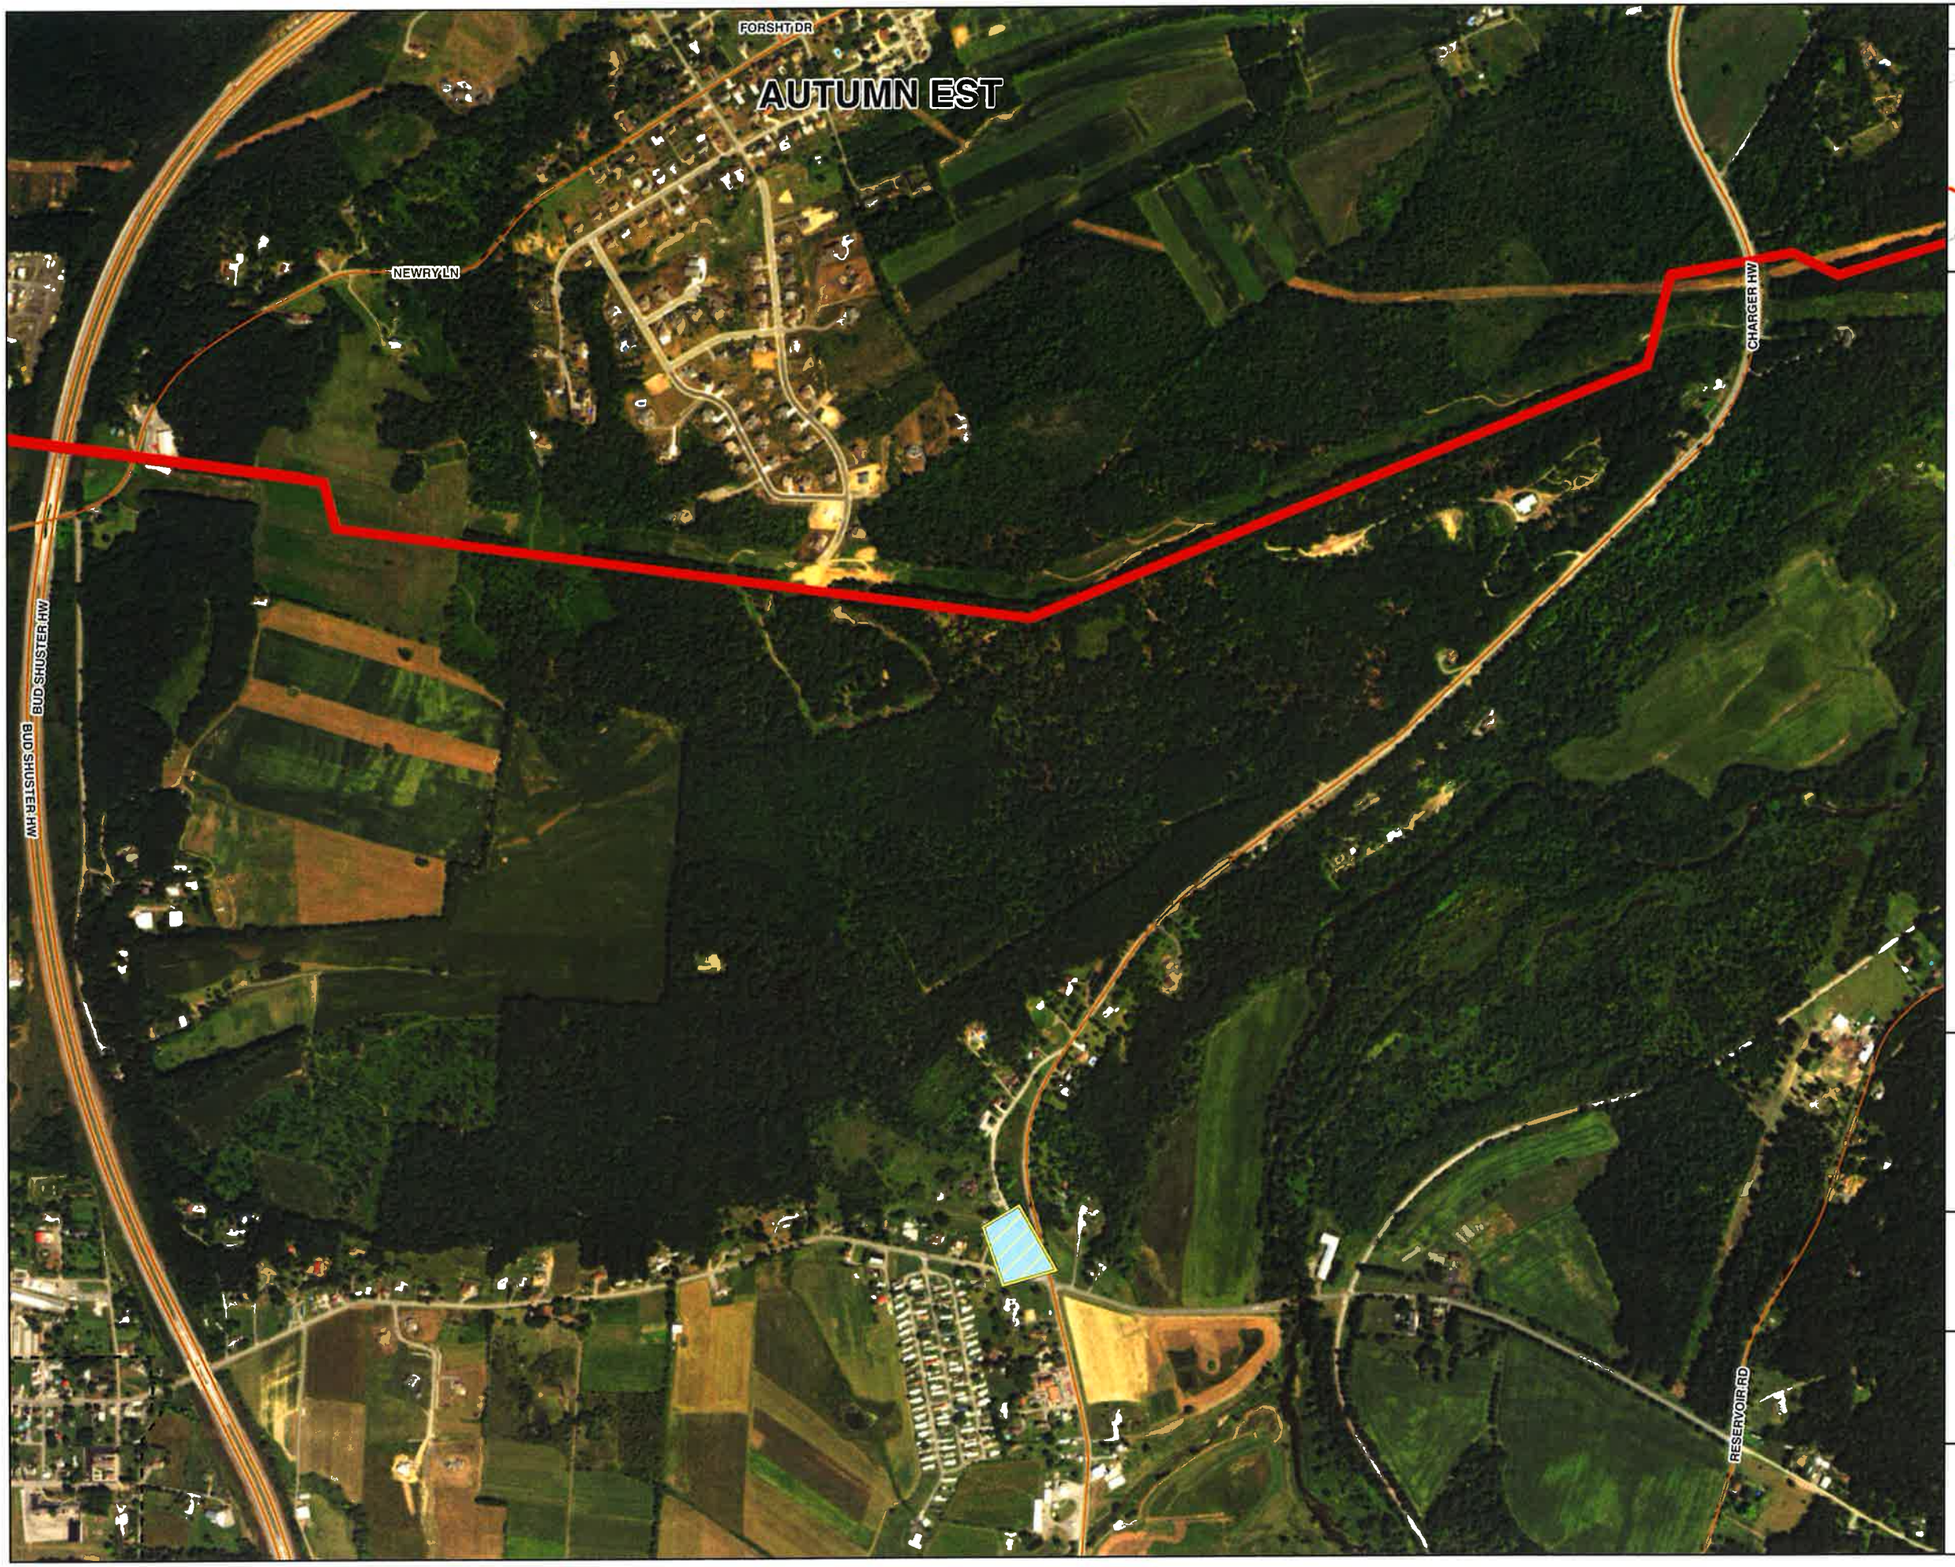



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Aviation Inn Telephone: 814-932-0595
Contact name:	Allen Butterbaugh
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Allen Butterbaugh at Aviation Inn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:29 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205827366 Delivered

Your package has been delivered

Tracking # 778205827366

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:26 am

c/o Allen Butterbaugh
Aviation Inn
721 E Logan Ave
ALTOONA, PA 16602
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205827366
Status:	Delivered: 01/19/2017 10:26 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	ALTOONA, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:28 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

AVIATION INN
c/o Allen Butterbaugh
721 E Logan Ave
Altoona, PA 16602

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Basil Pizzeria Telephone: 484-509-2066
Contact name:	Domenic Gentile
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Domenic Gentile at Basil Pizzeria on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 3:10 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204542199 Delivered

Your package has been delivered

Tracking # 778204542199

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 3:02 pm

c/o Domenic Gentile
Basil Pizzeria
776 Fritztown Rd
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204542199
Status:	Delivered: 01/19/2017 3:02 PM Signed for By: L.MANHOSIN
Reference:	112IC05958, 16
Signed for by:	L.MANHOSIN
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 2:07 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BASIL PIZZERIA
c/o Domenic Gentile
776 Fritztown Rd
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	BC Montessori Country Day Sch	Telephone: 610-777-3080
Contact name:	Cindy Rusnak - Director	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Cindy Rusnak at BC Montessori Country Day School on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:29 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204584611 Delivered

Your package has been delivered

Tracking # 778204584611

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:24 am

c/o Cindy Rusnak, Director
Bc Montessori
Country Day Sch
53 Vermont Road
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204584611
Status:	Delivered: 01/19/2017 10:24 AM Signed for By: G.RUSNAK
Reference:	112IC05958, 16
Signed for by:	G.RUSNAK
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:28 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BC MONTESSORI COUNTRY DAY SCH
c/o Cindy Rusnak - Director
53 Vermont Road
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Big Berthas Grill Telephone: 610-670-4540
Contact name:	Bob Schwartz
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Bob Schwartz at Big Berthas Grill on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:31 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204604628 Delivered

Your package has been delivered

Tracking # 778204604628

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:05 am

c/o Bob Schwartz
Big Berthas Grill
499 Mountain Home Rd
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204604628
Status:	Delivered: 01/19/2017 10:05 AM Signed for By: D.RUPP
Reference:	112IC05958, 16
Signed for by:	D.RUPP
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:31 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BIG BERTHAS GRILL
c/o Bob Schwartz
499 Mountain Home Rd
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Blair Twp Water & Sewer Auth	Telephone: 814-695-6300
Contact name:	Joseph Pyzowski	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Joseph Pyzowski at Blair Twp Water & Sewer Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Spoke with Tim on 9/21/16, he requested new maps zoomed out to the West, as well as zoomed in around the Holtzinger property. Mapping was provided on 9/22/16 via email. Spoke with Tim again on 10/18/16, he gave verbal approval, pending 30 ft clearance from culdesac.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:04 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276040324 Delivered

Your package has been delivered

Tracking # 777276040324

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:58 am

Joseph Pyzowski
Blair Twp Water and Sewer Authority
377 Cedarcrest Drive
DUNCANSVILLE, PA 16635
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276040324
Status:	Delivered: 09/21/2016 11:58 AM Signed for By: K.MCGRAW
Reference:	112IC05958, 16
Signed for by:	K.MCGRAW
Delivery location:	DUNCANSVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:03 AM CDT on 09/21/2016.


All weights are estimated.


To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

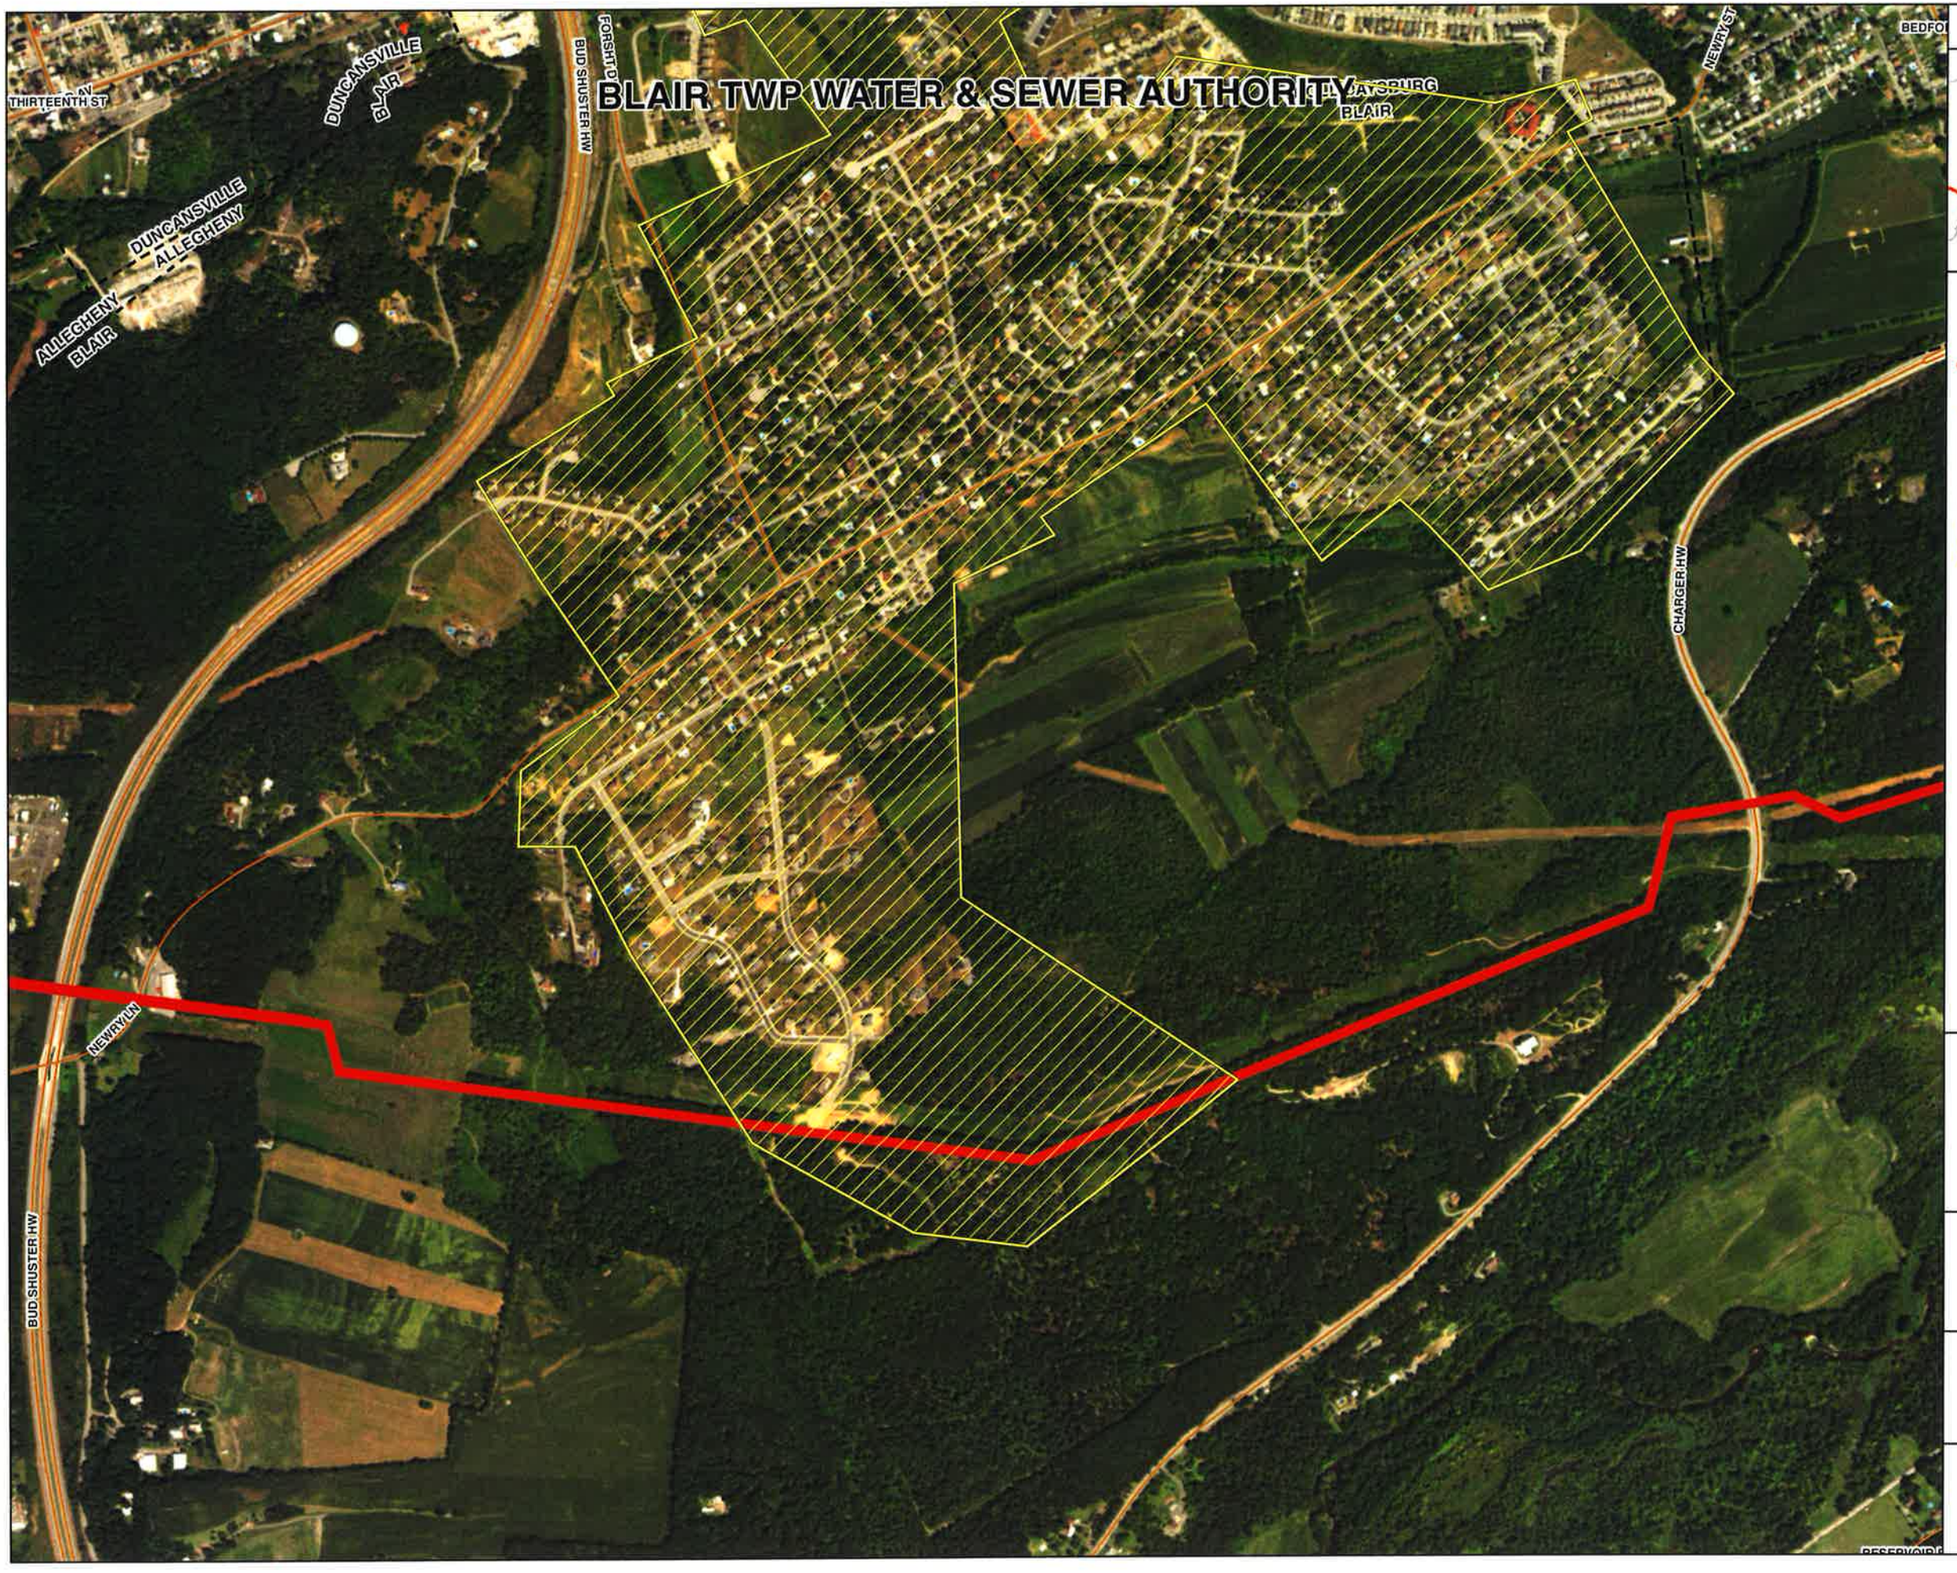



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Blairsville Muni Auth	Telephone: 724-459-9100
Contact name:	Ron Hood	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ron Hood at Blairsville Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:15 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275338690 Delivered

Your package has been delivered

Tracking # 777275338690

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 11:12 am

Ron Hood
Blairsville Muni Authority
203 Market St
BLAIRSVILLE, PA 15717
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275338690
Status:	Delivered: 09/21/2016 11:12 AM Signed for By: S.LEE
Reference:	112IC05958, 16
Signed for by:	S.LEE
Delivery location:	BLAIRSVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:15 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

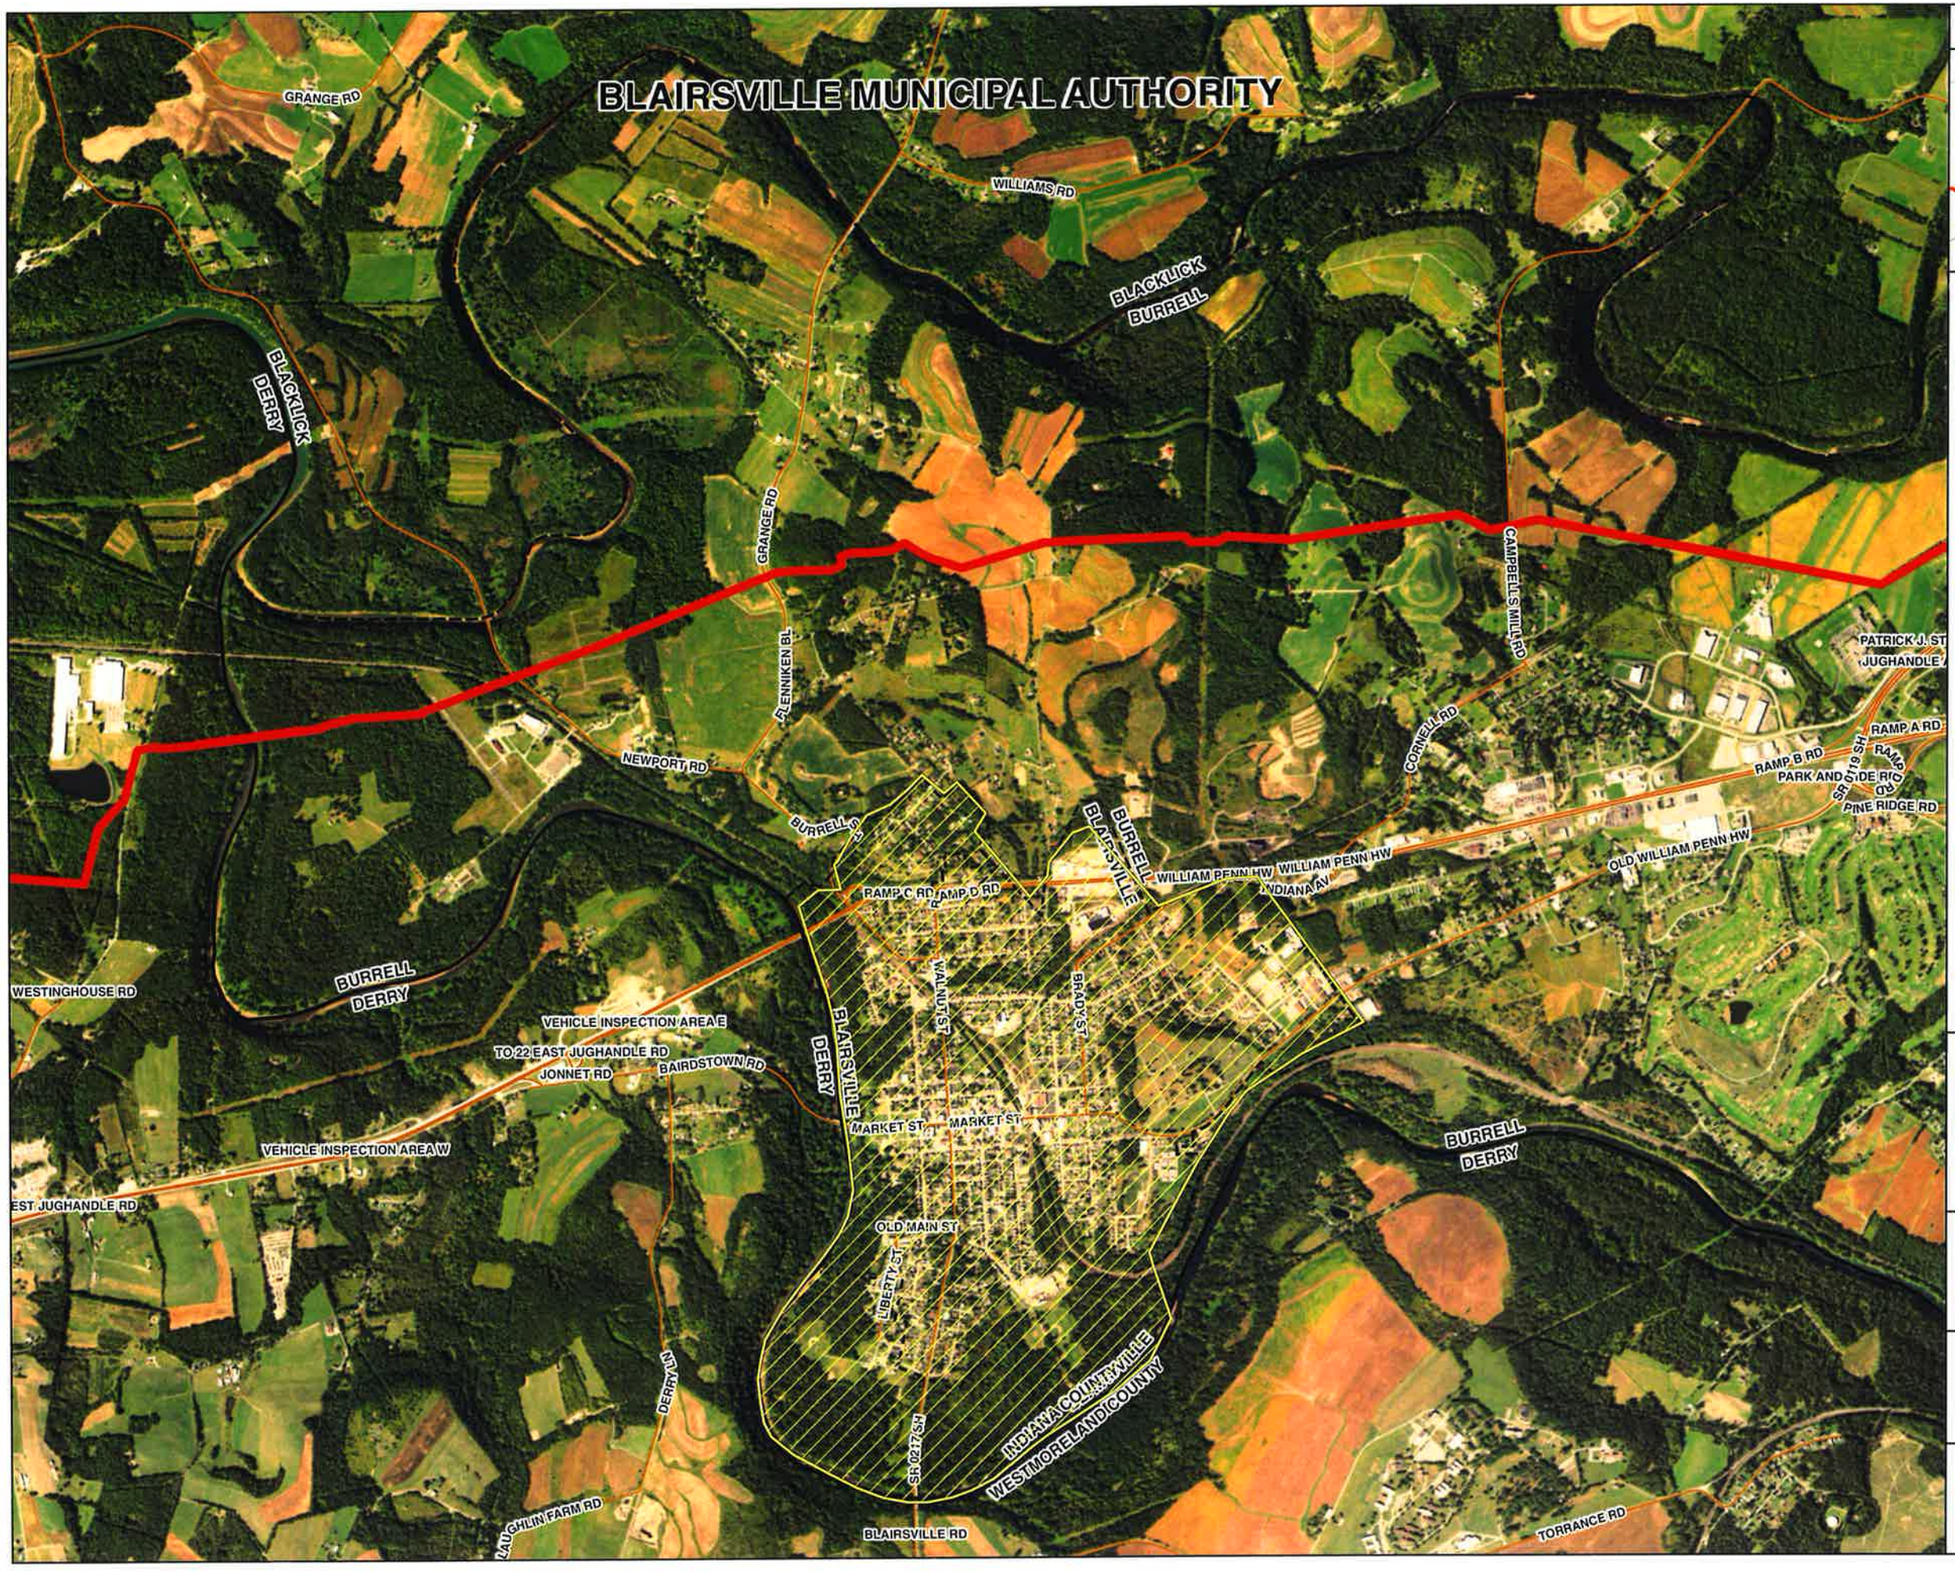

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Branch Cpgrd	Telephone: 814-643-0485
Contact name:	Ed Paterson	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ed Paterson at Branch Cpgrd on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:51 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206508299 Delivered

Your package has been delivered

Tracking # 778206508299

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:46 am

c/o Robert Moyer
Branch Cpgrd
203 Weaver Road
DUNCANSVILLE, PA 16635
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206508299
Status:	Delivered: 01/19/2017 10:46 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	DUNCANSVILLE, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

	Residential Delivery
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:50 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BRANCH CPGRD
c/o Robert Moyer
203 Weaver Road
Duncansville, PA 16635

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Brecknock Academy Telephone: 610-777-2980
Contact name:	Robert Graffius - Director
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Robert Graffius at Brecknock Academy on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:58 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204634046 Delivered

Your package has been delivered

Tracking # 778204634046

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:56 am

c/o Robert Graffius, Director
Brecknock Academy
4273 New Holland Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204634046
Status:	Delivered: 01/19/2017 09:56 AM Signed for By: R.GRAFFIUS
Reference:	112IC05958, 16
Signed for by:	R.GRAFFIUS
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:58 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BRECKNOCK ACADEMY
c/o Robert Graffius, Director
4273 New Holland Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Brecknock Twp Fire Company	Telephone: 610-777-9575
Contact name:	Russell Fryberger - President	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Russell Fryberger at Brecknock Twp Fire Company on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:09 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204670835 Delivered

Your package has been delivered

Tracking # 778204670835

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:06 am

c/o Russell Fryberger, President
Brecknock Twp Fire Company
1153 Kurtz Mill Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204670835
Status:	Delivered: 01/19/2017 10:06 AM Signed for By: V.BRUNO
Reference:	112IC05958, 16
Signed for by:	V.BRUNO
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:09 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BRECKNOCK TWP FIRE COMPANY
c/o Russell Fryberger, President
1153 Kurtz Mill Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Bush Recreation Area	Telephone: 729-639-9013
Contact name:	David Bishop	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to David Bishop at Bush Recreation Area on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:17 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206889095 Delivered

Your package has been delivered

Tracking # 778206889095

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 11:12 am

c/o David Bishop, Resource Mgr.
Bush Recreation Area
440 Loyalhanna Dam Road
SALTSBURG, PA 15681
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206889095
Status:	Delivered: 01/19/2017 11:12 AM Signed for By: P.TOMAN
Reference:	112IC05958, 16
Signed for by:	P.TOMAN
Delivery location:	SALTSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:17 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

BUSH RECREATION AREA
c/o David Bishop, Resource Mgr.
440 Loyalhanna Dam Road
Saltsburg, PA 15681

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Camp Adahi & Adahi Kids	Telephone: 610-856-7520
Contact name:	Judy Stump – Exc Dirng	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Judy Stump at Camp Adahi and Adahi Kids on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:51 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204709081 Delivered

Your package has been delivered

Tracking # 778204709081

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:46 am

c/o Judy Stump
Camp Adahi & Adahi Kids
172 Hartz Store Rd
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204709081
Status:	Delivered: 01/19/2017 09:46 AM Signed for By: S.PICCONE
Reference:	112IC05958, 16
Signed for by:	S.PICCONE
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:50 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CAMP ADAHI & ADAHI KIDS
c/o Judy Stump - Exc Dirng
172 Hartz Store Rd
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,



Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Camp Hill State Correctional Inst	Telephone: Not available
Contact name:	Matthew Klopotek	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Matthew Klopotek at Camp Hill State Correctional Inst on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received and email from Matthew Klopotek on 9/23/16 requesting additional mapping, which was sent via email on 9/23/16. Received an email on 10/17 from Howard Gouse expressing a finding of no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 11:26 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470701518 Delivered

Your package has been delivered

Tracking # 777470701518

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Mon, 10/17/2016 11:24 am

Camp Hill State Correctional Inst.
2500 Lisburn Road
CAMP HILL, PA 17011
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470701518
Status:	Delivered: 10/17/2016 11:24 AM Signed for By: J.JOHNSON
Reference:	112IC05958, 16
Signed for by:	J.JOHNSON
Delivery location:	CAMP HILL, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Adult Signature Required

	Deliver Weekday
Standard transit:	10/17/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:26 AM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

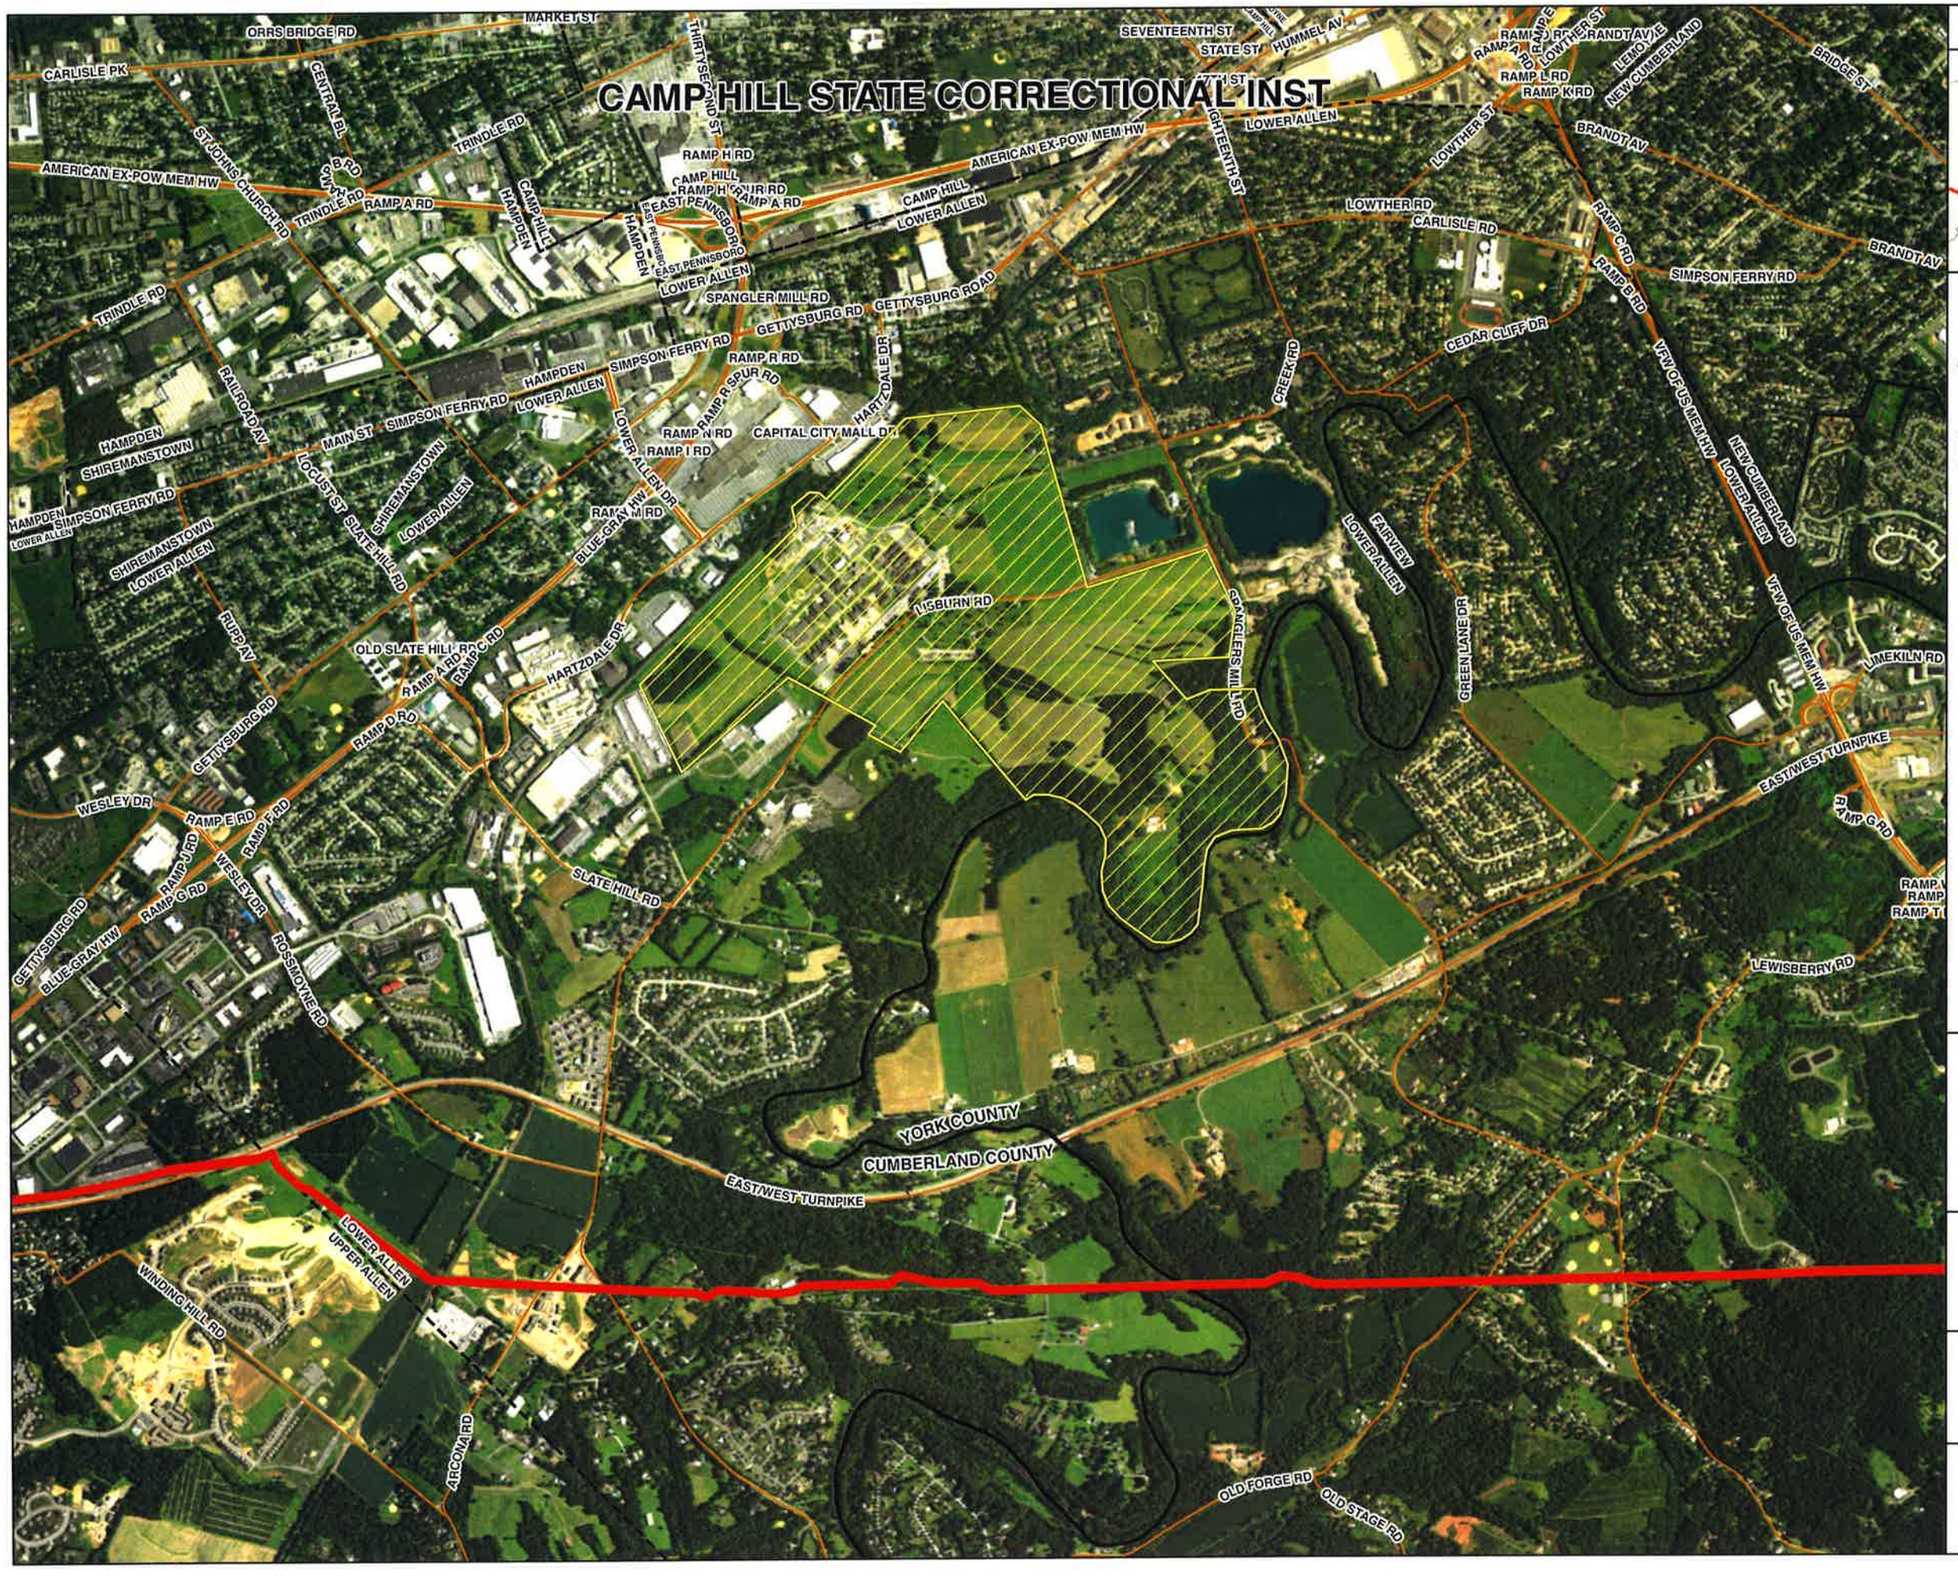

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Canonsburg Sportsment Associatn	Telephone: 724-745-0527
Contact name:	Matt Urham	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Matt Urham at Canonsburg Sportsment Associatn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7774

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

CANONSBURG, PA 15317

OFFICIAL USE

Certified Mail Fee	$3.30
$	$0.00
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
$	
Total Postage and Fees	$4.87
$	

0205
21

Postmark Here

01/19/2017

Sent To: CANONSBURG SPORTSMEN ASSOC.
Street and Apt.: c/o MATT URHAM
City, State, ZIP+: P.O. BOX 298
CANONSBURG, PA 15317

PS Form 3800

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237774

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 25, 2017 , 3:10 pm	**Available for Pickup**	**CANONSBURG, PA 15317**
Your item arrived at the CANONSBURG, PA 15317 post office at 3:10 pm on January 25, 2017 and is ready for pickup.		
January 21, 2017 , 8:38 am	Available for Pickup	CANONSBURG, PA 15317
January 20, 2017 , 6:12 pm	Arrived at USPS Facility	WARRENDALE, PA 15086
January 20, 2017 , 8:56 am	Arrived at USPS Destination Facility	PITTSBURGH, PA 15290
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

CANONSBURG SPORTSMEN ASSOCIATN
c/o Matt Urham
P.O. Box 298
Canonsburg, PA 15317

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Car Sense Uwchland	Telephone: 610-458-3700
Contact name:	Tony Gorgone	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Tony Gorgone at Car Sense Uwchland on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:35 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205958986 Delivered

Your package has been delivered

Tracking # 778205958986

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:21 am

c/o Tony Gorgone
Car Sense Uwchland
21 Pottstown Pike
UWCHLAND, PA 19480
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205958986
Status:	Delivered: 01/19/2017 09:21 AM Signed for By: T.TETITTA
Reference:	112IC05958, 16
Signed for by:	T.TETITTA
Delivery location:	UWCHLAND, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:35 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CAR SENSE UWCHLAND
c/o Tony Gorgone
21 Pottstown Pike
Uwchland, PA 19480

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Carlisle Ys Mens Club	Telephone: 717-243-1892
Contact name:	Lewis Burgett	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Lewis Burgett at Carlisle Ys Mens Club on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:14 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206014018 Delivered

Your package has been delivered

Tracking # 778206014018

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:08 am

c/o Lewis Burgett
Carlisle Ys Mens Club
311 Southwest Street
CARLISLE, PA 17013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206014018
Status:	Delivered: 01/19/2017 10:08 AM Signed for By: K.TRACY
Reference:	112IC05958, 16
Signed for by:	K.TRACY
Delivery location:	CARLISLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:13 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CARLISLE YS MENS CLUB
c/o Lewis Burgett
311 Southwest Street
Carlisle, PA 17013

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Catering by John Lowe Telephone: 610-873-7229
Contact name:	John Lowe
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to John Lowe at Catering by John Lowe on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:52 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204727600 Delivered

Your package has been delivered

Tracking # 778204727600

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:47 am

c/o John Lowe
Catering By John Lowe
400 N. Guthriesville Road
DOWNINGTOWN, PA 19335
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204727600
Status:	Delivered: 01/19/2017 09:47 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	DOWNINGTOWN, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:52 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CATERING BY JOHN LOWE
c/o John Lowe
400 N. Guthriesville Road
Downingtown, PA 19335

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Cernarvon Twp Auth	Telephone: 610-286-1017
Contact name:	Robert Weaver	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Robert Weaver at Cernarvon Twp Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:05 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275360523 Delivered

Your package has been delivered

Tracking # 777275360523

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:59 am

Robert Weaver
Caernarvon Township Authority
601 Hemlock Road
CAERNARVON, PA 19543
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275360523
Status:	Delivered: 09/21/2016 11:59 AM Signed for By: C.BOWMAN
Reference:	112IC05958, 16
Signed for by:	C.BOWMAN
Delivery location:	CAERNARVON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:04 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

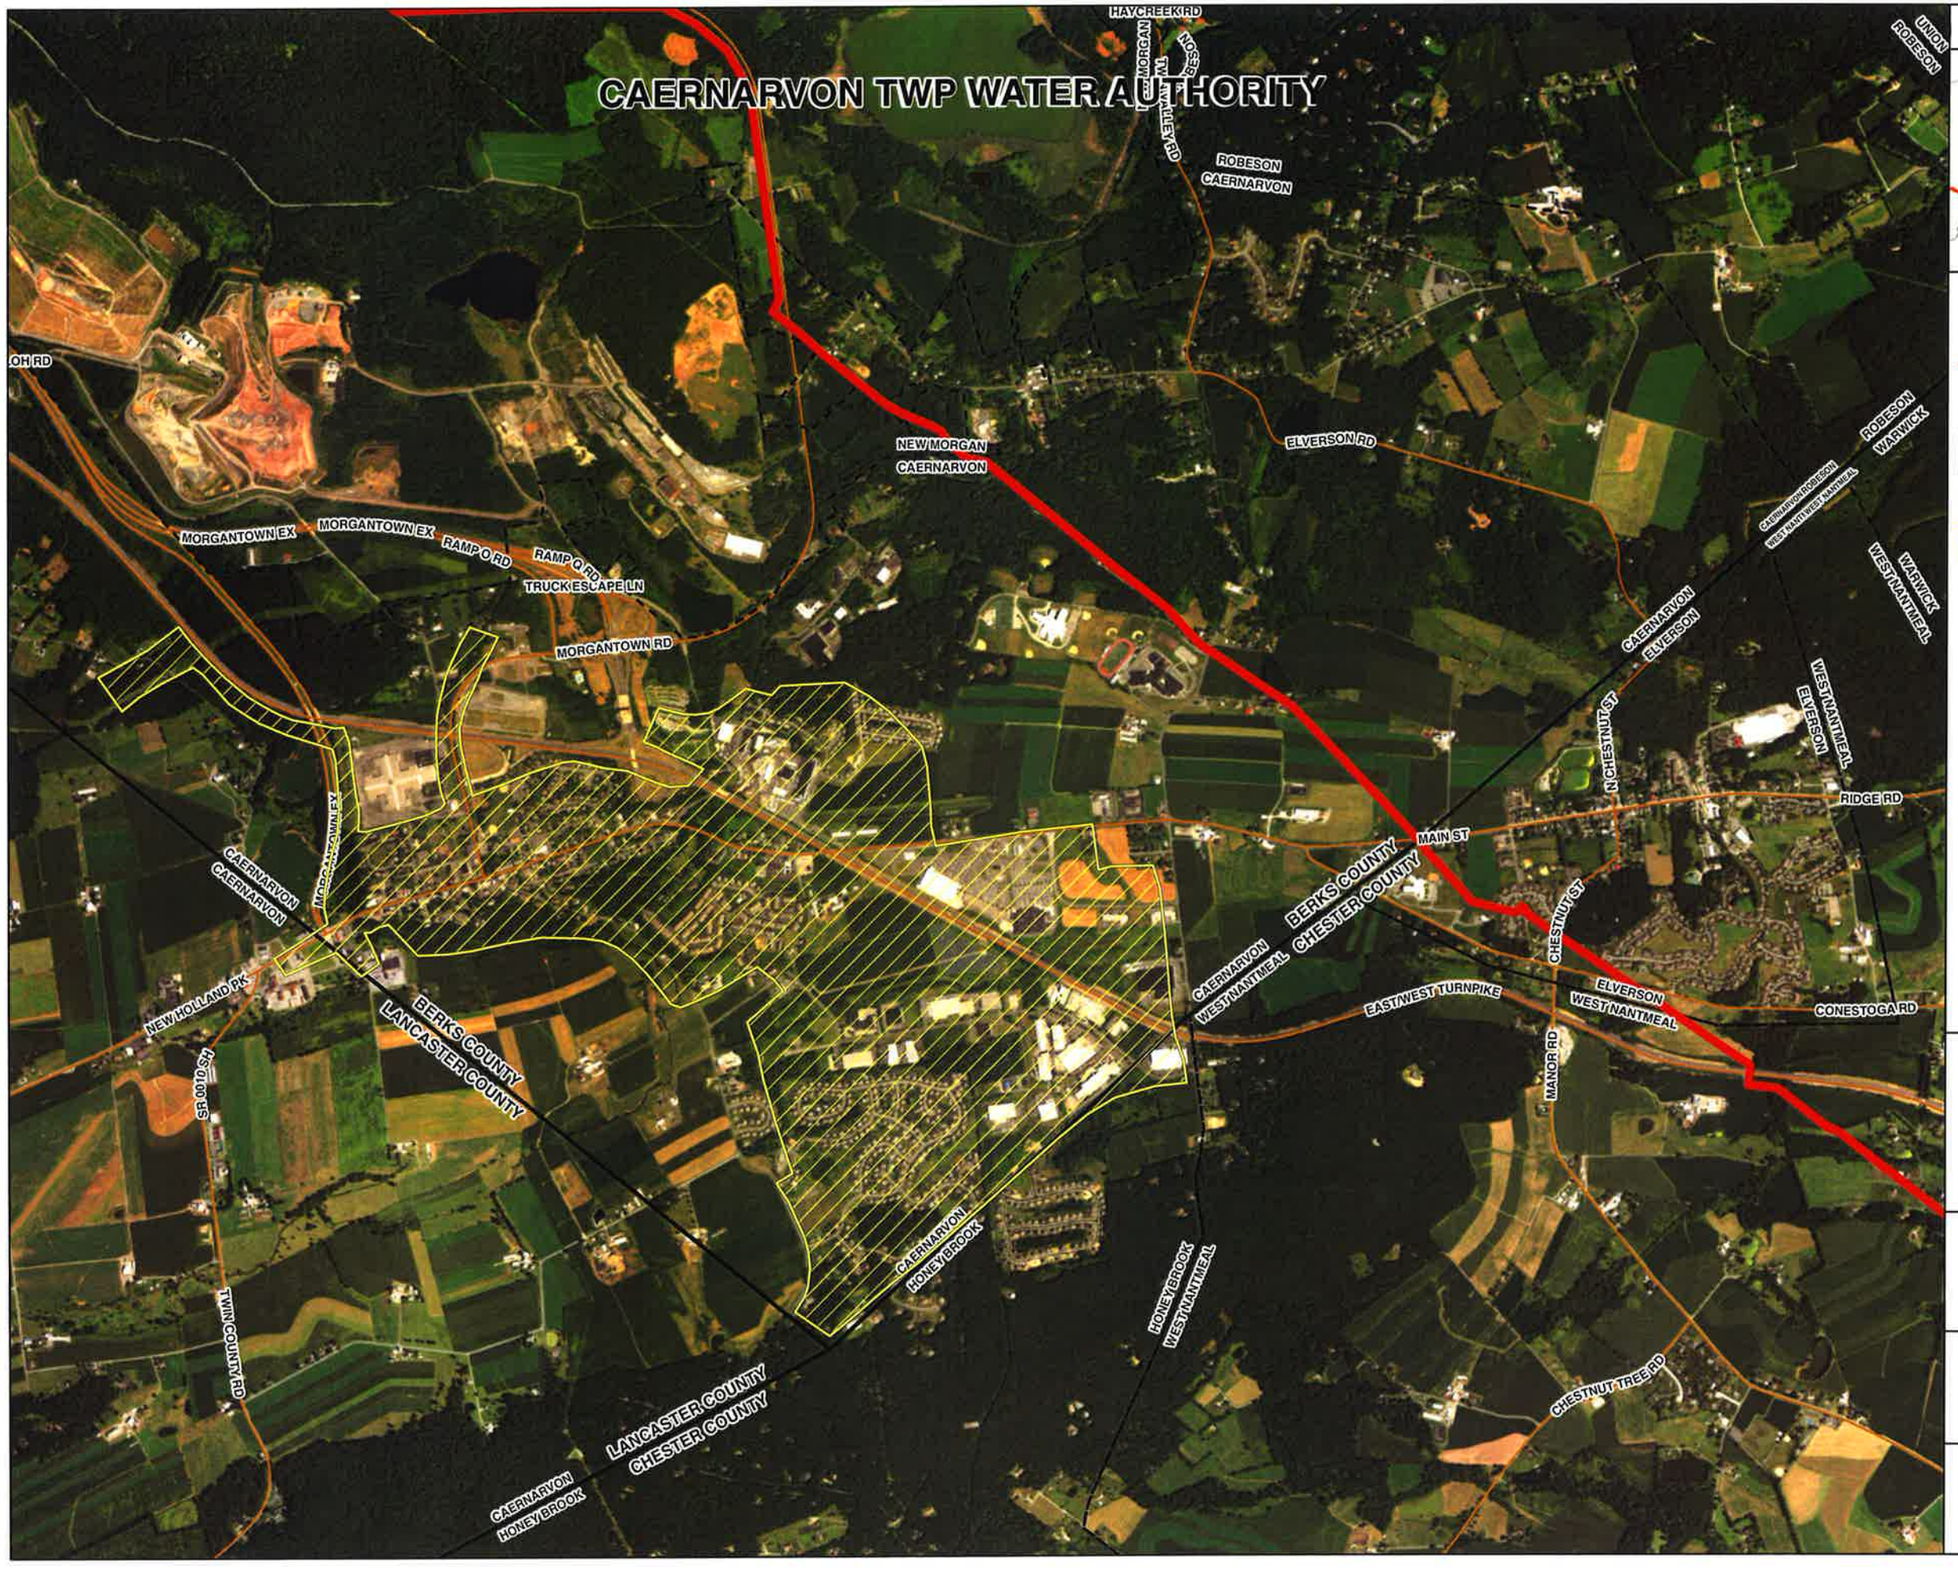

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Chester Water Authority	Telephone: 610-876-8185
Contact name:	Robert Judge	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Robert Judge at Chester Water Authority on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Email received on 10/7/16 stating a Letter of No Objection had been signed.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 9:10 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470722733 Delivered

Your package has been delivered

Tracking # 777470722733

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Mon, 10/17/2016 9:06 am

Chester Water Authority
415 Welsh Street
CHESTER, PA 19013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470722733
Status:	Delivered: 10/17/2016 09:06 AM Signed for By: D.WELLS
Reference:	112IC05958, 16
Signed for by:	D.WELLS
Delivery location:	CHESTER, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Adult Signature Required

	Deliver Weekday
Standard transit:	10/17/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:09 AM CDT on 10/17/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 12,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Cocalico Creek Cpgrd	Telephone: 717-336-2014
Contact name:	Jody Rampolla	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Jody Rampolla at Cocalico Creek Cpgrd on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Jody Rampolla called on January 19, 2017 and requested a different map be sent to her.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:05 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206554357 Delivered

Your package has been delivered

Tracking # 778206554357

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:32 am

c/o Jody Rampolla
Cocalico Creek Cpgrd
560 Cocalico Creek
DENVER, PA 17517
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206554357
Status:	Delivered: 01/19/2017 10:32 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	DENVER, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:05 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

COCALICO CREEK CPGRD
c/o Jody Rampolla
560 Cocalico Creek
Denver, PA 17517

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Community Fire Co of Frityztown	Telephone: 610-678-0502
Contact name:	Ray Dilaplane – Head Trustee	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ray Dilaplane at Community Fire Co of Fritztown on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 3:13 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204787877 Delivered

Your package has been delivered

Tracking # 778204787877

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 3:08 pm

c/o Ray Dilaplane
Community Fire Co of Fritztown
1060 Fritztown Rd
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204787877
Status:	Delivered: 01/19/2017 3:08 PM Signed for By: P.RICE
Reference:	112IC05958, 16
Signed for by:	P.RICE
Delivery location:	SINKING SPRING, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 2:13 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

COMMUNITY FIRE CO OF FRITZTOWN
c/o Ray Dilaplane Head Trustee
1060 Fritztown Rd
Sinking Spring, PA 19608

Reference: Sunoco Pipeline L.P. – Pennsylvania Pipeline Project
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Cornwall Boro Muni Auth	Telephone: 717-274-5441
Contact name:	Bob Henry	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Bob Henry at Cornwall Boro Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email from Bard Henry on 10/4/16 requesting further consulation. Spoke with her on 10/7/16, Barb emailed a map. The authority signed a Letter of No Objection.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:12 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275460949 Delivered

Your package has been delivered

Tracking # 777275460949

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 12:08 pm

Barb Henry
Cornwall Boro Muni Authority
44 Rexmont Road
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275460949
Status:	Delivered: 09/21/2016 12:08 PM Signed for By: B.HENRY
Reference:	112IC05958, 16
Signed for by:	B.HENRY
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:12 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Country View Est	Telephone: 717-776-7109
Contact name:	John D Walter	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	


A letter was sent to John D Walter at Country View Est on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.


Delivery confirmation indicated the letter was received on September 23, 2016.

Received a call on 9/23/16 from Mr. Walter, verbally stating no impact, but was going to review the package when he received it.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Country View Estates – PWS Delivery Confirmation

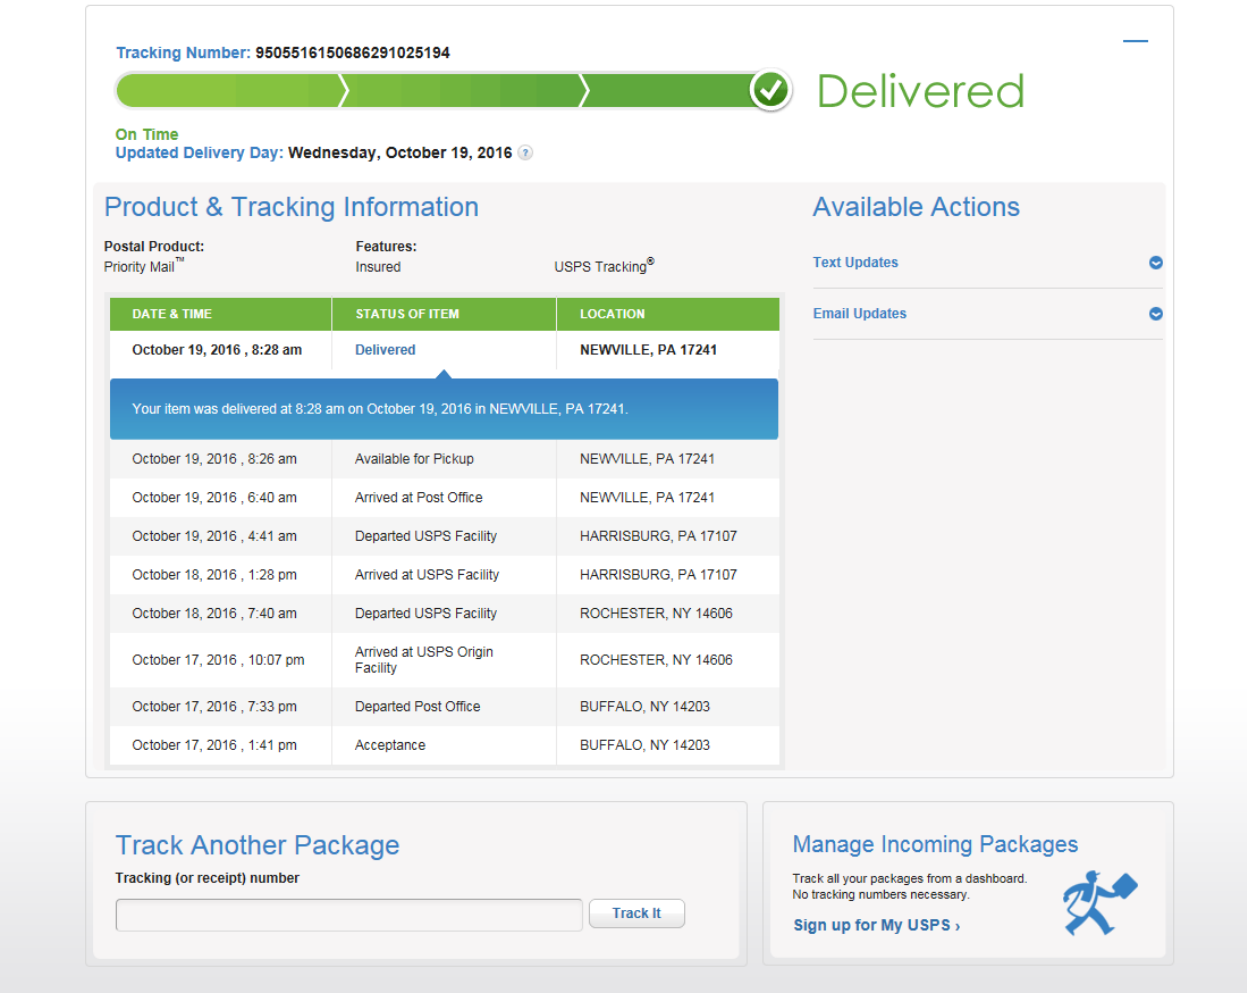

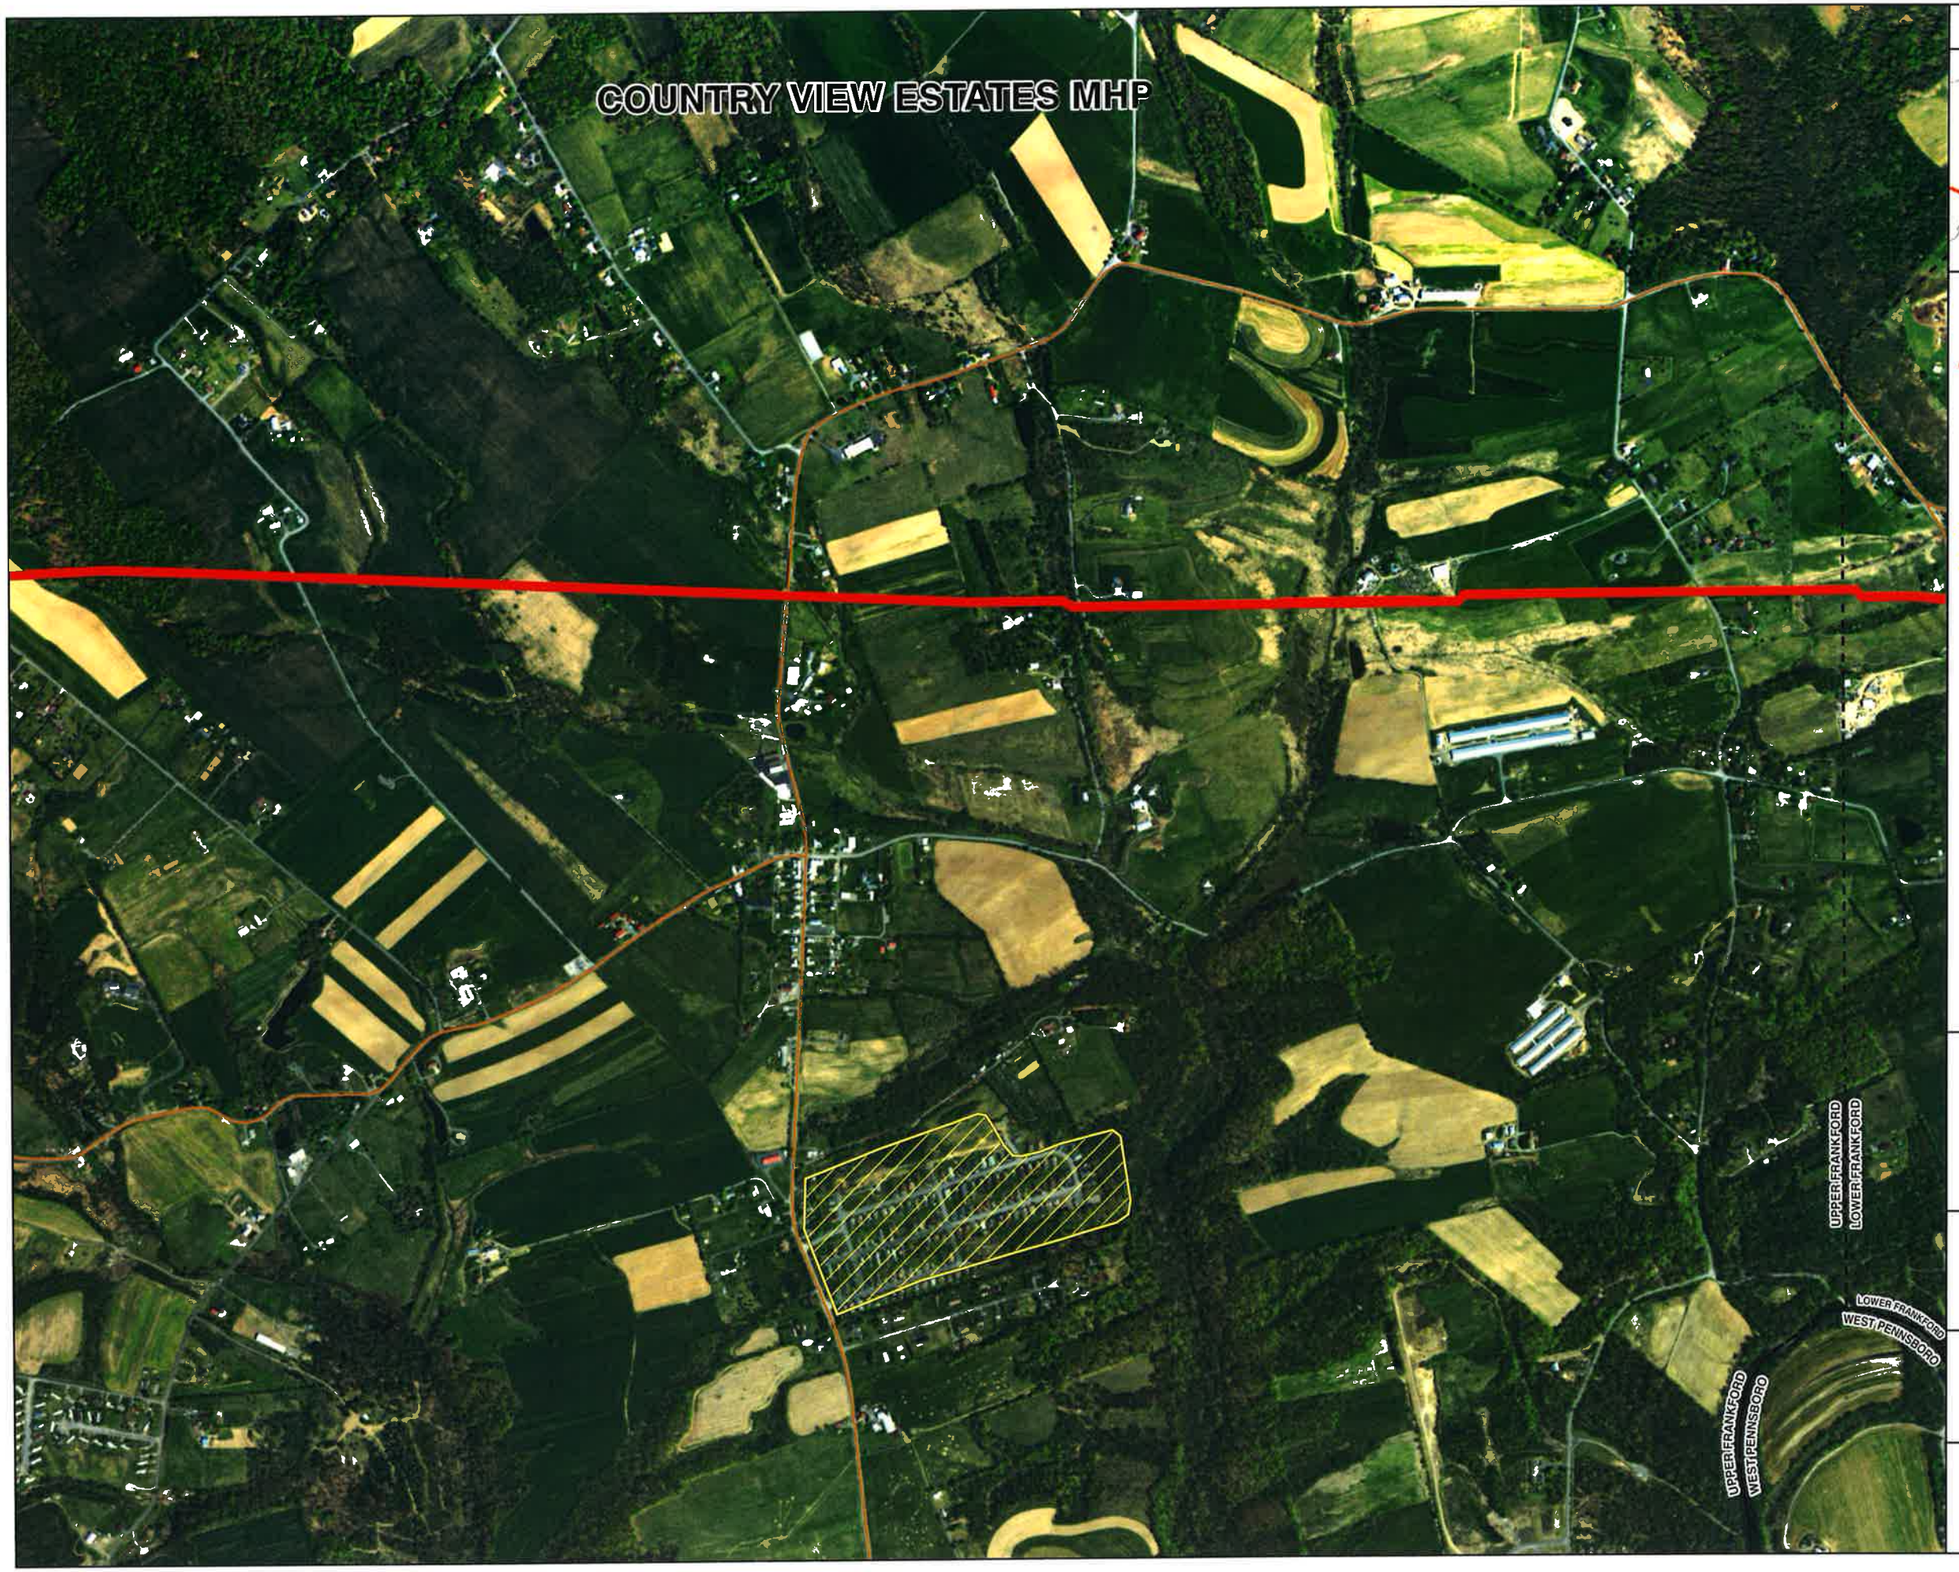

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Creek View Mobile Home Commun	Telephone: 717-245-2100
Contact name:	Justin Neidlinger	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Justin Neidlinger at Creek View Mobile Home Commun on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:23 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275498508 Delivered

Your package has been delivered

Tracking # 777275498508

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 12:12 pm

Justin Neidlinger
Creek View Mobile Home Community
493 Potato Road
CARLISLE, PA 17013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275498508
Status:	Delivered: 09/21/2016 12:12 PM Signed for By: L.JOHN
Reference:	112IC05958, 16
Signed for by:	L.JOHN
Delivery location:	CARLISLE, PA
Delivered to:	Residence
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
	Residential Delivery
Standard transit:	9/21/2016 by 8:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:22 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

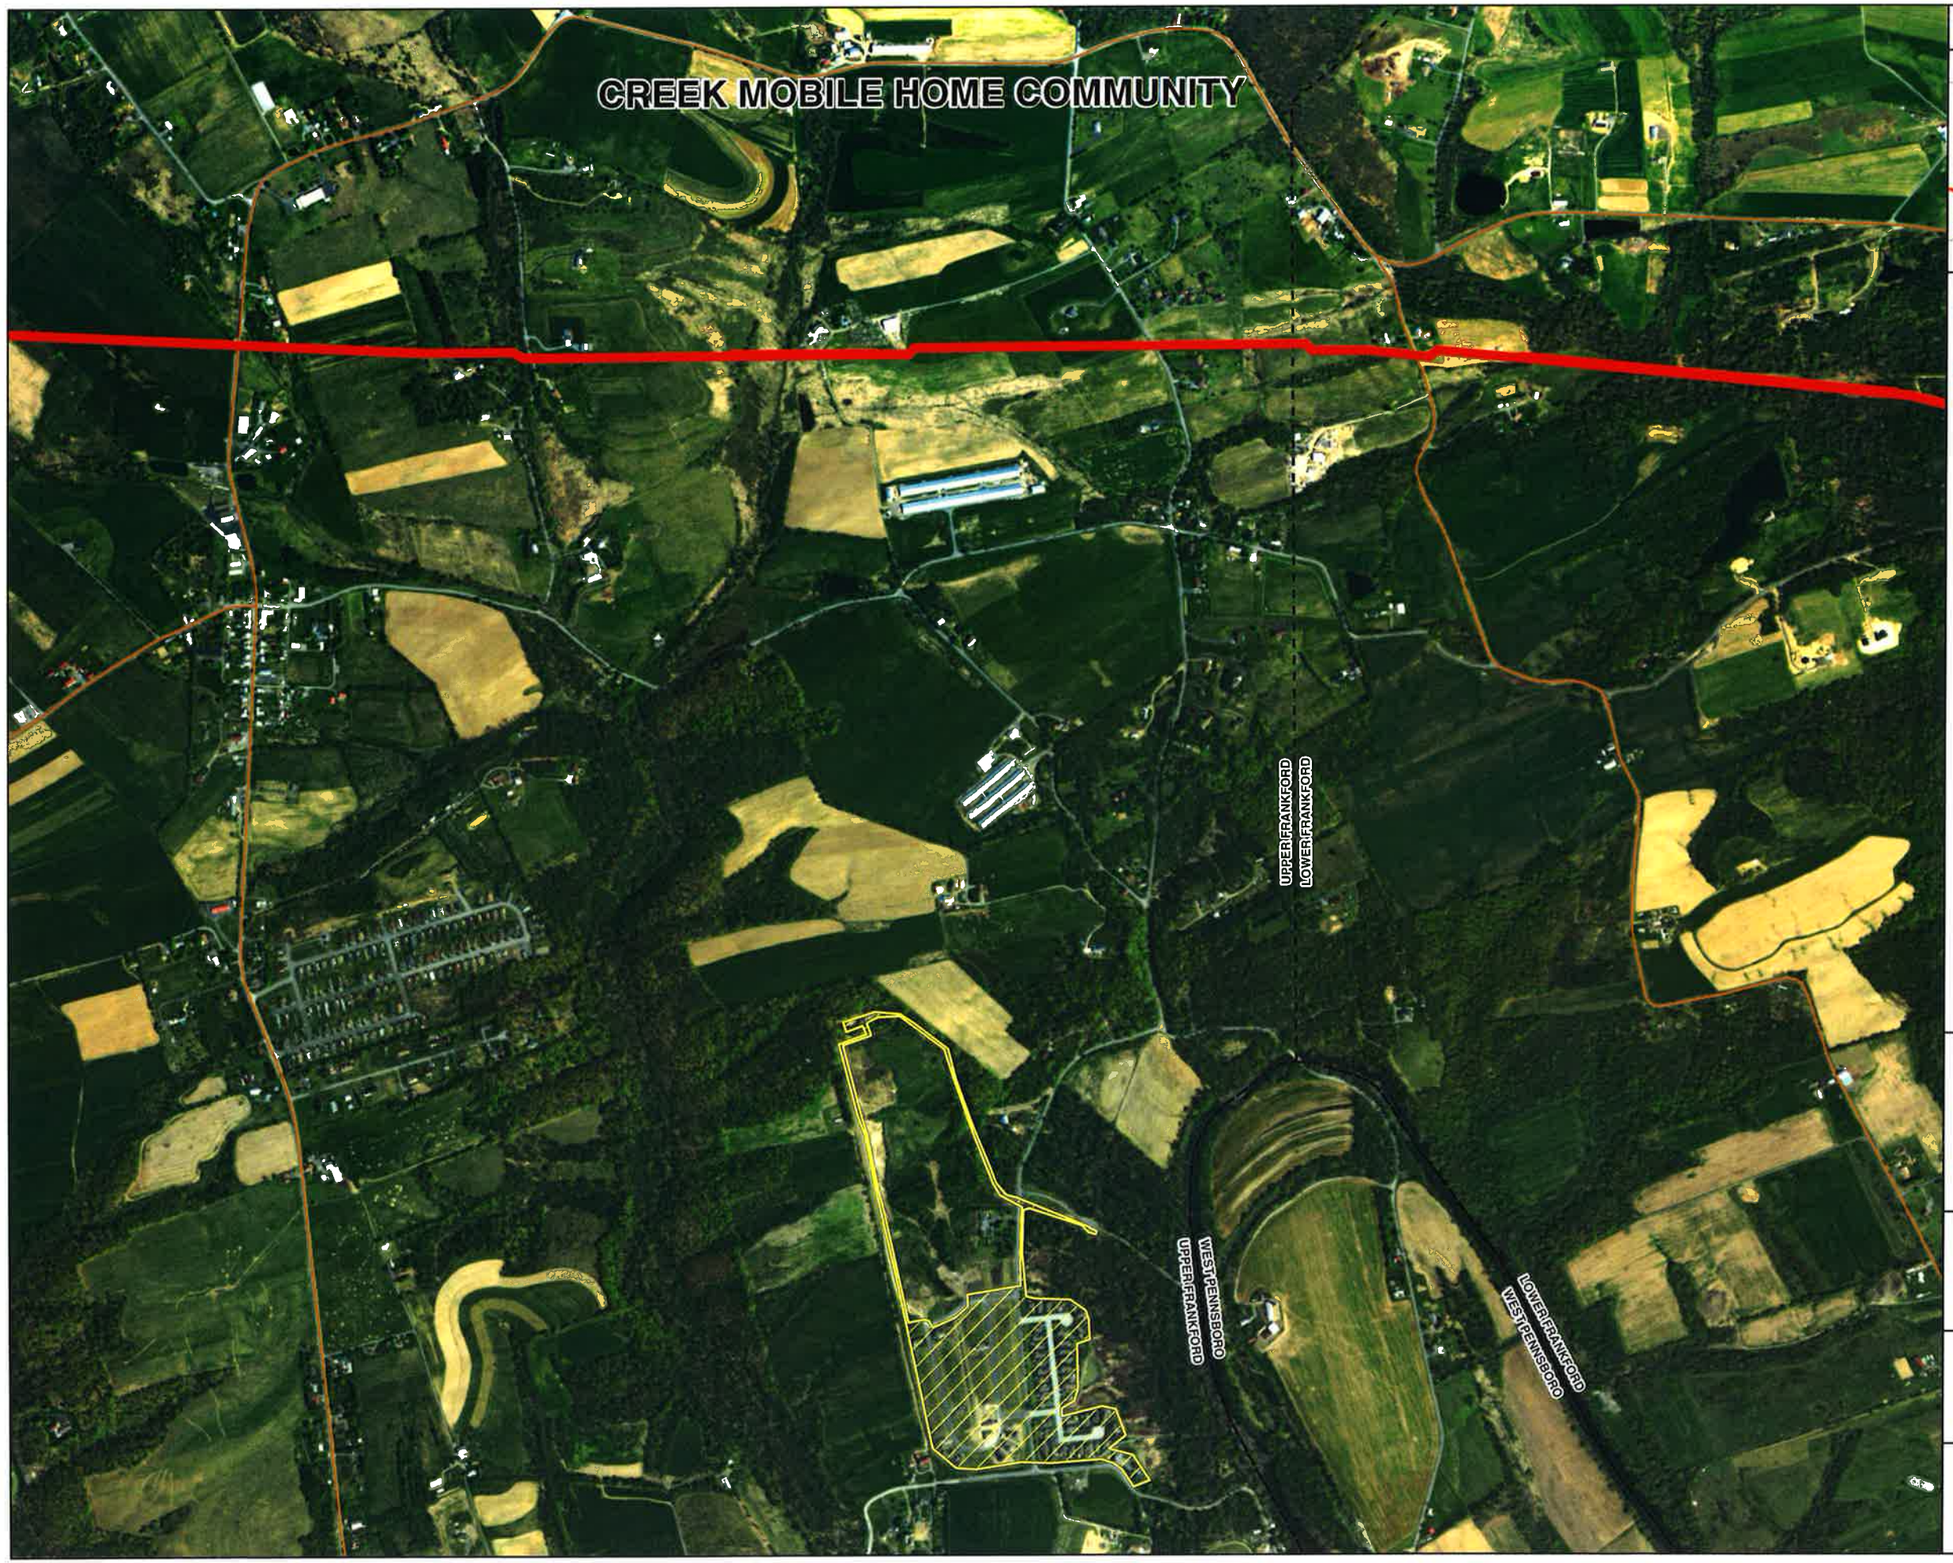

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Cresson Boro Water Sys	Telephone: 814-886-2139
Contact name:	Joseph Pupo	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Joseph Pupo at Cresson Boro Water Sys on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:48 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275588750 Delivered

Your package has been delivered

Tracking # 777275588750

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 10:44 am

Joseph Pupo
Cresson Boro Water Sys
631 Second Street
CRESSON, PA 16630
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275588750
Status:	Delivered: 09/21/2016 10:44 AM Signed for By: J.EAGER
Reference:	112IC05958, 16
Signed for by:	J.EAGER
Delivery location:	CRESSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:48 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.


Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

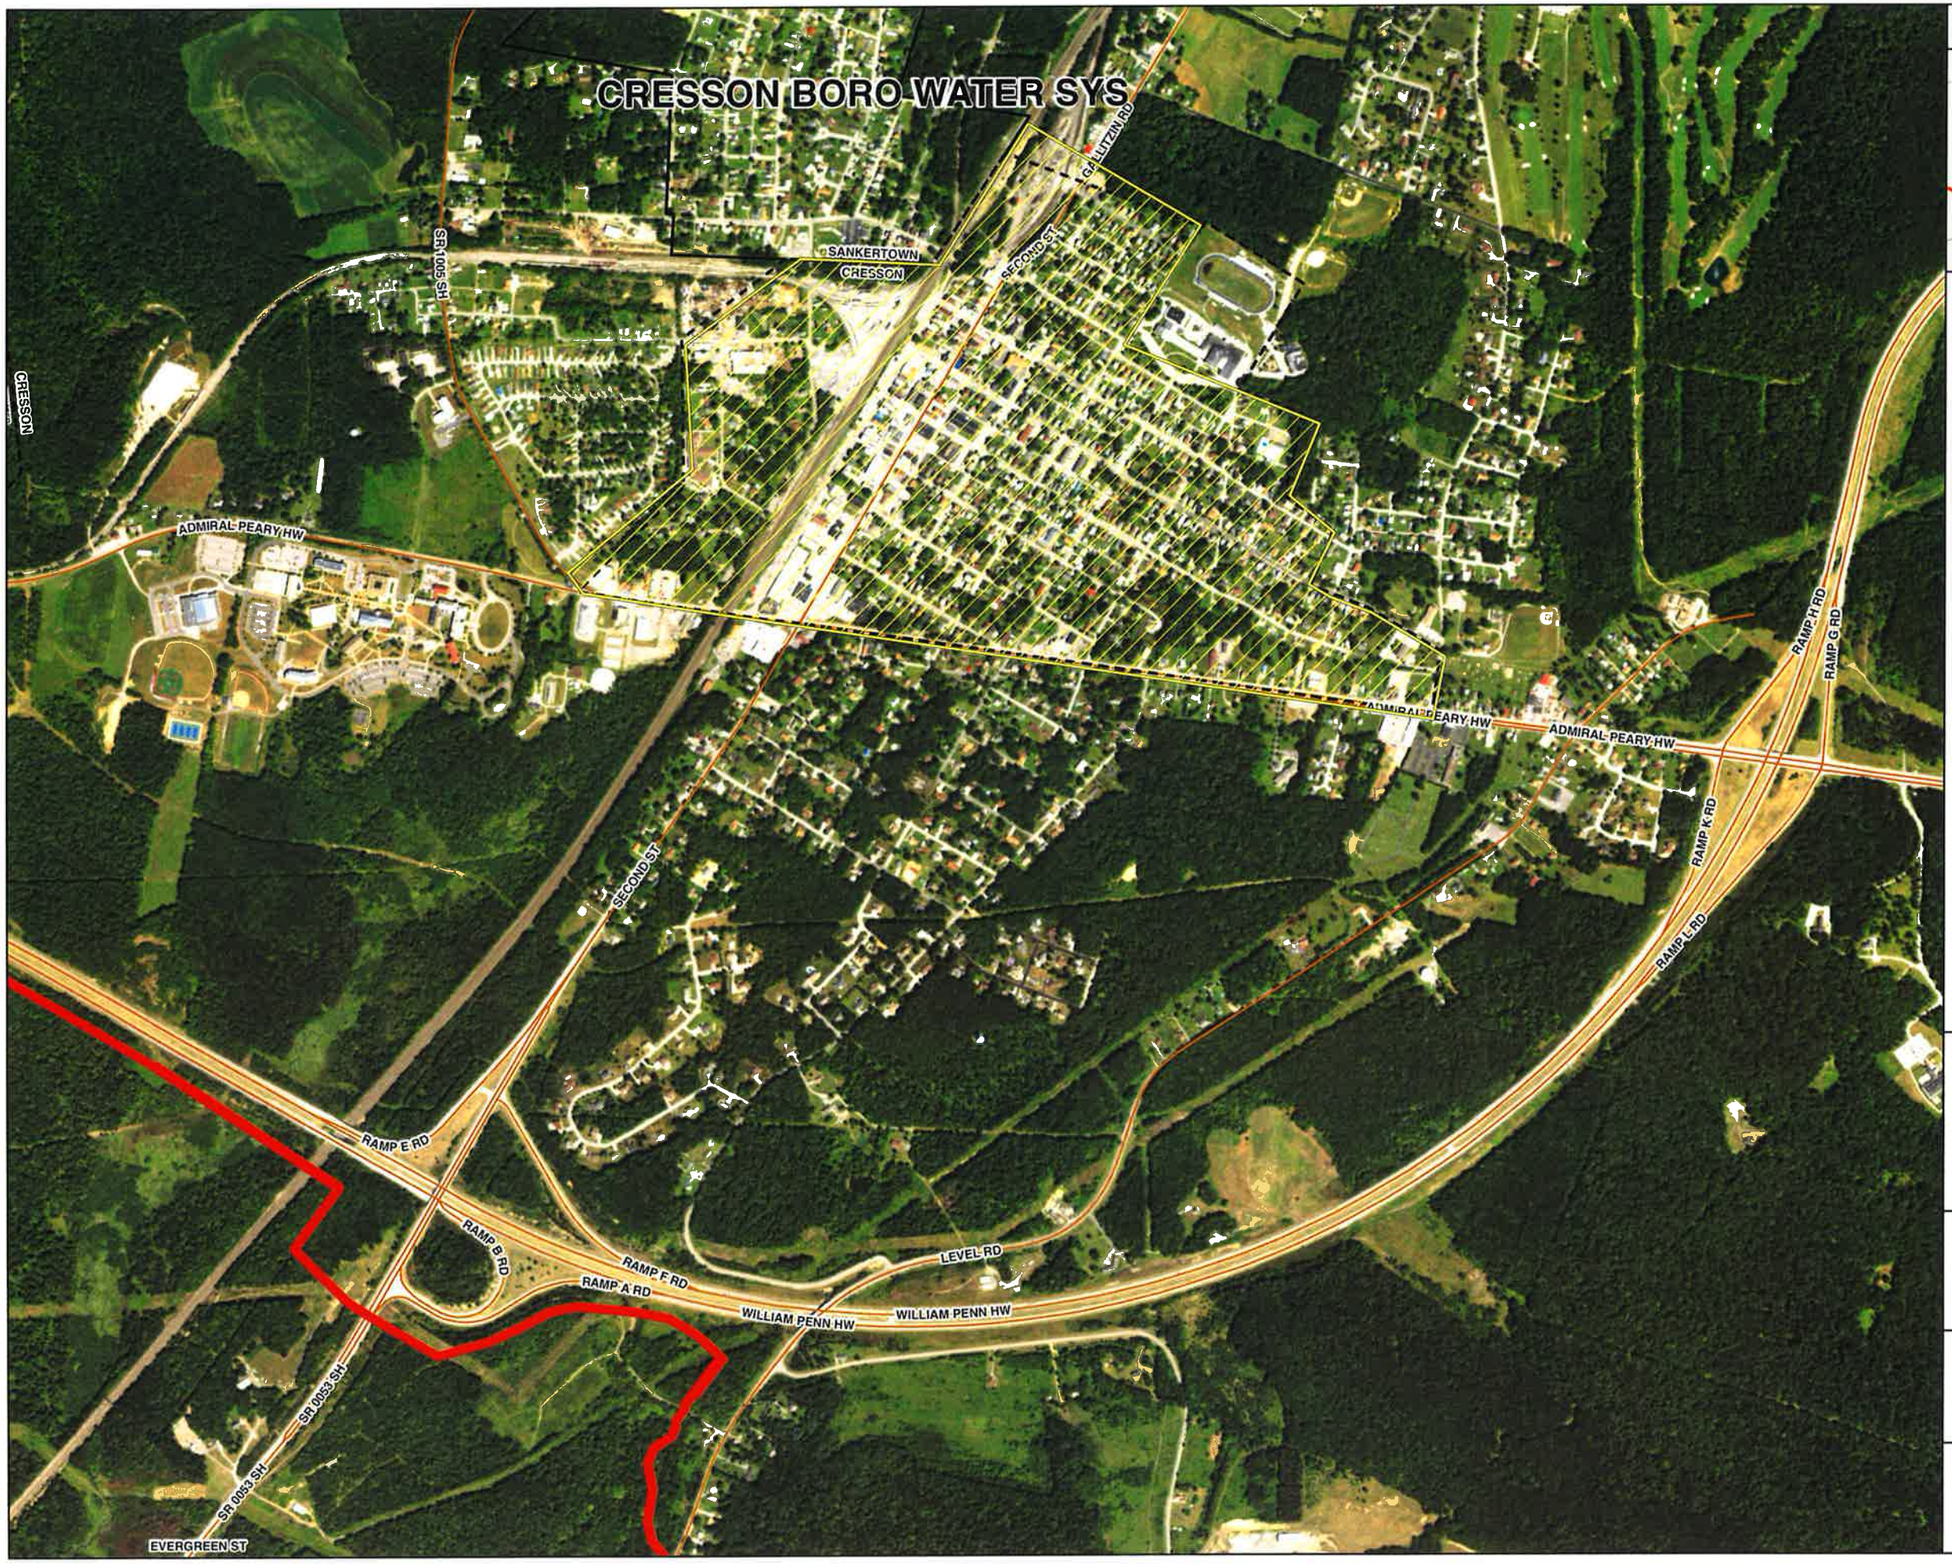

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Cresson Twp Muni Auth	Telephone: 814-886-2793
Contact name:	Veronica Harkins	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Veronica Harkins at Cresson Twp Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:27 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275606123 Delivered

Your package has been delivered

Tracking # 777275606123

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 10:20 am

Veronica Harkins
Cresson Twp. Muni. Authority
730 Portage Road
CRESSON, PA 16630
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275606123
Status:	Delivered: 09/21/2016 10:20 AM Signed for By: B.STRITTMATTER
Reference:	112IC05958, 16
Signed for by:	B.STRITTMATTER
Delivery location:	CRESSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:26 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

CRESSON TWP MUNICIPAL AUTHORITY

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Croyle Twp Water Auth	Telephone: 814-495-9009
Contact name:	Fred Meier	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Fred Meier at Croyle Twp Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 23, 2016.

Missed call received from POC on 9/21. Return message was left on 9/21/16 for POC.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

From: auto-reply@usps.com
To: Grosse, Nate
Subject: USPS Item Delivered, PO Box for Shipment 9505516150686291025187
Date: Wednesday, October 19, 2016 10:06:51 AM

Tracking Number: 9505516150686291025187

Hello Nate Grosse,

Thank you for using USPS.com.

This is a post-only message. Please do not respond.

Nate Grosse has requested that you receive a USPS Tracking® delivery or delivery attempt update, as shown below.

USPS Tracking® e-mail update information provided by the U.S. Postal Service.

Tracking Number: 9505516150686291025187

Updated Delivery Date: October 19, 2016

Service Type: USPS Tracking®

Shipment Activity	Location	Date & Time	Shipping Partner
Delivered, PO Box	SUMMERHILL, PA 15958	October 19, 2016 8:36 am	
Available for Pickup	SUMMERHILL, PA 15958	October 19, 2016 8:35 am	
Arrived at Post Office	SUMMERHILL, PA 15958	October 19, 2016 8:32 am	
Departed USPS Facility	WARRENDALE, PA 15086	October 18, 2016	

		4:13 pm
Arrived at USPS Facility	WARRENDALE, PA 15086	October 18, 2016 8:57 am
Departed USPS Facility	ROCHESTER, NY 14606	October 18, 2016 4:00 am
Arrived at USPS Origin Facility	ROCHESTER, NY 14606	October 17, 2016 10:08 pm
Departed Post Office	BUFFALO, NY 14203	October 17, 2016 7:33 pm
Acceptance	BUFFALO, NY 14203	October 17, 2016 1:40 pm

Reminder: USPS Tracking® by email

Date of email request: October 19, 2016

Future activity will continue to be emailed for up to 2 weeks from the Date of Request shown above. If you need to initiate the USPS Tracking® by email process again at the end of the 2 weeks, please do so at the USPS Tracking® site at http://www.usps.com/shipping/uspstrackingfaqs.htm

Results provided by the U.S. Postal Service.

Want to Track on the go?
You can track your packages using USPS Text Tracking™ by texting your tracking number to 28777 (2USPS™) or selecting the Text Update option on our USPS Tracking® site. Standard Message and Data Rates may apply.
For more information go to https://www.usps.com/text-tracking/welcome.htm

Download USPS Mobile®




USPS.com| Privacy Policy| Customer Service| FAQs










This is an automated email please do not reply to this message. This message is for the designated recipient only and may contain privileged, proprietary, or otherwise private information. If you have received it in error, please delete. Any other use of the email by you is prohibited.

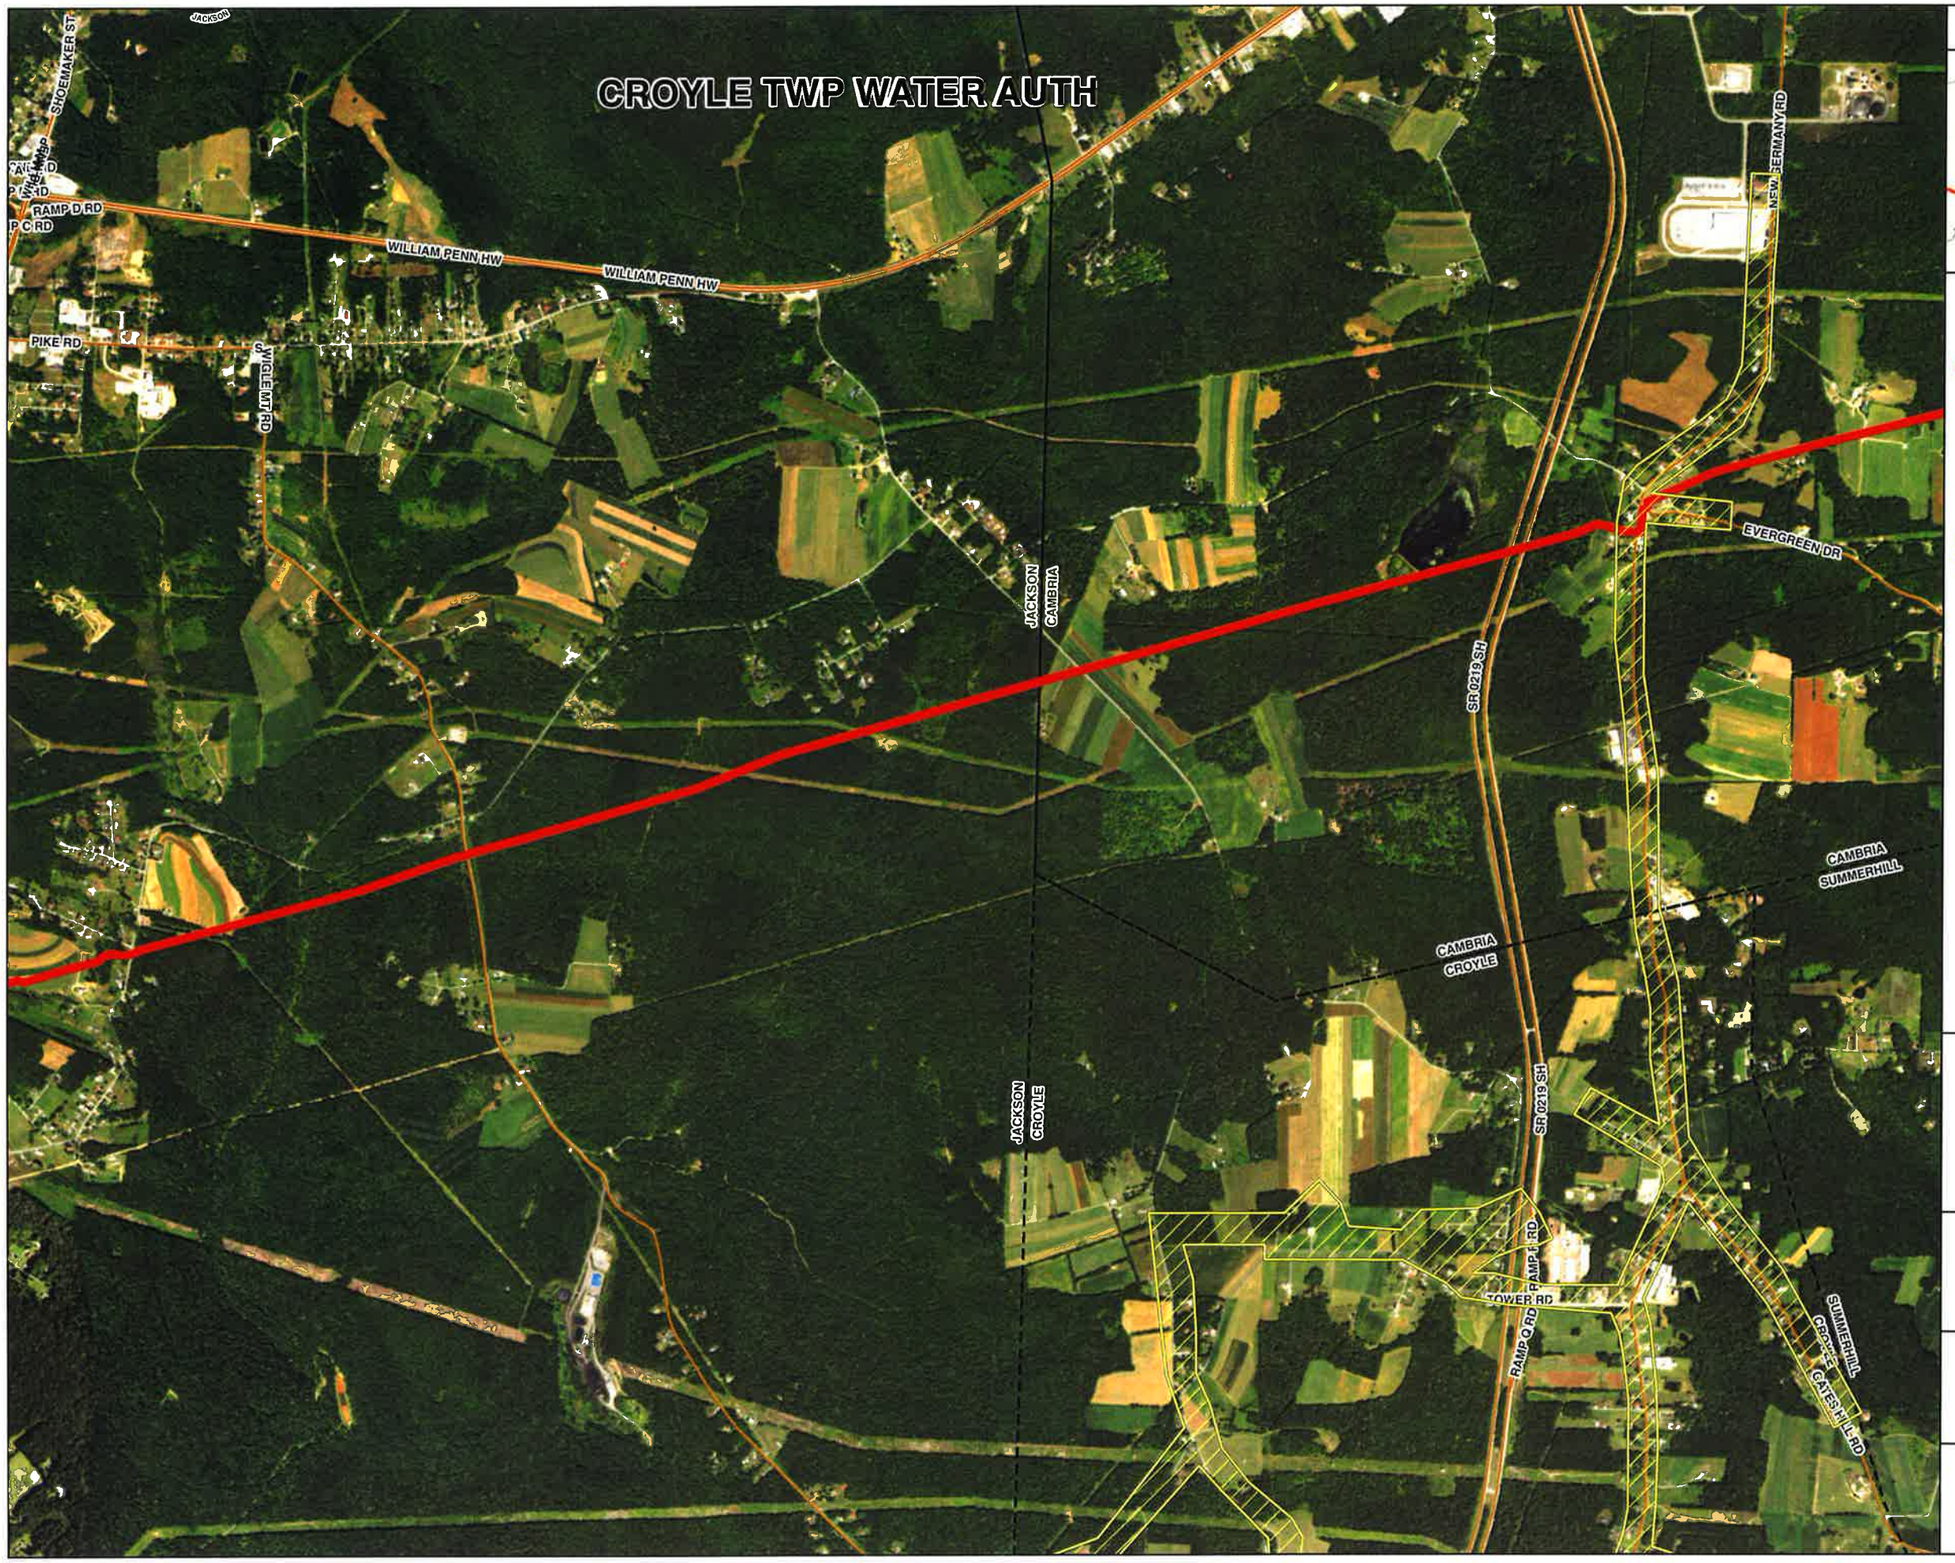

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Culhanes Steak House	Telephone: 717-938-0930
Contact name:	Tom Sagonas	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Tom Sagonas at Culhanes Steak House on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:22 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206975058 Delivered

Your package has been delivered

Tracking # 778206975058

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:17 am

c/o Tom Sagonas
Culhanes Steak House
1 Laurel Rd
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206975058
Status:	Delivered: 01/19/2017 10:17 AM Signed for By: M.SAGONAS
Reference:	112IC05958, 16
Signed for by:	M.SAGONAS
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:22 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CULHANES STEAK HOUSE
c/o Tom Sagonas
1 Laurel Rd
New Cumberland, PA 17070

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Cushion Peak Rod & Gun Club Telephone: 610-670-9558
Contact name:	Beverly Ansley / Lee Balkman
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Beverly Ansley at Cushion Peak Rod & Gun Club on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017. Additionally, Lee Balkman (President of Cushion Peak Rod & Gun Club) called on January 20, 2017 and explained that the process was already addressed in 2016 with Sunoco and there were no issues/concerns.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:46 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204803329 Delivered

Your package has been delivered

Tracking # 778204803329

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 11:41 am

c/o Beverly Ansley
Cushion Peak Rod & Gun Club
180 Vinemont Rd
REINHOLDS, PA 17569
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204803329
Status:	Delivered: 01/19/2017 11:41 AM Signed for By: M.GRUBB
Reference:	112IC05958, 16
Signed for by:	M.GRUBB
Delivery location:	REINHOLDS, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:46 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

CUSHION PEAK ROD & GUN CLUB
c/o Beverly Ansley
180 Vinemont Rd
Reinholds, PA 17569

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Devereux Foundation Brandywine	Telephone: 610-942-5900
Contact name:	Scott Carter	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Scott Carter at Devereux Foundation Brandywine on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:41 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275625015 Delivered

Your package has been delivered

Tracking # 777275625015

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 1:38 pm

Scott Carter
Devereux Foundation Brandywine
160 Devereux Road
GLENMOORE, PA 19343
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275625015
Status:	Delivered: 09/21/2016 1:38 PM Signed for By: D.DRUMHELLER
Reference:	112IC05958, 16
Signed for by:	D.DRUMHELLER
Delivery location:	GLENMOORE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:40 PM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Dogwood Acres Rec Area	Telephone: 717-766-5203
Contact name:	Charles Strub	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Charles Strub at Dogwood Acres Rec Area on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Dogwood Acres Rec Area called Josh Baird on January 19, 2017 requesting further mapping.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 2:10 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206037269 Delivered

Your package has been delivered

Tracking # 778206037269

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 2:05 pm

c/o Charles Strub
Dogwood Acres Rec Area
4500 Enola Road
NEWVILLE, PA 17241
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206037269
Status:	Delivered: 01/19/2017 2:05 PM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	NEWVILLE, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:09 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

DOGWOOD ACRES REC AREA
c/o Charles Strub
4500 Enola Road
Newville, PA 17241

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Duncansville Muni Water Auth	Telephone: 814-695-1497
Contact name:	Robert Hazenstab	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Robert Hazenstab at Duncansville Muni Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:53 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275643367 Delivered

Your package has been delivered

Tracking # 777275643367

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 1:46 pm

Robert Hazenstab
Duncansville Muni Water Authority
1146 Third Avenue
DUNCANSVILLE, PA 16635
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275643367
Status:	Delivered: 09/21/2016 1:46 PM Signed for By: P.FOX
Reference:	112IC05958, 16
Signed for by:	P.FOX
Delivery location:	DUNCANSVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:52 PM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

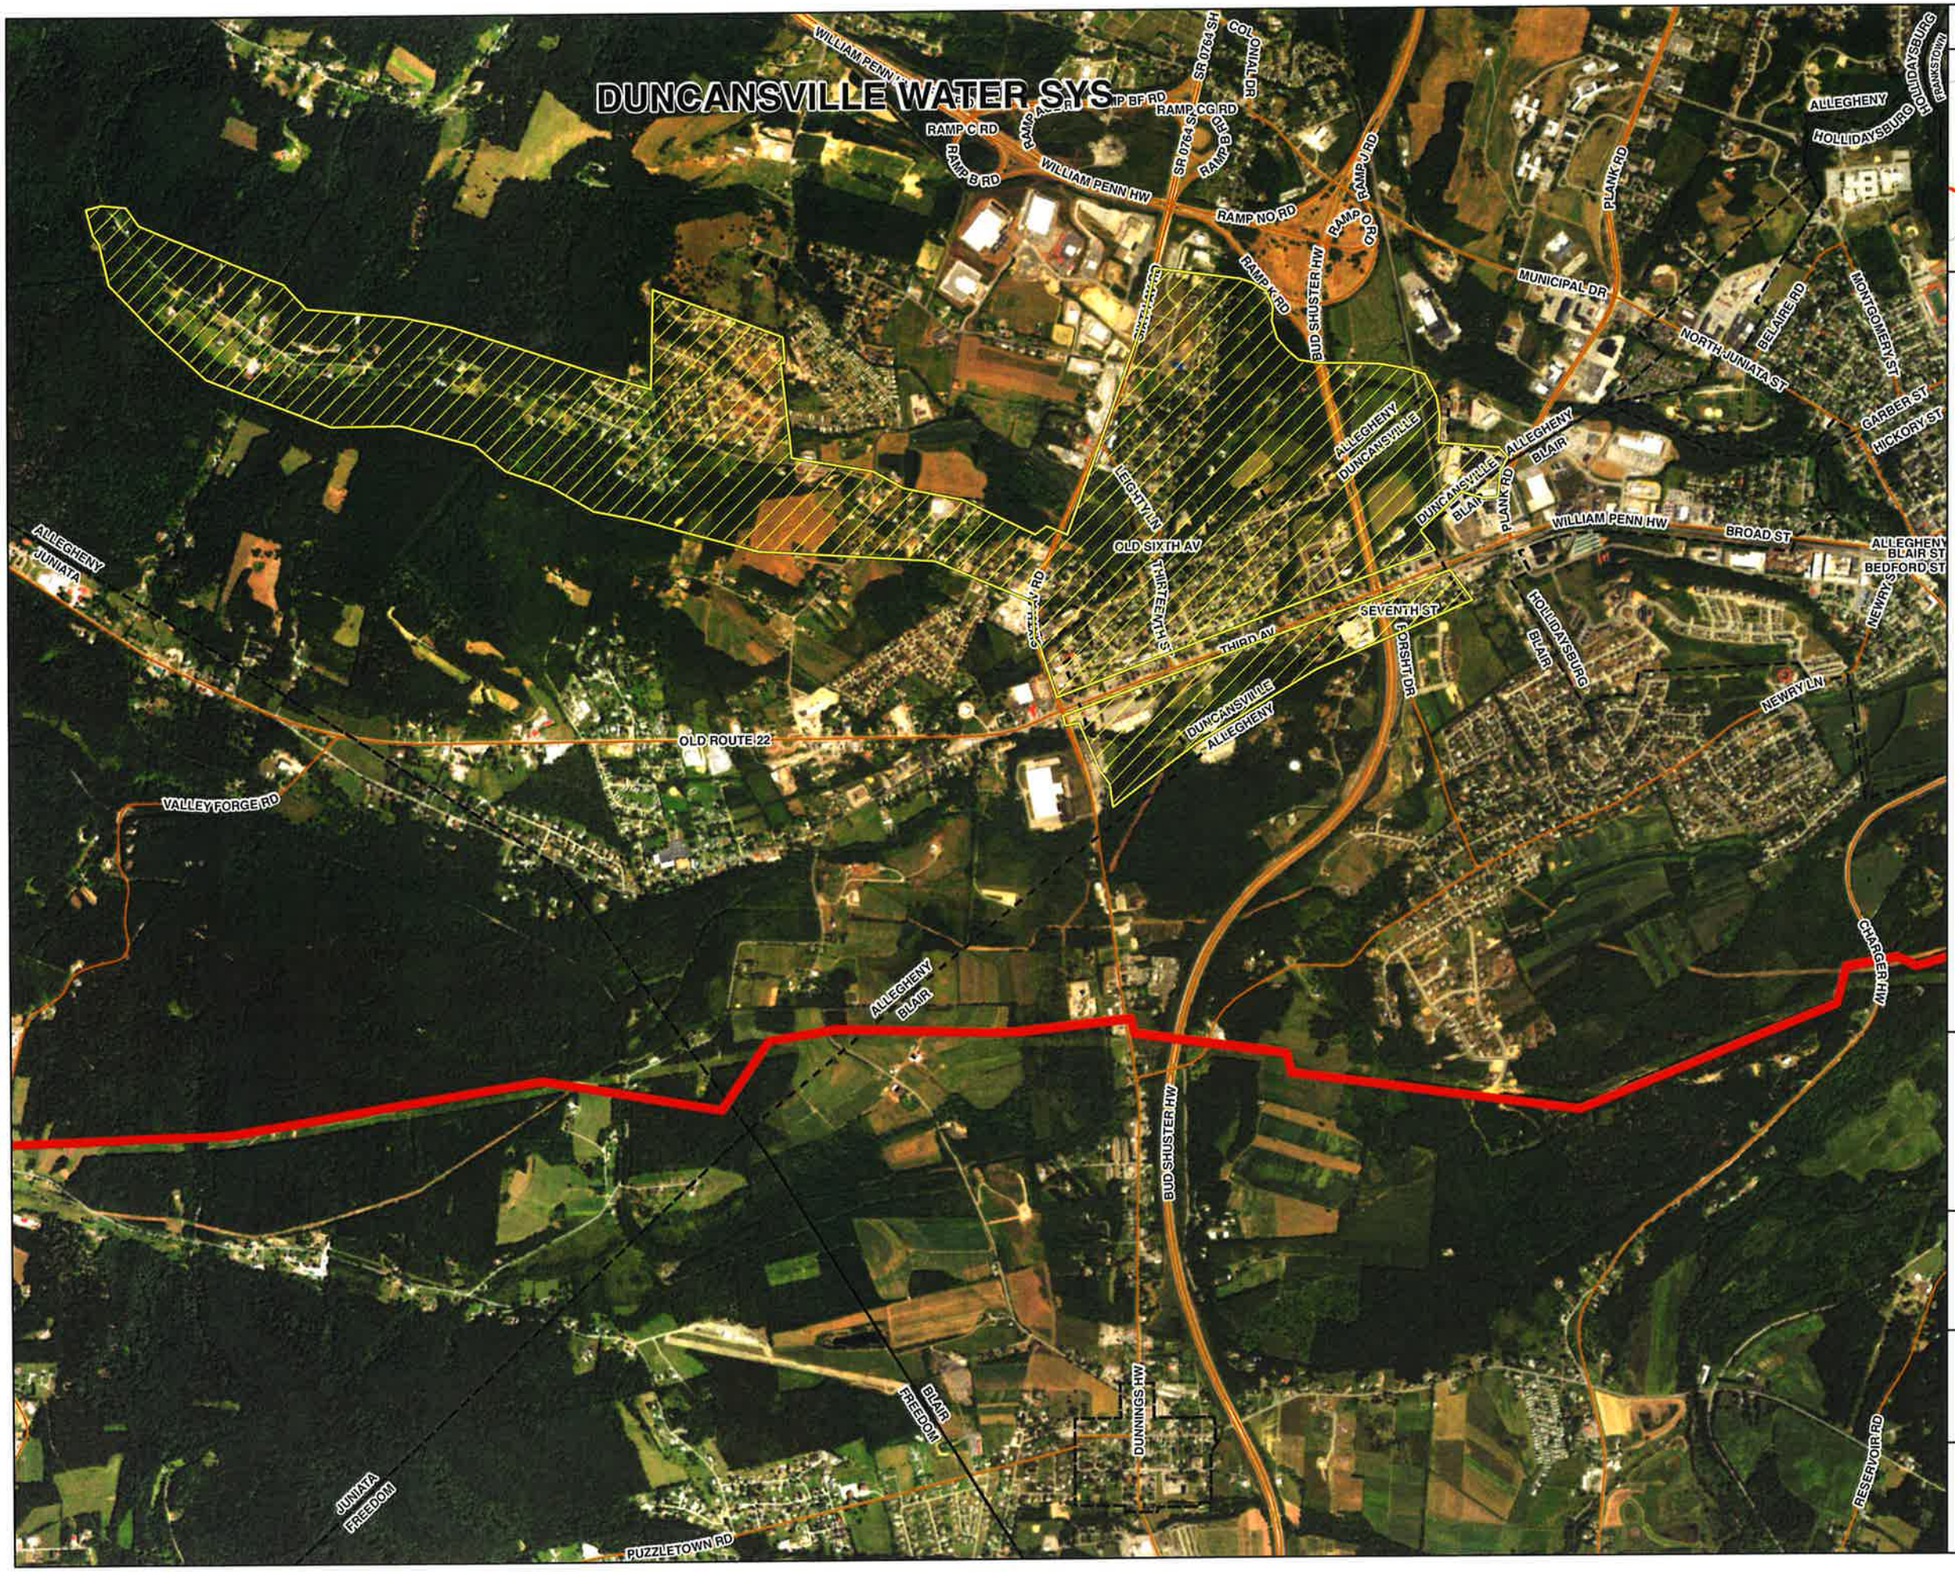

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Econolodge Telephone: 717-766-4728
Contact name:	Shirish Patel
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Shirish Patel at Econolodge on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:15 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206060039 Delivered

Your package has been delivered

Tracking # 778206060039

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:10 am

c/o Shirish Patel
Econolodge
650 Gettysburg Rd
MECHANICSBURG, PA 17055
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206060039
Status:	Delivered: 01/19/2017 09:10 AM Signed for By: S.PATEL
Reference:	112IC05958, 16
Signed for by:	S.PATEL
Delivery location:	MECHANICSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:15 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ECONOLODGE
c/o Shirish Patel
650 Gettysburg Rd
Mechanicsburg, PA 17055

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Ebensburg Boro Muni Auth	Telephone: 814-472-8780
Contact name:	Daniel L. Penatzer	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Daniel L. Penatzer at Ebensburg Boro Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 9/21/16 stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:01 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275662671 Delivered

Your package has been delivered

Tracking # 777275662671

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 12:56 pm

Daniel L. Penatzer, Mgr.
Ebensburg Boro Muni Authority
300 W High Street
EBENSBURG, PA 15931
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275662671
Status:	Delivered: 09/21/2016 12:56 PM Signed for By: R.MYERS
Reference:	112IC05958, 16
Signed for by:	R.MYERS
Delivery location:	EBENSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:00 PM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Elverson Water Company	Telephone: 610-286-5115
Contact name:	Merel Stolzfus	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Merel Stolzfus at Elverson Water Company on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 9/30/16 stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 12:45 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470871848 Delivered

Your package has been delivered

Tracking # 777470871848

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Mon, 10/17/2016 12:40 pm

Elverson Water Company
26 E. Main Street
ELVERSON, PA 19520
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470871848
Status:	Delivered: 10/17/2016 12:40 PM Signed for By: D.SLYE
Reference:	112IC05958, 16
Signed for by:	D.SLYE
Delivery location:	ELVERSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	10/17/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:45 AM CDT on 10/17/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Fairview Elem Sch	Telephone: 717-938-9577
Contact name:	Russell Barnell	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Russell Barnell at Fairview Elem Sch on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:27 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206989801 Delivered

Your package has been delivered

Tracking # 778206989801

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:21 am

c/o Russel Burnell
Fairview Elem School
507 Fishing Creek Road
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206989801
Status:	Delivered: 01/19/2017 10:21 AM Signed for By: D.JONES
Reference:	112IC05958, 16
Signed for by:	D.JONES
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:26 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

FAIRVIEW ELEM SCH
c/o Russel Burnell
507 Fishing Creek Road
New Cumberland, PA 17070

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Fairview GC Telephone: 717-867-4403
Contact name:	Jim Jones
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Jim Jones at Fairview GC on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:53 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206708467 Delivered

Your package has been delivered

Tracking # 778206708467

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:50 am

c/o Jim Jones
Fairview Gc
2399 Quentin Rd
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206708467
Status:	Delivered: 01/19/2017 09:50 AM Signed for By: J.JONES
Reference:	112IC05958, 16
Signed for by:	J.JONES
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:53 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

FAIRVIEW GC
c/o Jim Jones
2399 Quentin Rd
Lebanon, PA 17042

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Fairview Twp Bldg	Telephone: 717-901-5261
Contact name:	Steve Smith	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Steve Smith at Fairview Twp Bldg on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:02 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778207013029 Delivered

Your package has been delivered

Tracking # 778207013029

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:58 am

c/o Steve Smith
Fairview Twp Bldg
599 Lewisberry Road
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778207013029
Status:	Delivered: 01/19/2017 09:58 AM Signed for By: J.GIBB
Reference:	112IC05958, 16
Signed for by:	J.GIBB
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:02 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

FAIRVIEW TWP BLDG
c/o Steve Smith
599 Lewisberry Road
New Cumberland, PA 17070

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Fowlers Hollow St Park	Telephone: 717-776-5272
Contact name:	Col Dennigh St Pk	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Col Dennigh St Pk at Fowlers Hollow St Park on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 2:22 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206778544 Delivered

Your package has been delivered

Tracking # 778206778544

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 2:16 pm

c/o Col Denning St Pk
Fowlers Hollow St Park
1599 Doubling Gap Rd
NEWVILLE, PA 17241
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206778544
Status:	Delivered: 01/19/2017 2:16 PM Signed for By: J.JOHNS
Reference:	112IC05958, 16
Signed for by:	J.JOHNS
Delivery location:	NEWVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:22 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

FOWLERS HOLLOW ST PARK
c/o Col Denning St Pk
1599 Doubling Gap Rd
Newville, PA 17241

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Freedom Twp Water & Sewer	Telephone: 814-695-8051
Contact name:	Susahn Claycomb	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Susahn Claycomb at Freedom Twp Water & Sewer on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:09 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275681129 Delivered

Your package has been delivered

Tracking # 777275681129

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 11:07 am

Susahn Claycomb
Freedom Twp. Water & Sewer
131 Municipal Street
EAST FREEDOM, PA 16637
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275681129
Status:	Delivered: 09/21/2016 11:07 AM Signed for By: S.CLAYCOMB
Reference:	112IC05958, 16
Signed for by:	S.CLAYCOMB
Delivery location:	EAST FREEDOM, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:09 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

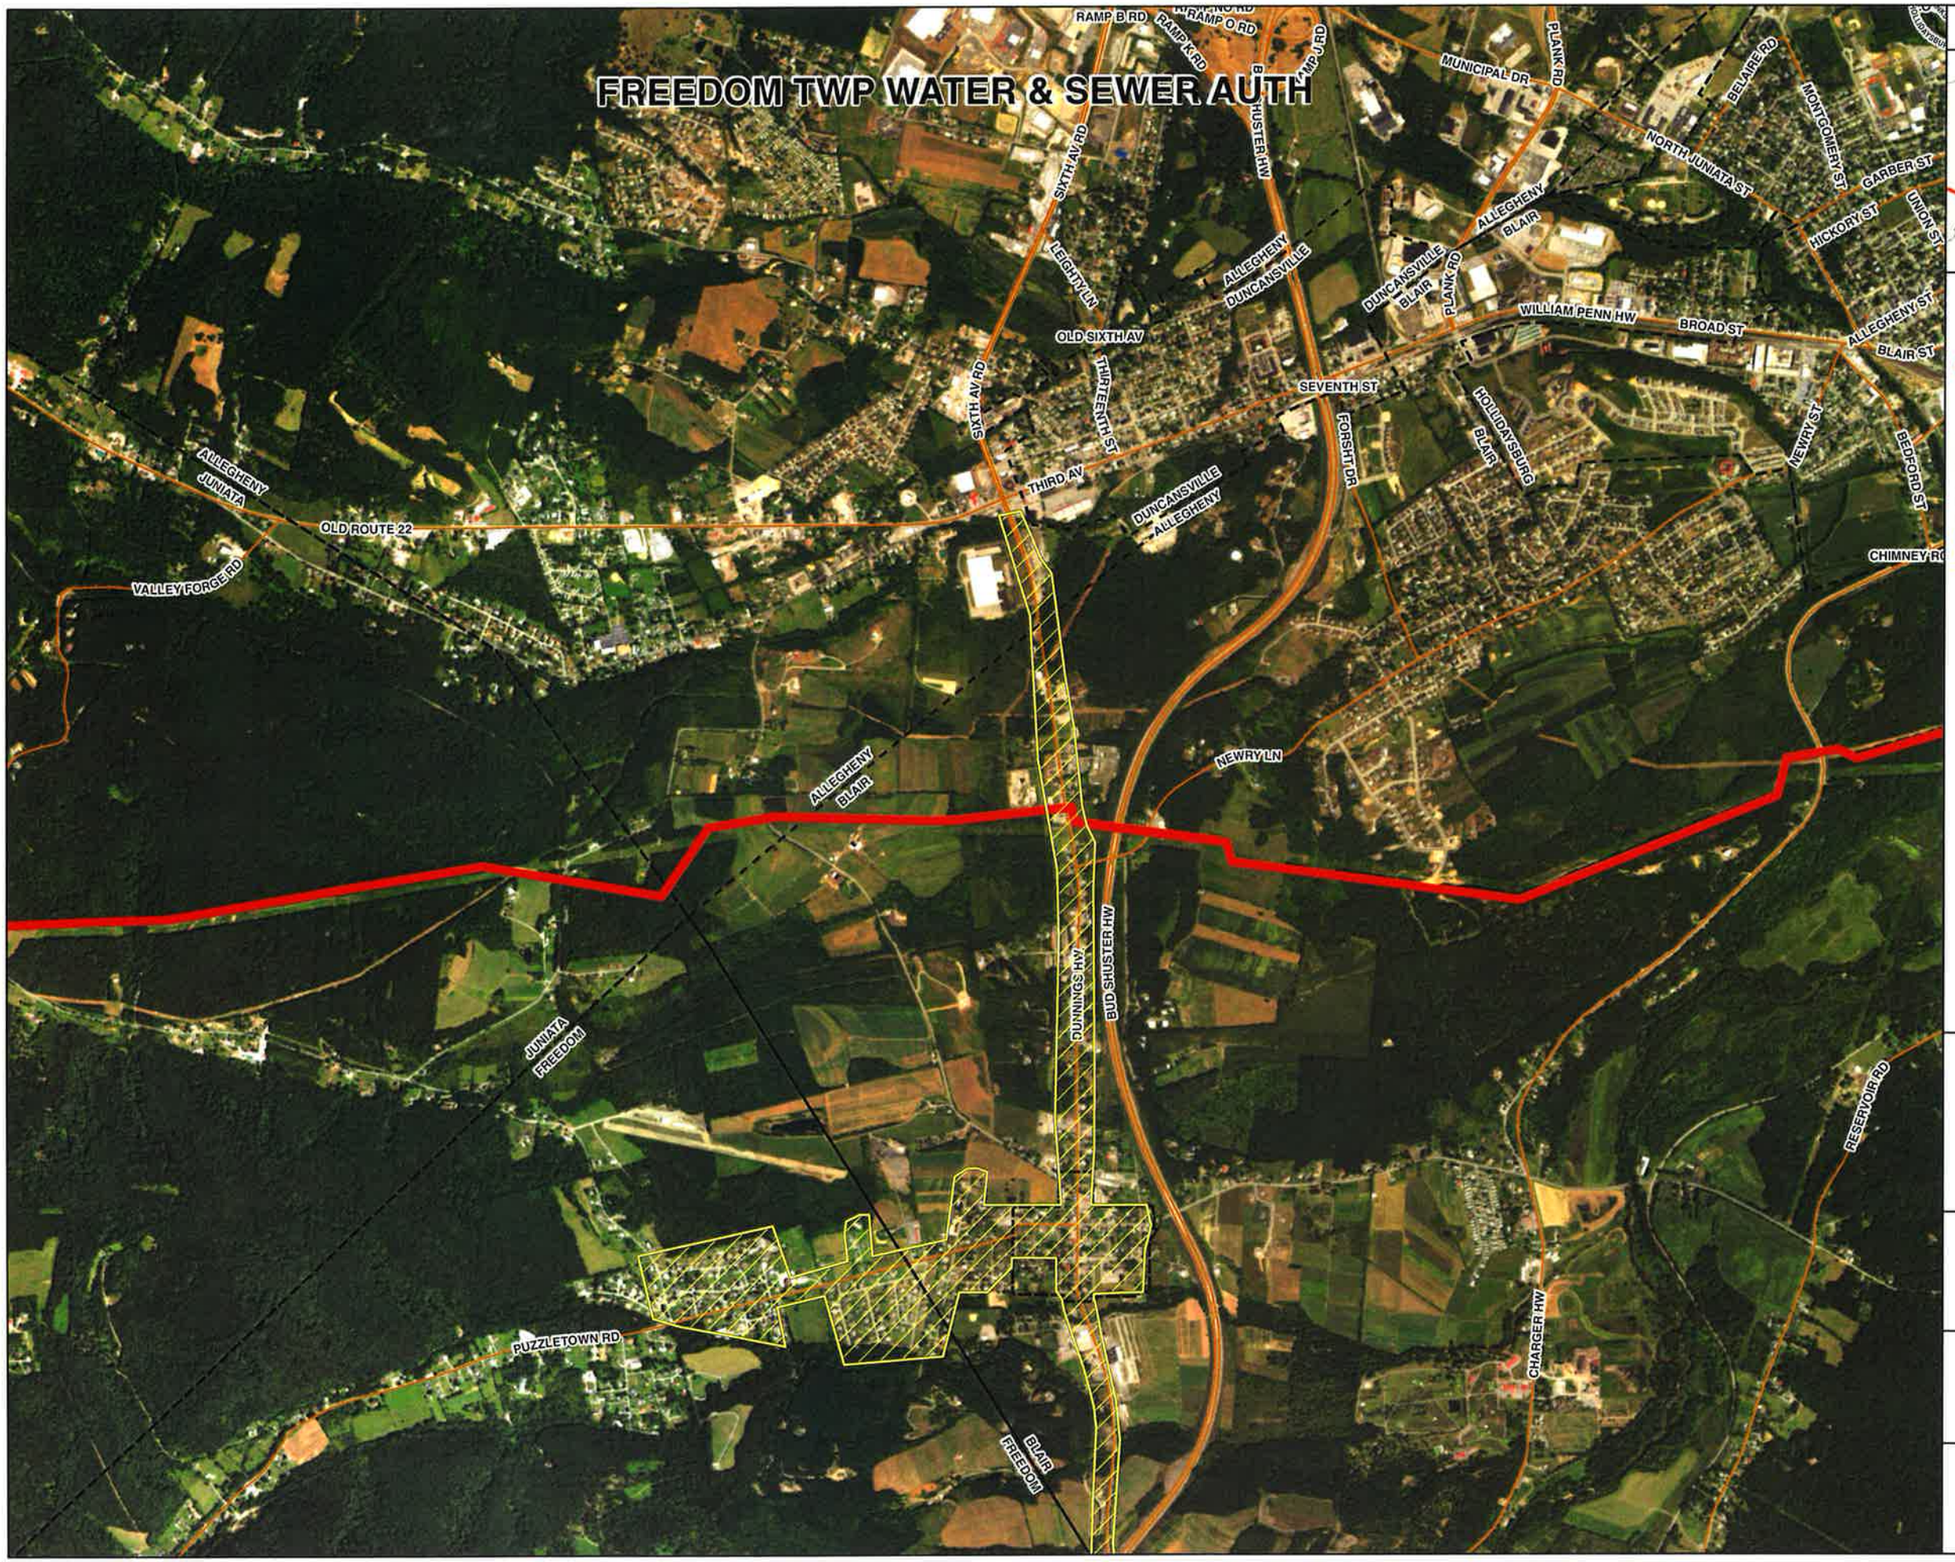

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Galen Hall CC Inc Telephone: 610-678-8011
Contact name:	Brian Stiefel
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Brian Stiefel at Galen Hall CC Inc on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 23, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7250

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

WERNERSVILLE, PA 19565

OFFICIAL USE

Certified Mail Fee	$3.30
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
Total Postage and Fees	$4.87

Postmark Here

01/19/2017

Sent To
GALEN HALL CC INC.

Street and Ap
c/o BRIAN STIEFEL

City, State, Zi
P.O. BOX 127
WERNERSVILLE, PA 19565

PS Form 38

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237750

On Time
Updated Delivery Day: Monday, January 23, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 23, 2017 , 8:53 am	**Delivered**	**WERNERSVILLE, PA 19565**
Your item was delivered at 8:53 am on January 23, 2017 in WERNERSVILLE, PA 19565.		
January 23, 2017 , 7:00 am	Available for Pickup	WERNERSVILLE, PA 19565
January 23, 2017 , 6:57 am	Arrived at Unit	WERNERSVILLE, PA 19565
January 23, 2017 , 1:08 am	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:53 am	In Transit to Destination	
January 21, 2017 , 8:53 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

GALEN HALL CC INC
c/o Brian Stiefel
P.O. Box 127
Wernersville, PA 19565

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Geesytown Vol Fire Co Telephone: 814-695-8003
Contact name:	Claude M Walls
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Claude M Walls at Geesytown Vol Fire Co on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:29 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205848489 Delivered

Your package has been delivered

Tracking # 778205848489

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 11:24 am

c/o Claude M Walls
Geeseytown Vol Fire Co
215 Mary St.
HOLLIDAYSBURG, PA 16648
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205848489
Status:	Delivered: 01/19/2017 11:24 AM Signed for By: Signature Release on file
Reference:	112IC05958, 16
Signed for by:	Signature Release on file
Delivery location:	HOLLIDAYSBURG, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:28 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

GEESEYTOWN VOL FIRE CO
c/o Claude M Walls
215 Mary St.
Hollidaysburg, PA 16648

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Gouglersville Fire Company Telephone: 610-777-2449
Contact name:	Ron Heffner - President
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Ron Heffner at Gouglersville Fire Company on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:33 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204833262 Delivered

Your package has been delivered

Tracking # 778204833262

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:28 am

c/o Ron Heffner, President
Gouglersville Fire Co
475 Mohns Hill Road
READING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204833262
Status:	Delivered: 01/19/2017 10:28 AM Signed for By: V.WALLACE
Reference:	112IC05958, 16
Signed for by:	V.WALLACE
Delivery location:	READING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:33 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

GOUGLERSVILLE FIRE CO
c/o Ron Heffner, President
475 Mohns Hill Road
Reading, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Gov Mifflin Brecknock Elem Sch Telephone: 610-775-5079
Contact name:	Mark Naylon
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Mark Naylon at Gov Mifflin Brecknock Elem Sch on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:17 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204862453 Delivered

Your package has been delivered

Tracking # 778204862453

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:09 am

c/o Mark Naylon
Gov Mifflin Brecknock Elem Sch
10 S. Waverly St
SHILLINGTON, PA 19607
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204862453
Status:	Delivered: 01/19/2017 10:09 AM Signed for By: M.TIM
Reference:	112IC05958, 16
Signed for by:	M.TIM
Delivery location:	SHILLINGTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:17 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

GOV MIFFLIN BRECKNOCK ELEM SCH
c/o Mark Naylon
10 S Waverly St
Shillington, PA 19607

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Grace Brethren Retreat Center	Telephone: 717-336-2541
Contact name:	Mike Gehlert	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Mike Gehlert at Grace Brethren Retreat Center on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:33 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206621347 Delivered

Your package has been delivered

Tracking # 778206621347

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:27 am

c/o Mike Gehlert
Grace Brethren Retreat Center
480 Forest Rd
DENVER, PA 17517
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206621347
Status:	Delivered: 01/19/2017 10:27 AM Signed for By: D.MILLER
Reference:	112IC05958, 16
Signed for by:	D.MILLER
Delivery location:	DENVER, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:32 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

GRACE BRETHREN RETREAT CENTER
c/o Mike Gehlert
480 Forest Rd
Denver, PA 17517

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Gradyville Foods Country Deli	Telephone: 610-558-3354
Contact name:	Donald Butler	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Donald Butler at Gradyville Foods Country Deli on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7835

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

GRADYVILLE PA 19039

OFFICIAL USE

Certified Mail Fee $3.30 — 0205 21

Extra Services & Fees *(check box, add fee as appropriate)*
- ☐ Return Receipt (hardcopy) $ $0.00
- ☐ Return Receipt (electronic) $ $0.00
- ☐ Certified Mail Restricted Delivery $ $0.00
- ☐ Adult Signature Required $ $0.00
- ☐ Adult Signature Restricted Delivery $

Postage $1.36

Total Postage and Fees $4.66

Postmark Here

01/19/2017

Sent To
Street and Apt. N
City, State, ZIP+

GRADYVILLE FOODS COUNTRY DELI
c/o DONALD BUTLER
P.O. BOX 209
GRADYVILLE, PA 19037

PS Form 3800

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237835

Expected Delivery Day: Monday, January 23, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 23, 2017 , 3:10 pm	**Delivered**	**GRADYVILLE, PA 19039**
Your item was delivered at 3:10 pm on January 23, 2017 in GRADYVILLE, PA 19039.		
January 22, 2017 , 9:03 am	In Transit to Destination	
January 21, 2017 , 2:03 am	Departed USPS Destination Facility	PHILADELPHIA, PA 19176
January 20, 2017 , 1:45 pm	Arrived at USPS Destination Facility	PHILADELPHIA, PA 19176
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:50 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

HELPFUL LINKS
Contact Us
Site Index
FAQs

ON ABOUT.USPS.COM
About USPS Home
Newsroom
USPS Service Updates
Forms & Publications
Government Services
Careers

OTHER USPS SITES
Business Customer Gateway
Postal Inspectors
Inspector General
Postal Explorer
National Postal Museum
Resources for Developers

LEGAL INFORMATION
Privacy Policy
Terms of Use
FOIA
No FEAR Act EEO Data

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

January 18th, 2017

GRADYVILLE FOODS COUNTRY DELI
c/o Donald Butler
Po Box 209
Gradyville, PA 19037

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Greendown Acres Mhp	Telephone: 814-695-1464
Contact name:	David Reynolds	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to David Reynolds at Greendown Acres Mhp on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 2:15 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470910996 Delivered

Your package has been delivered

Tracking # 777470910996

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Mon, 10/17/2016 12:09 pm

Greendown Acres Mobile Home Park
210 Allen Lane
CEDAREDGE, CO 81413
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470910996
Status:	Delivered: 10/17/2016 12:09 PM Signed for By: P.WIKKERSON
Reference:	112IC05958, 16
Signed for by:	P.WIKKERSON
Delivery location:	CEDAREDGE, CO
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	10/17/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:14 PM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

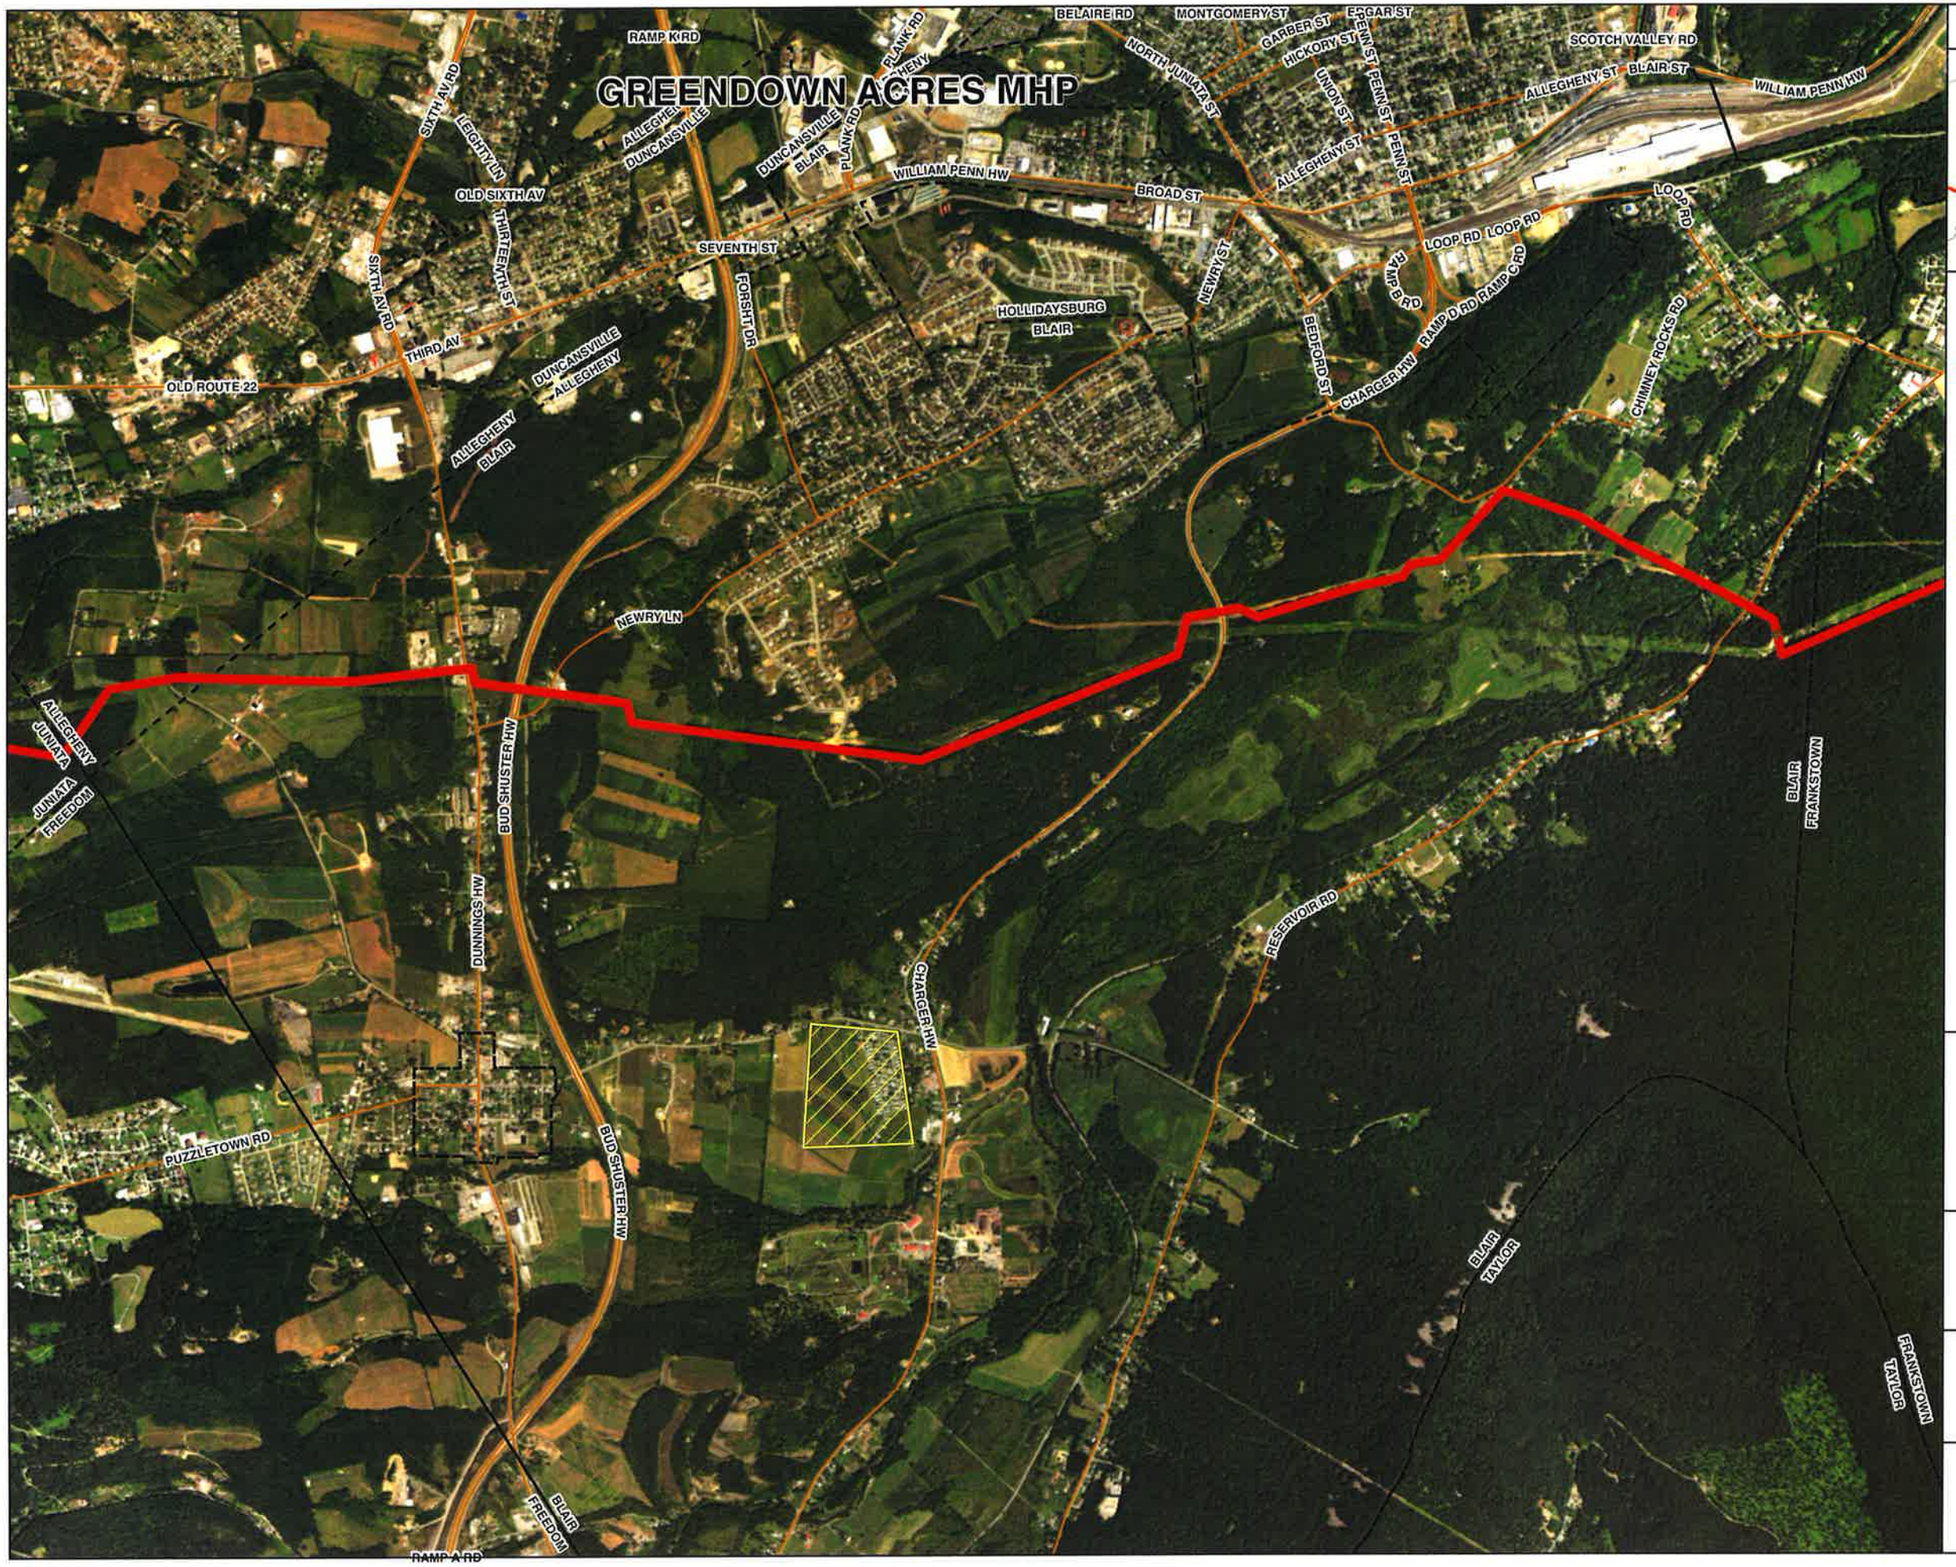

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Guy Shelly Amer Legion 974	Telephone: 717-774-3149
Contact name:	Ray Martz	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ray Martz at Guy Shelly Amer Legion 974on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:15 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778207029521 Delivered

Your package has been delivered

Tracking # 778207029521

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:10 am

c/o Ray Martz
Guy Shelly Amer Legion 974
352 March Run Rd
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778207029521
Status:	Delivered: 01/19/2017 09:10 AM Signed for By: G.MARTZ
Reference:	112IC05958, 16
Signed for by:	G.MARTZ
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:15 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

GUY SHELLY AMER LEGION 974
c/o Ray Martz
352 March Run Rd
New Cumberland, PA 17070

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Happy Trails Campground	Telephone: 814-458-3101
Contact name:	Greg Trail	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Greg Trail at Happy Trails Campground on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 20, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Friday, January 20, 2017 1:03 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206416607 Delivered

Your package has been delivered

Tracking # 778206416607

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Fri, 1/20/2017 12:57 pm

c/o Greg Trail
Happy Trails Campground
13682 Upper Corners Rd
HESSTON, PA 16647
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206416607
Status:	Delivered: 01/20/2017 12:57 PM Signed for By: G.TRAILS
Reference:	112IC05958, 16
Signed for by:	G.TRAILS
Delivery location:	HESSTON, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:02 PM CST on 01/20/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

HAPPY TRAILS CAMPGROUND
c/o Greg Trail
13682 Upper Corners Rd
Hesstonlle, PA 16647

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Harmony Estates Mhp	Telephone: 717-730-4141
Contact name:	Kim Losh Co	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Kim Losh Co at Harmony Estates Mhp on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivered on 9/21, and returned to sender on 9/30/16 due to inability to reach recipient for signature.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Friday, October 28, 2016 3:26 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777571134410 Delivered

Your package has been delivered

Tracking # 777571134410

Ship date:
Thu, 10/27/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Fri, 10/28/2016 3:24 pm

Harmony Estates Mobile Home Park
123 Gilpin Drive
WEST CHESTER, PA 19382
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777571134410
Status:	Delivered: 10/28/2016 3:24 PM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	WEST CHESTER, PA
Delivered to:	Residence
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	No Signature Required
	Deliver Weekday
	Residential Delivery
Standard transit:	10/28/2016 by 8:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 2:25 PM CDT on 10/28/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

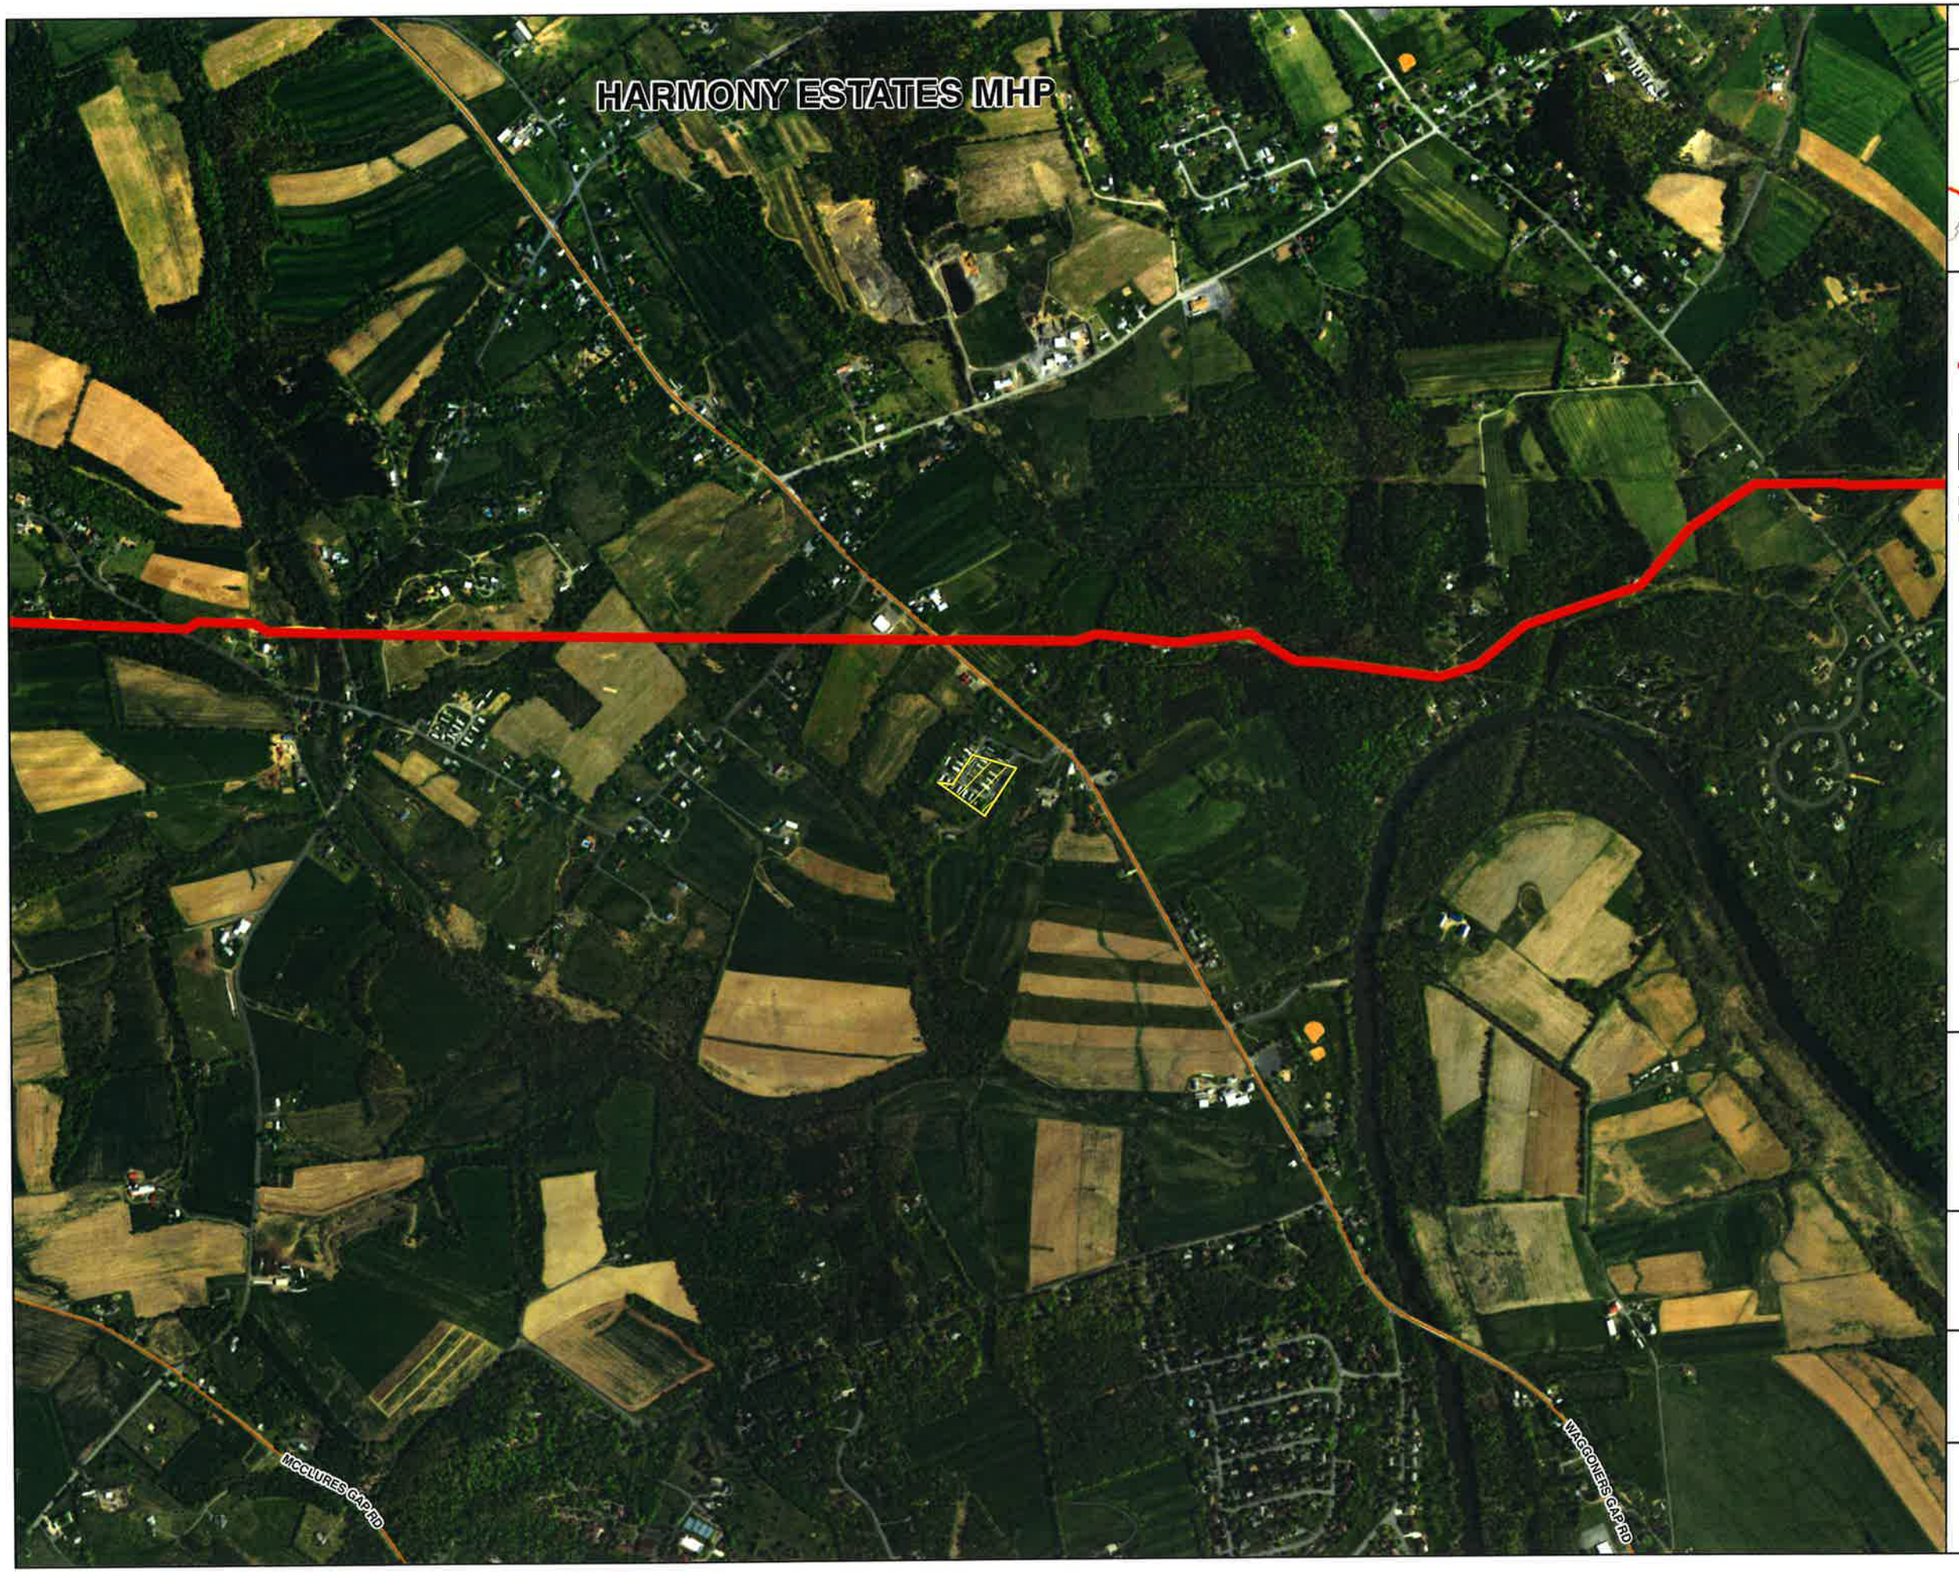

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Harrisburg Intl Airport	Telephone: 717-948-3900
Contact name:	Scott Snoke	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Scott Snoke at Harrisburg Intl Airport on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:10 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206161965 Delivered

Your package has been delivered

Tracking # 778206161965

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:04 am

c/o Scott Snoke
Harrisburg Intl Airport
One Terminal Drive, Suite 300
MIDDLETOWN, PA 17057
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206161965
Status:	Delivered: 01/19/2017 10:04 AM Signed for By: C.WALKER
Reference:	112IC05958, 16
Signed for by:	C.WALKER
Delivery location:	MIDDLETOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:09 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

HARRISBURG INTL AIRPORT
c/o Scott Snoke
One Terminal Drive, Suite 300
Middletown, PA 17057

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Heidelberg Twp Muni Auth	Telephone: 717-949-6977
Contact name:	Ed Hartman	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ed Hartman at Heidelberg Twp Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 22, 2016.

Received a phone call on 9/30/16 requesting the information via email. Email with information was sent on 10/3/16. A letter indicating no impact was received on 10/19/16.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

From: auto-reply@usps.com
To: Grosse, Nate
Subject: USPS Item Delivered, PO Box for Shipment 9505516150686291025163
Date: Wednesday, October 19, 2016 10:20:23 AM

Tracking Number: 9505516150686291025163

Hello Nate Grosse,

Thank you for using USPS.com.

This is a post-only message. Please do not respond.

Nate Grosse has requested that you receive a USPS Tracking® delivery or delivery attempt update, as shown below.

USPS Tracking® e-mail update information provided by the U.S. Postal Service.

Tracking Number: 9505516150686291025163

Updated Delivery Date: October 19, 2016

Service Type: USPS Tracking®

Shipment Activity	Location	Date & Time	Shipping Partner
Delivered, PO Box	SCHAEFFERSTOWN, PA 17088	October 19, 2016 8:48 am	
Arrived at Post Office	SCHAEFFERSTOWN, PA 17088	October 19, 2016 8:48 am	
Departed USPS Facility	HARRISBURG, PA 17107	October 19, 2016 5:19 am	
Arrived at USPS Facility	HARRISBURG, PA 17107	October 18, 2016	

		1:28 pm
Departed USPS Facility	ROCHESTER, NY 14606	October 18, 2016 7:40 am
Arrived at USPS Origin Facility	ROCHESTER, NY 14606	October 17, 2016 10:06 pm
Departed Post Office	BUFFALO, NY 14203	October 17, 2016 7:33 pm
Acceptance	BUFFALO, NY 14203	October 17, 2016 1:39 pm

Reminder: USPS Tracking® by email

Date of email request: October 19, 2016

Future activity will continue to be emailed for up to 2 weeks from the Date of Request shown above. If you need to initiate the USPS Tracking® by email process again at the end of the 2 weeks, please do so at the USPS Tracking® site at http://www.usps.com/shipping/uspstrackingfaqs.htm

Results provided by the U.S. Postal Service.

Want to Track on the go?
You can track your packages using USPS Text Tracking™ by texting your tracking number to 28777 (2USPS™) or selecting the Text Update option on our USPS Tracking® site. Standard Message and Data Rates may apply.
For more information go to https://www.usps.com/text-tracking/welcome.htm

Download USPS Mobile®

USPS.com| Privacy Policy| Customer Service| FAQs



This is an automated email please do not reply to this message. This message is for the designated recipient only and may contain privileged, proprietary, or otherwise private information. If you have received it in error, please delete. Any other use of the email by you is prohibited.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Highlands S & W Auth Beaverdam	Telephone: 814-266-3146
Contact name:	Edward J. Englehart	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Edward J. Englehart at Highlands S & W Auth Beaverdam on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 9/21/16 indicating source location, and stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:39 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275721880 Delivered

Your package has been delivered

Tracking # 777275721880

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 10:37 am

Edward J. Englehart, Mgr.
Highland S&W Auth - Beaverdam
120 Tank Drive
JOHNSTOWN, PA 15904
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275721880
Status:	Delivered: 09/21/2016 10:37 AM Signed for By: D.MORISA
Reference:	112IC05958, 16
Signed for by:	D.MORISA
Delivery location:	JOHNSTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:38 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

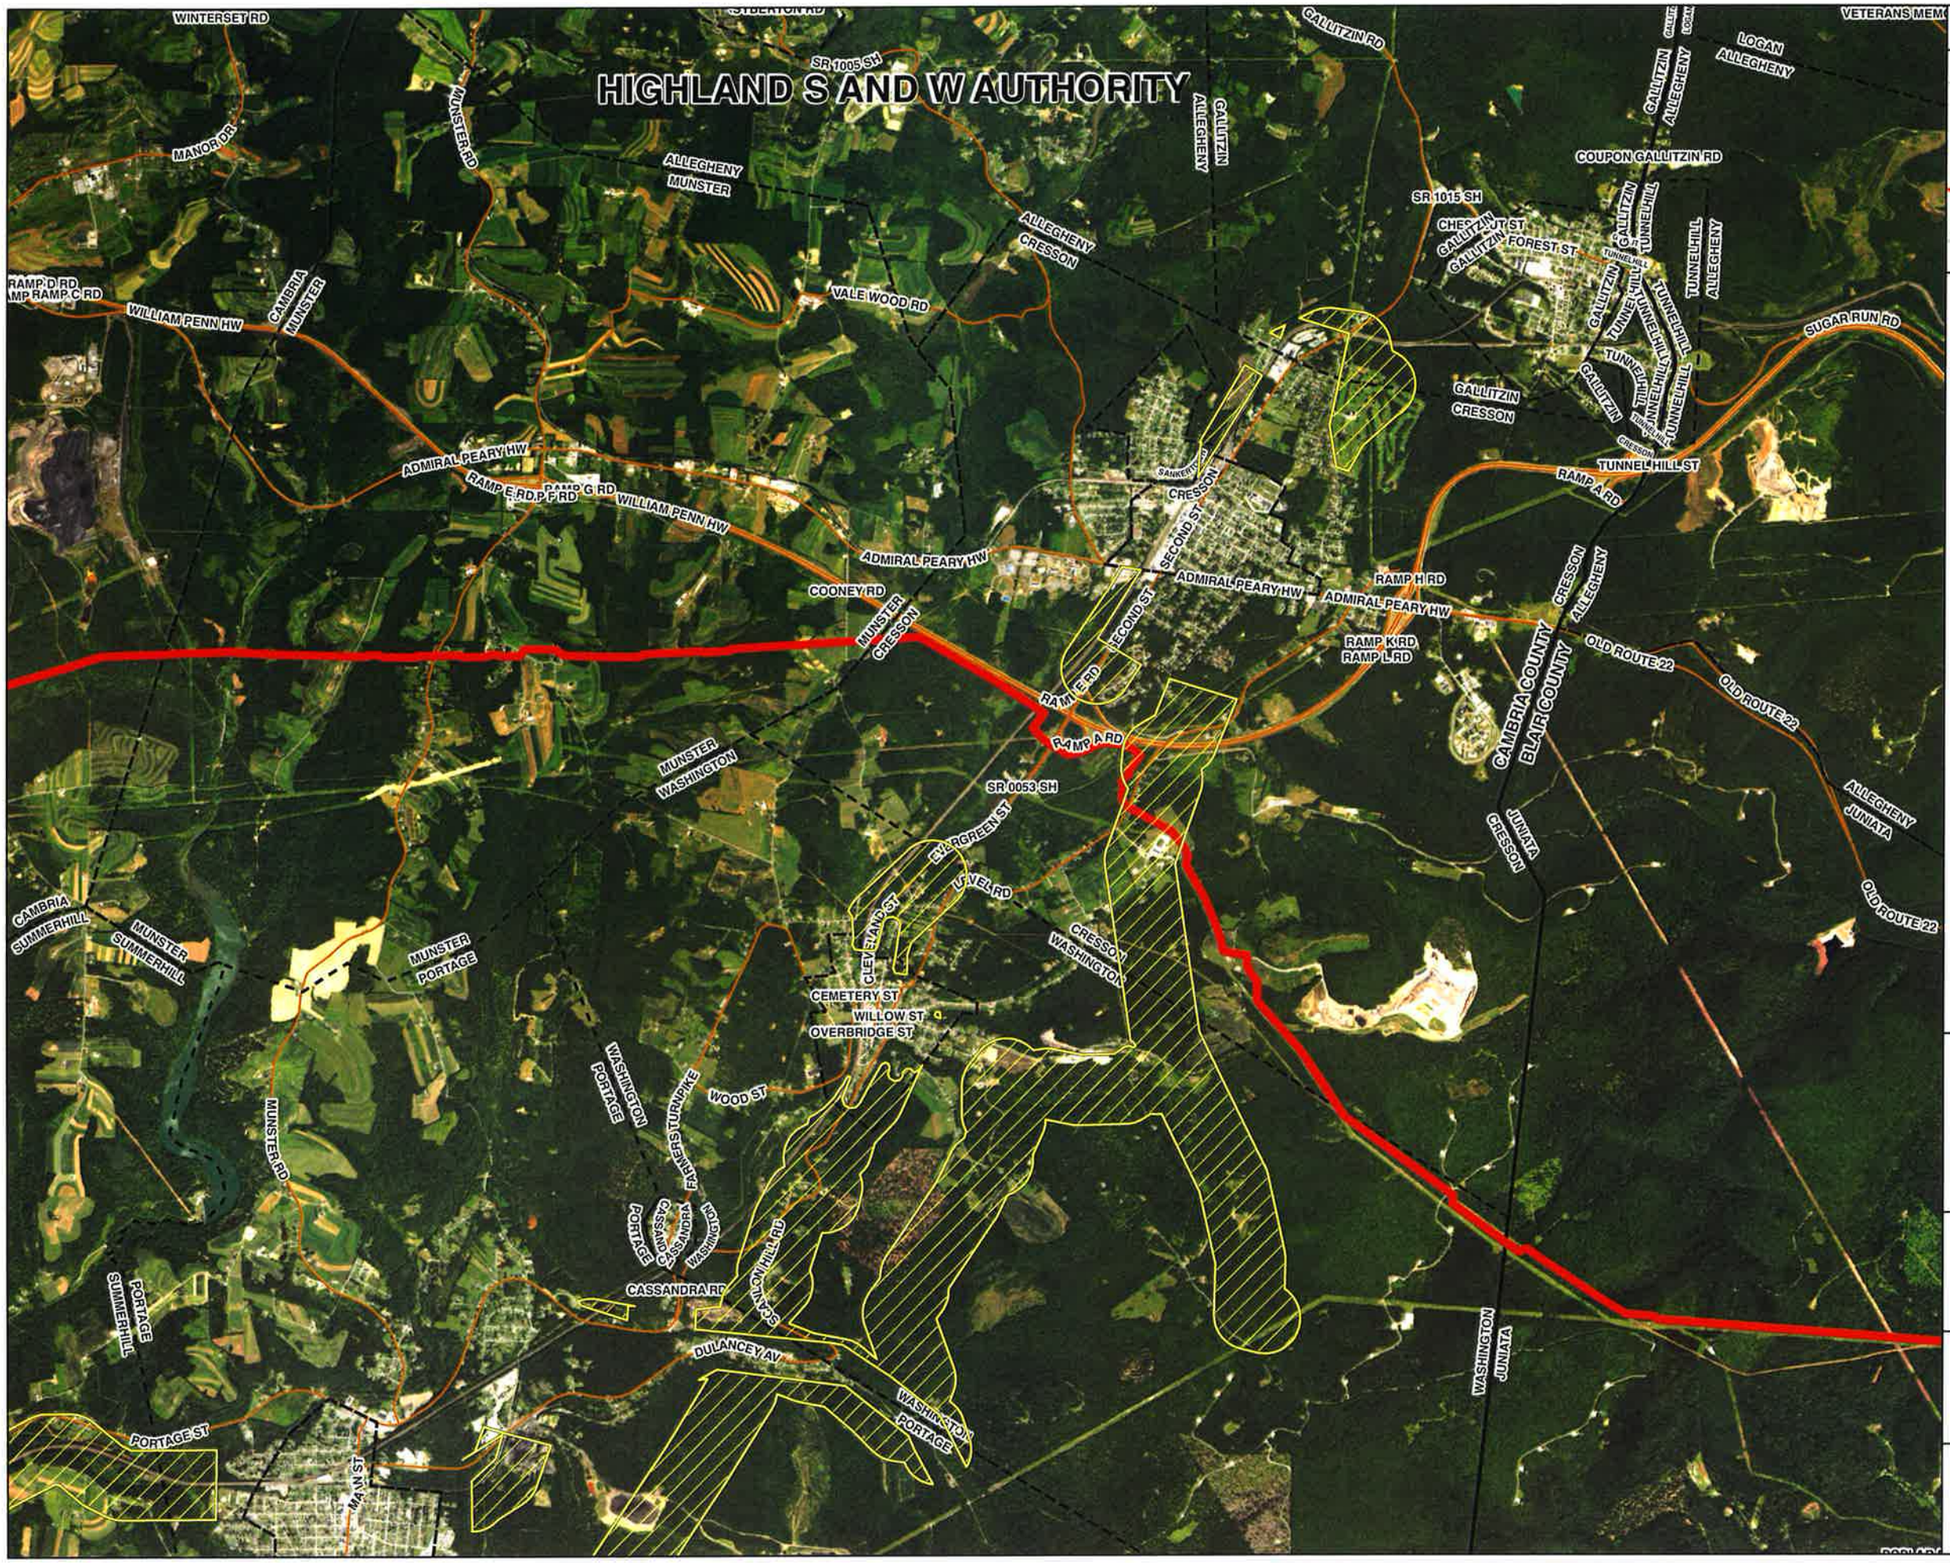

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Highlands S & W Auth Lloydell	Telephone: 814-266-3146
Contact name:	Edward J. Englehart	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Edward J. Englehart at Highlands S & W Auth Lloydell on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 9/21/16 indicating source location, and stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 9:40 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470967470 Delivered

Your package has been delivered

Tracking # 777470967470

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Mon, 10/17/2016 9:34 am

Highland Sewer&Water Auth. Lloydell
120 Tank Drive
JOHNSTOWN, PA 15904
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470967470
Status:	Delivered: 10/17/2016 09:34 AM Signed for By: H.HOHON
Reference:	112IC05958, 16
Signed for by:	H.HOHON
Delivery location:	JOHNSTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
Standard transit:	10/17/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:39 AM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

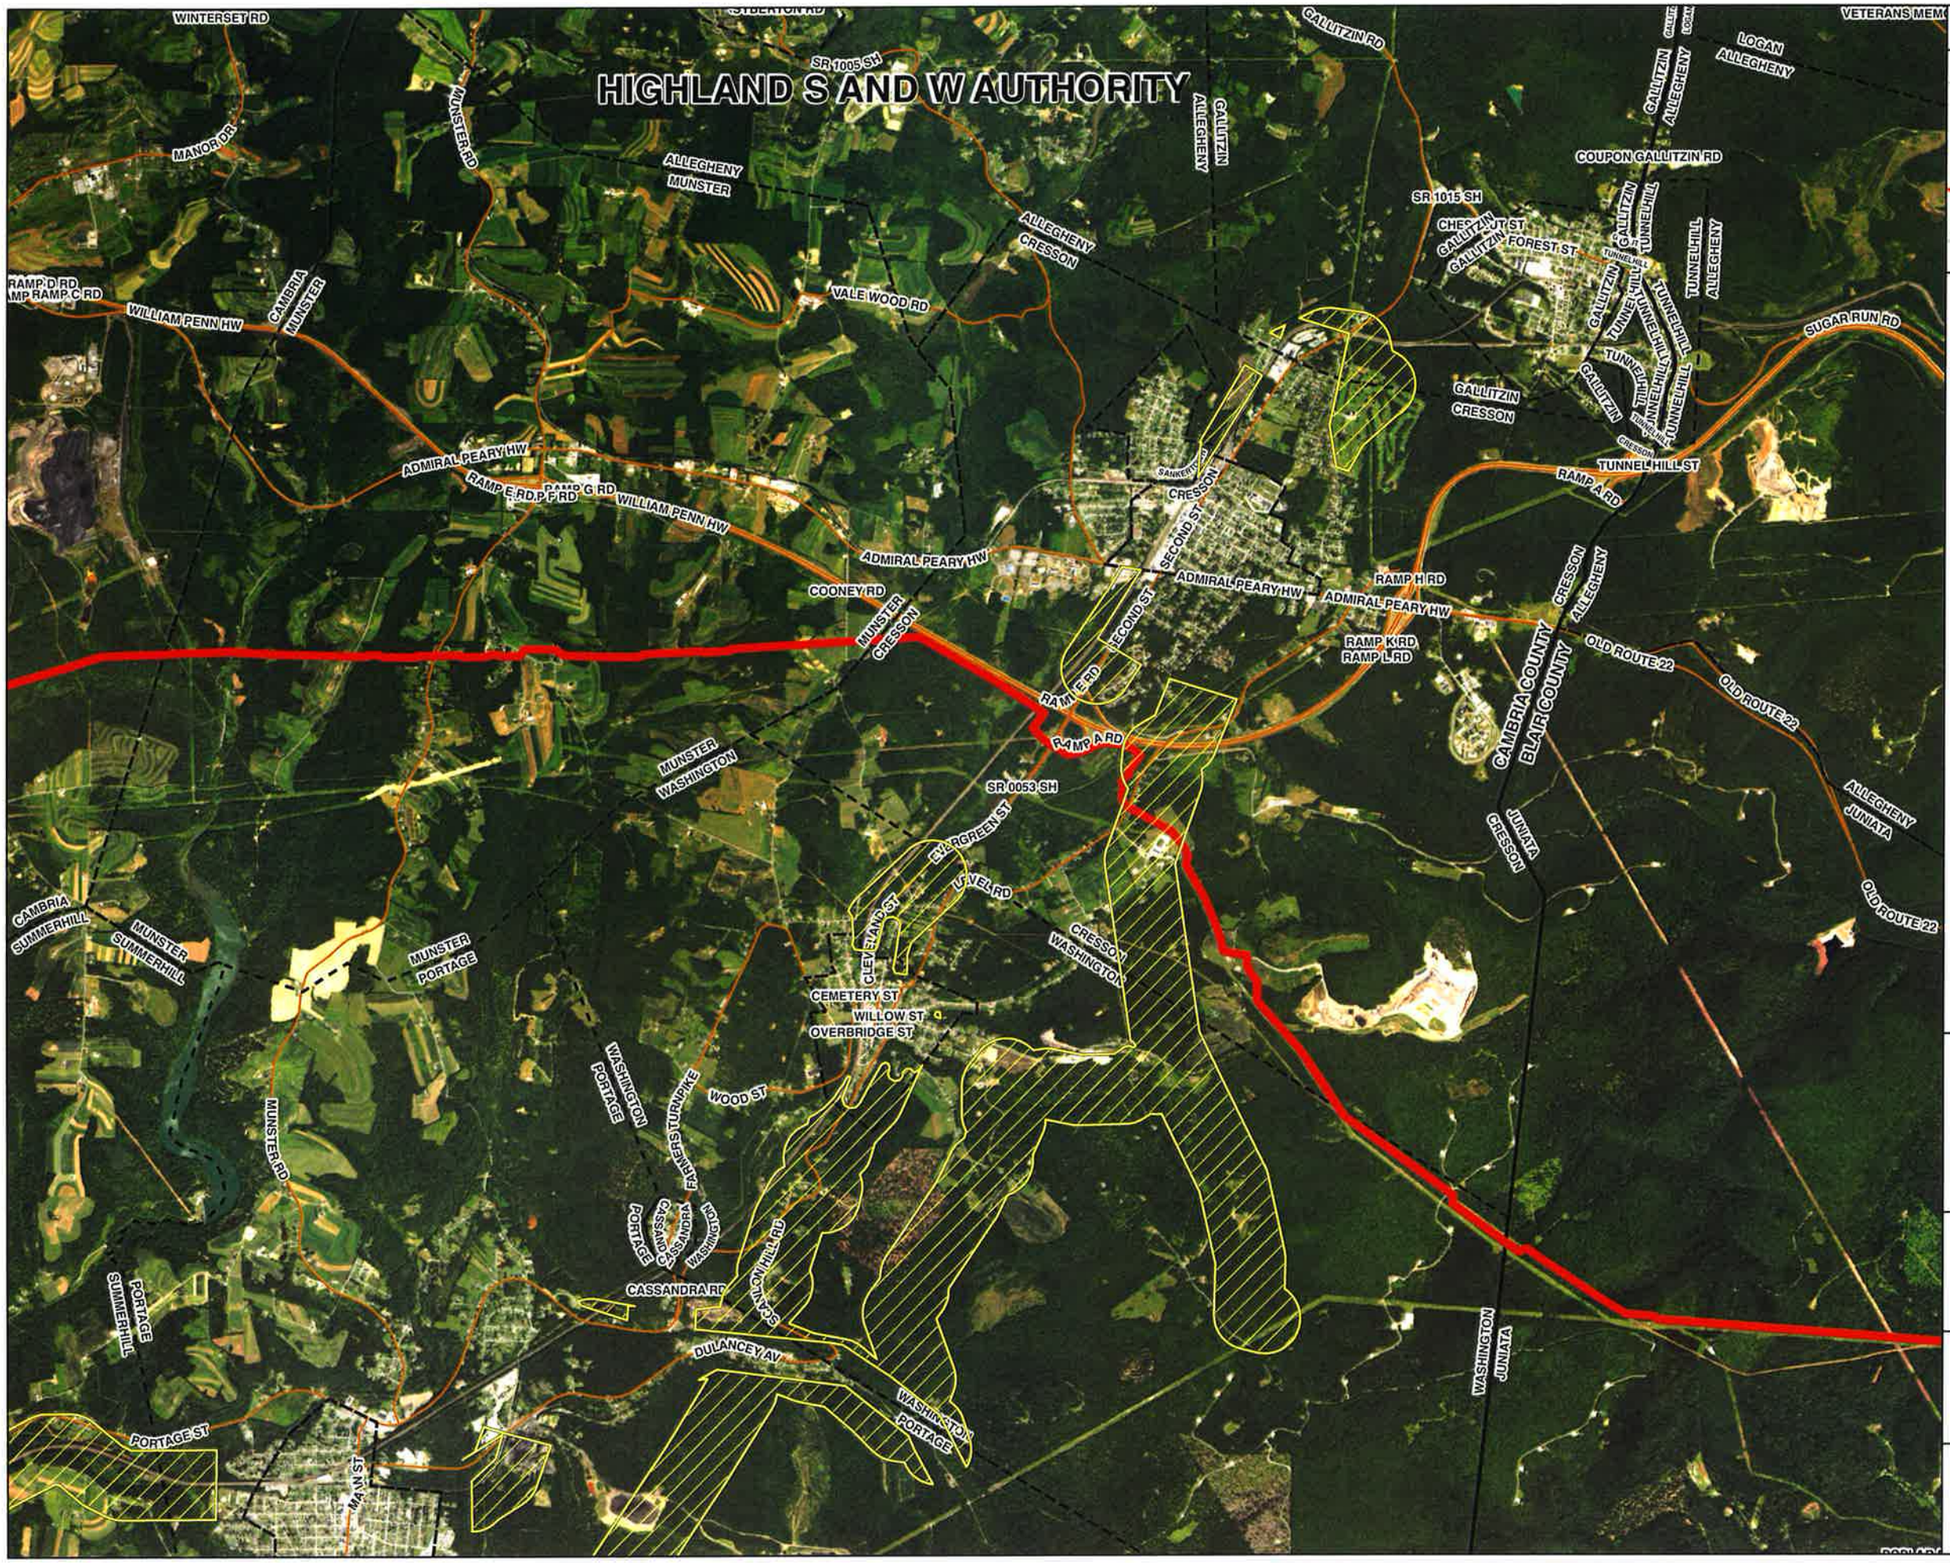

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Highlands S & W Auth Northern End	Telephone: 814-266-3146
Contact name:	Edward J. Englehart	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Edward J. Englehart at Highlands S & W Auth Northern End on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 9/21/16 indicating source location, and stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 9:40 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777470987596 Delivered

Your package has been delivered

Tracking # 777470987596

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Mon, 10/17/2016 9:34 am

Highland S&W Authority Northern End
120 Tank Drive
JOHNSTOWN, PA 15904
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777470987596
Status:	Delivered: 10/17/2016 09:34 AM Signed for By: H.HOHON
Reference:	112IC05958, 16
Signed for by:	H.HOHON
Delivery location:	JOHNSTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
Standard transit:	10/17/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:39 AM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

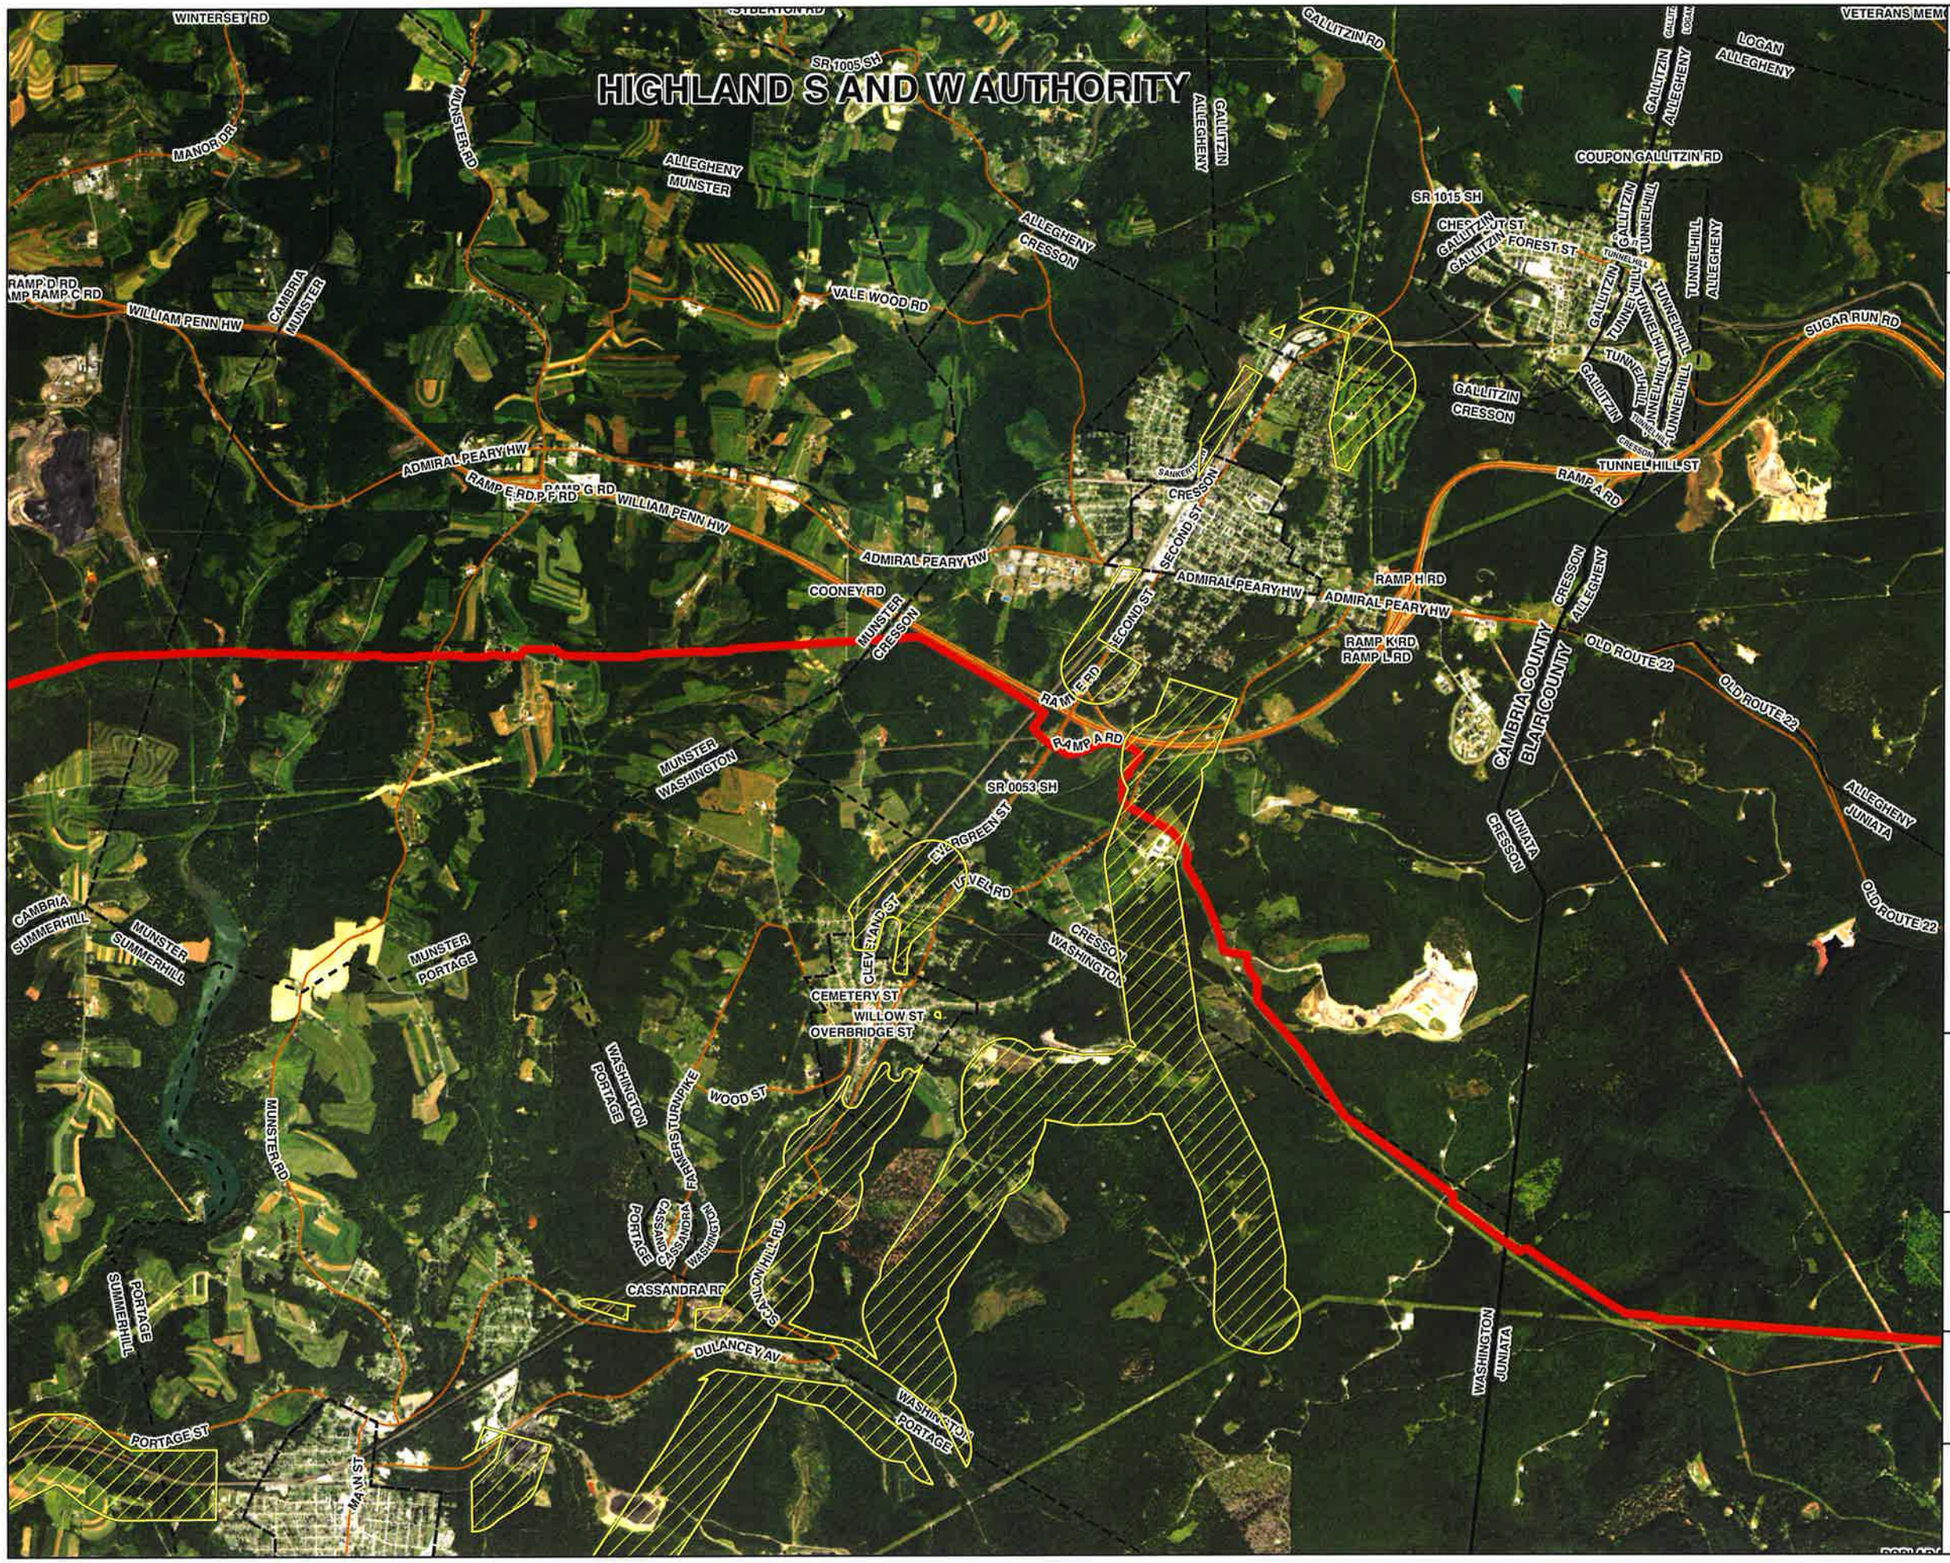

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Highridge Water Auth	Telephone: 888-557-4343
Contact name:	George E. Sulkosky	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to George E. Sulkosky at Highridge Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received email on 9/23/16 stating no impact.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:34 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275779110 Delivered

Your package has been delivered

Tracking # 777275779110

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 12:31 pm

George E. Sulkosky, Ex. Director
Highridge Water Authority
17 Maple Avenue
BLAIRSVILLE, PA 15717
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275779110
Status:	Delivered: 09/21/2016 12:31 PM Signed for By: C.HRISTINE
Reference:	112IC05958, 16
Signed for by:	C.HRISTINE
Delivery location:	BLAIRSVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:33 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

HIGHRIDGE WATER AUTHORITY

INDIANA COUNTY

CAMBRIA COUNTY

WESTMORELAND COUNTY

INDIANA COUNTY


WESTMORELAND COUNTY

CAMBRIA COUNTY

CAMBRIA COUNTY

SOMERSET COUNTY

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 13,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Hillside Mhp Telephone: 717-576-3155
Contact name:	Steve Hollenbaugh
From:	Josh Baird (Tt)
Date:	September 20, 2016
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Steve Hollenbaugh at Hillside Mhp on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Saturday, September 24, 2016 2:05 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275794371 Delivered

Your package has been delivered

Tracking # 777275794371

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Sat, 9/24/2016 2:04 pm

Steve Hollenbaugh
Hillside MHP
2404 Walnut Bottom Road
CARLISLE, PA 17015
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275794371
Status:	Delivered: 09/24/2016 2:04 PM Signed for By: S. HOLLENBAUGH
Door Tag number:	DT104394686116
Reference:	112IC05958, 16
Signed for by:	S. HOLLENBAUGH
Delivery location:	MIDDLETOWN, PA
Delivered to:	FedEx Location
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
	Residential Delivery
Standard transit:	9/21/2016 by 8:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:04 PM CDT on 09/24/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Historic Acres of Hershey	Telephone: 570-298-6340
Contact name:	Kevin Freedman	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Kevin Freedman at Historic Acres of Hershey on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

TETRA TECH

Contact Report

To:	Hollidaysburg Muni Auth	Telephone: 814-695-7543
Contact name:	John Little	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to John Little at Hollidaysburg Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received a letter dated 10/3/16 requesting additional information (plans and profiles). Called Gary Winsor at Stiffler & McGraw on 10/12/16, left a voicemail in regards to the letter. Spoke with Gary Winsor on 10/17. He had some documents to review in regards to the Project, but said he thought everything was good and would contact us if he has any futher questions.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:52 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275810555 Delivered

Your package has been delivered

Tracking # 777275810555

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 12:42 pm

John Little
Hollidaysburg Muni Authority
401 Blair Street
HOLLIDAYSBURG, PA 16648
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275810555
Status:	Delivered: 09/21/2016 12:42 PM Signed for By: S.OSWALD
Reference:	112IC05958, 16
Signed for by:	S.OSWALD
Delivery location:	HOLLIDAYSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:52 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

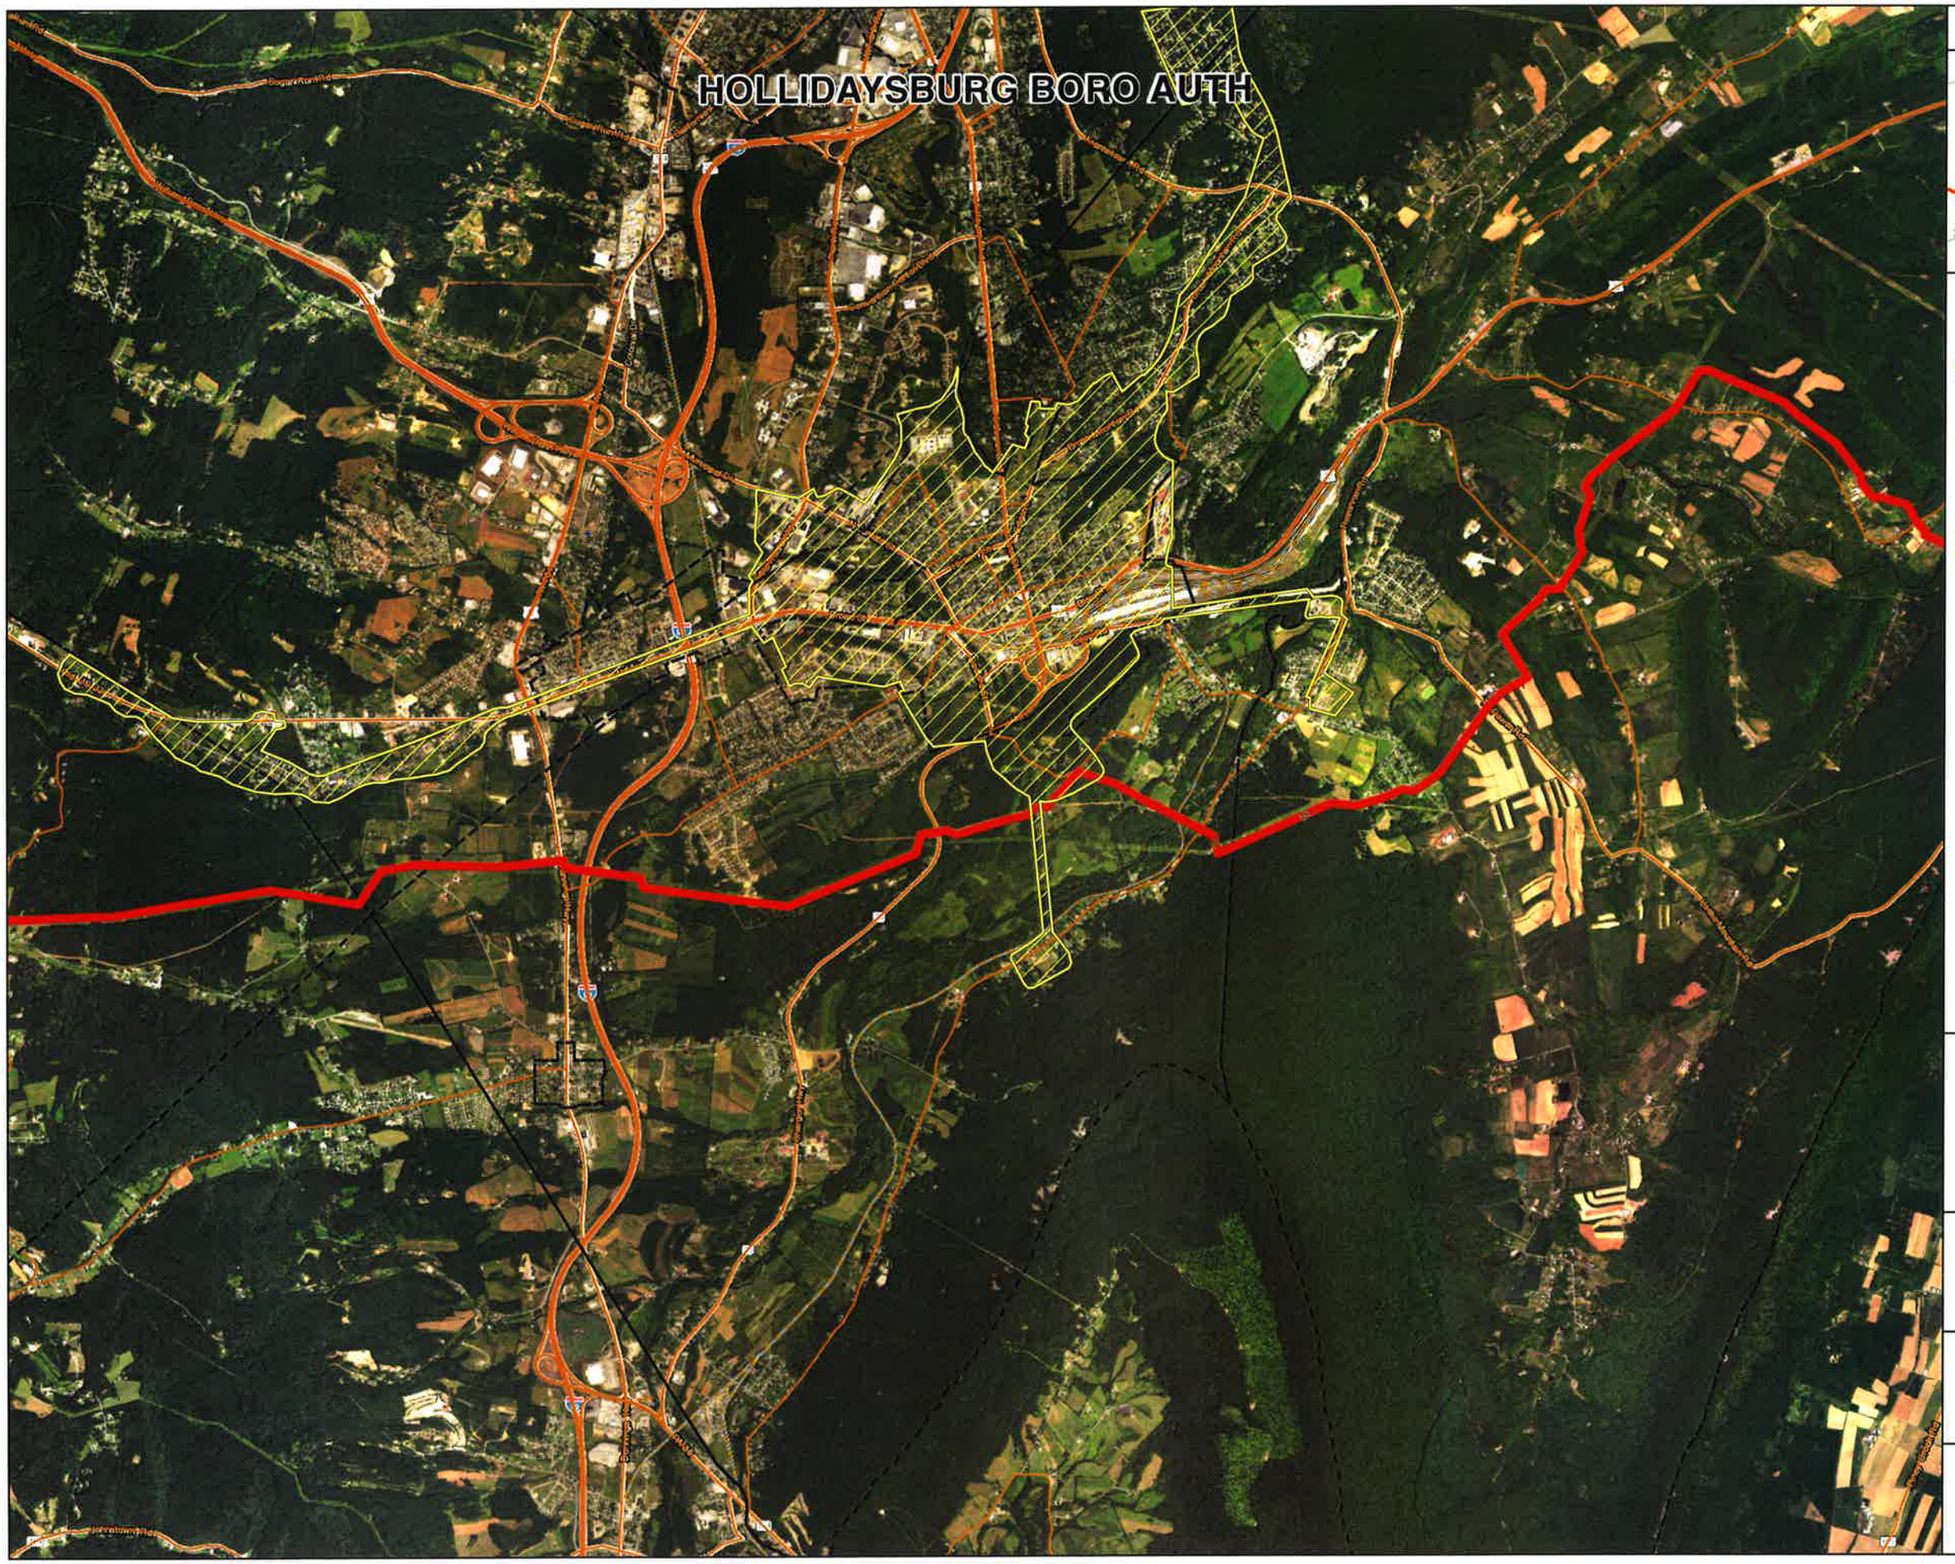

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Houston Sunoco	Telephone: 724-745-1214
Contact name:	Mehul Vakil	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Mehul Vakil at Houston Sunoco on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:30 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206866760 Delivered

Your package has been delivered

Tracking # 778206866760

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:27 am

c/o Mehul Vakil
Houston Sunoco
2300 Hill Church Road
CANONSBURG, PA 15317
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206866760
Status:	Delivered: 01/19/2017 09:27 AM Signed for By: M.VECHIL
Reference:	112IC05958, 16
Signed for by:	M.VECHIL
Delivery location:	CANONSBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:29 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

HOUSTON SUNOCO
c/o Mehul Vakil
2300 Hill Church Road
Canonsburg, PA 15317

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Huies Gray Fox Inn	Telephone: 717-484-2625
Contact name:	Dale Huie	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Dale Huie at Huies Gray Fox Inn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:51 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206640971 Delivered

Your package has been delivered

Tracking # 778206640971

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 11:47 am

c/o Dale Huie
Huies Gray Fox Inn
2142 South Galen Hall Rd
REINHOLDS, PA 17569
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206640971
Status:	Delivered: 01/19/2017 11:47 AM Signed for By: D.HUIE
Reference:	112IC05958, 16
Signed for by:	D.HUIE
Delivery location:	REINHOLDS, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:50 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

HUIES GRAY FOX INN
c/o Dale Huie
2142 South Galen Hall Rd
Reinholds, PA 17569

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Jackson Twp Water Auth	Telephone: 814-322-1262
Contact name:	Walter Ditchcreek	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Walter Ditchcreek at Jackson Twp Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:04 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275831391 Delivered

Your package has been delivered

Tracking # 777275831391

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 12:59 pm

Walter Ditchcreek, Chairman
Jackson Twp Water Authority
2949 William Penn Avenue
JOHNSTOWN, PA 15909
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275831391
Status:	Delivered: 09/21/2016 12:59 PM Signed for By: D.BUSKA
Reference:	112IC05958, 16
Signed for by:	D.BUSKA
Delivery location:	JOHNSTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:04 PM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

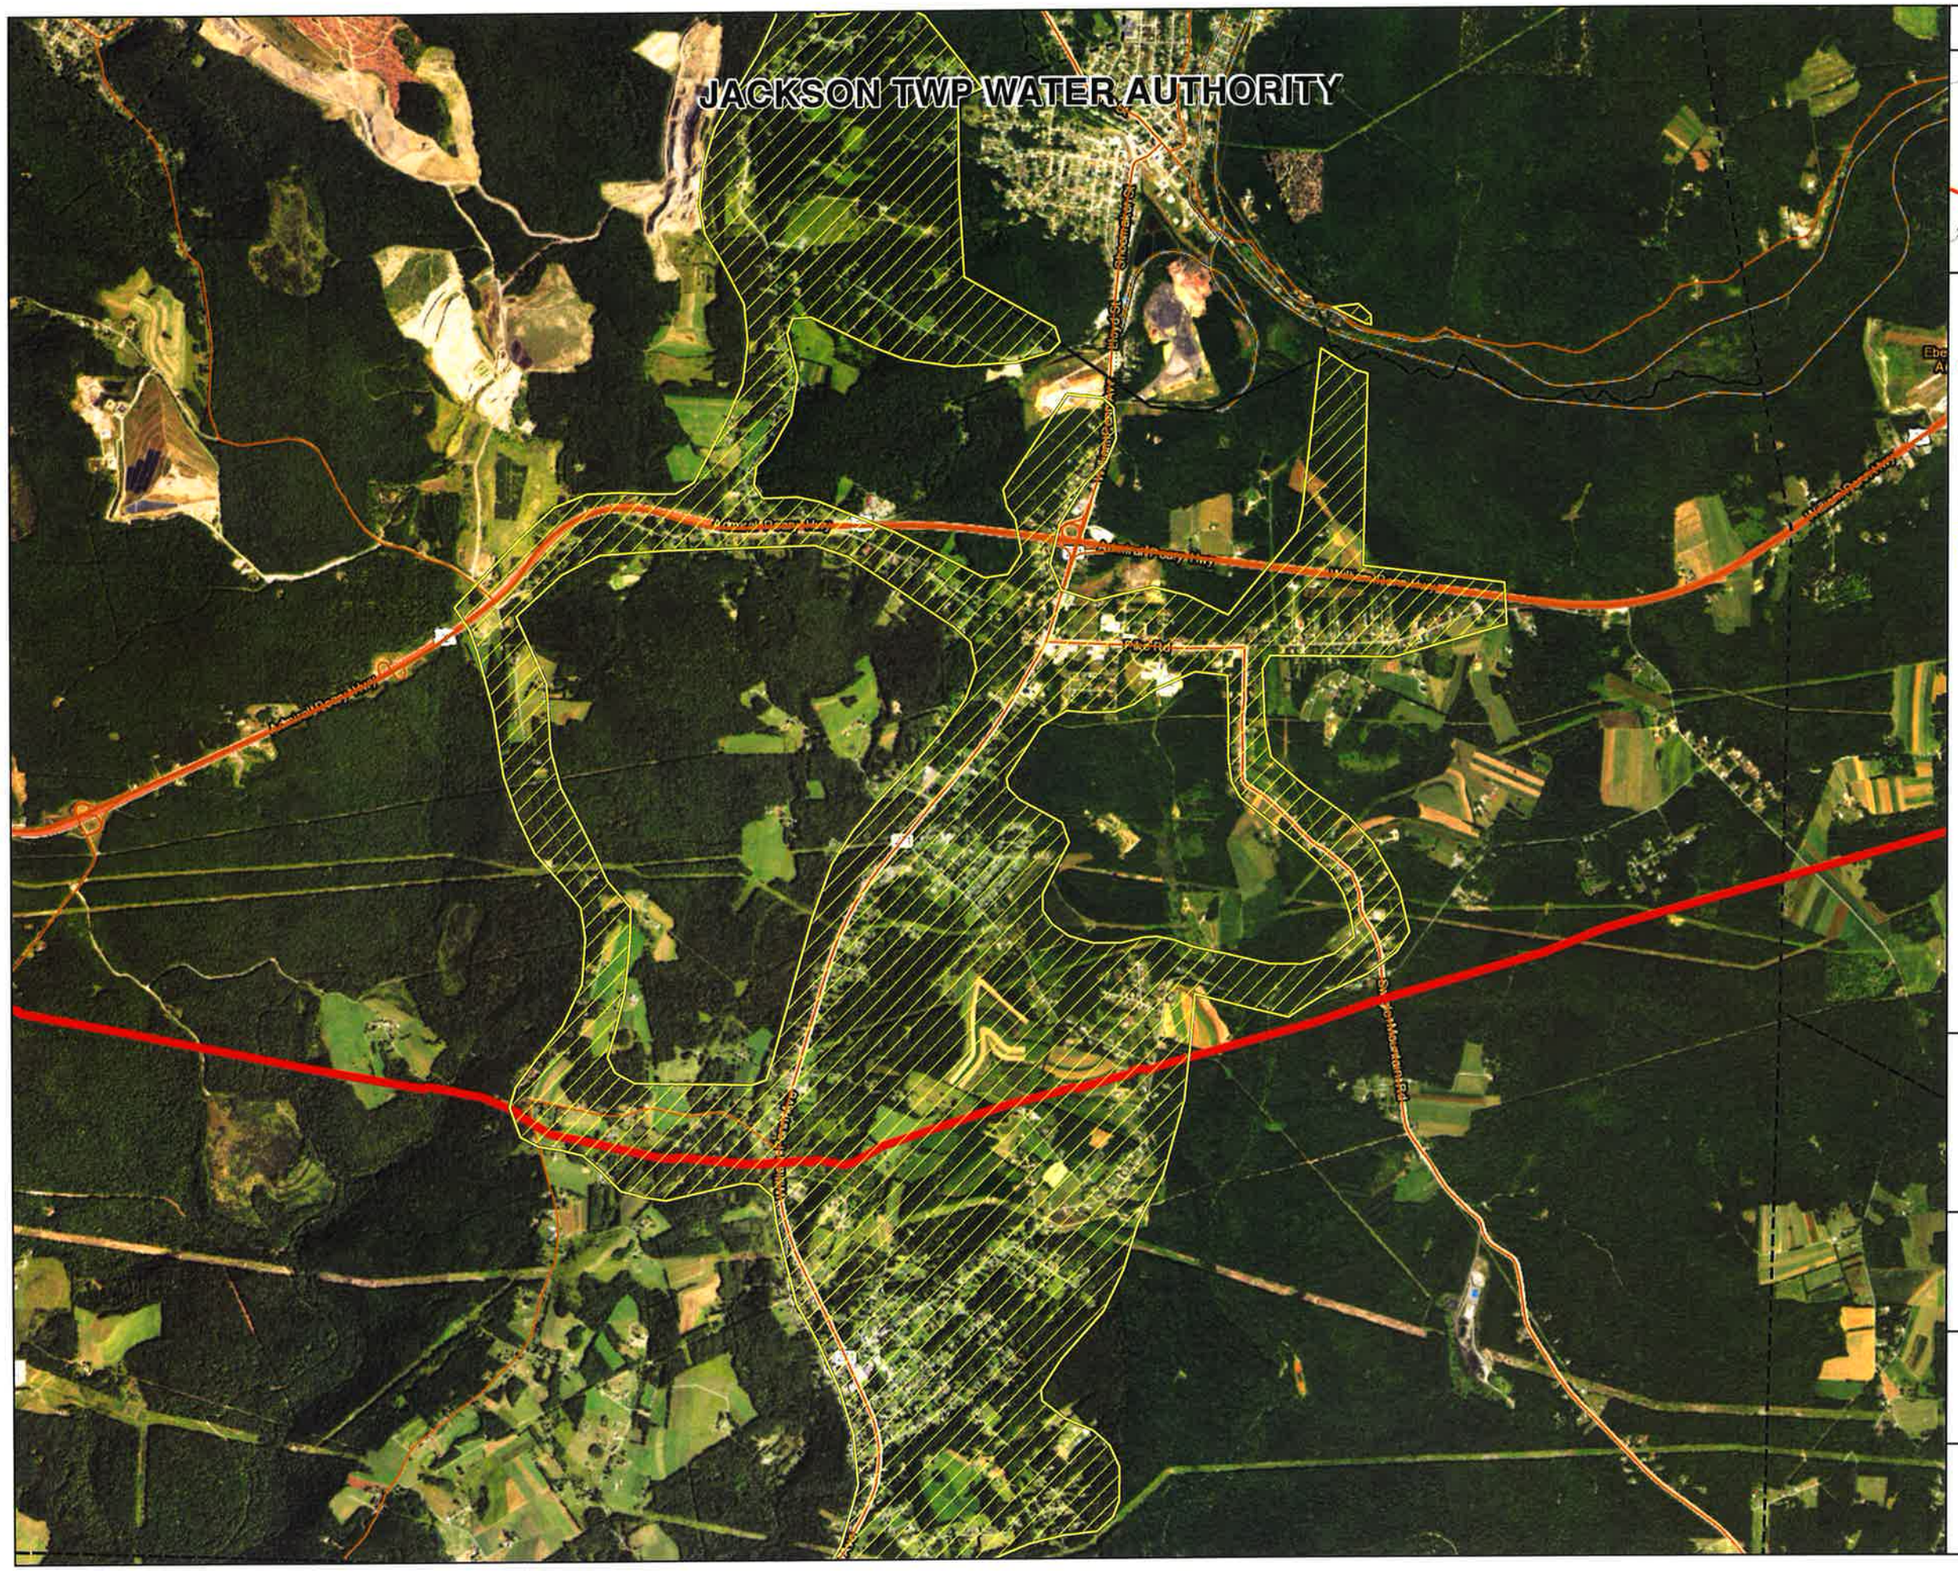

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Joanna Furnace Telephone: 610-286-0388
Contact name:	Mark Zerr
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Mark Zerr at Joanna Furnace on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 27, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7743

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

GEIGERTOWN, PA 19523

OFFICIAL USE

Certified Mail Fee	$3.30
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$0.00
Postage	$1.57
Total Postage and Fees	$4.87

0205
21

Postmark Here

JAN 19 2017

GEIGERTOWN PA STATION

01/19/2017

Sent To
JOANNA FURNACE
Street and
c/o MARK ZERR
City, State
P.O. BOX 36
GEIGERTOWN, PA 19523

PS Form

tions

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237743

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 27, 2017 , 12:47 pm	**Delivered, Individual Picked Up at Post Office**	**GEIGERTOWN, PA 19523**
Your item was picked up at the post office at 12:47 pm on January 27, 2017 in GEIGERTOWN, PA 19523.		
January 23, 2017 , 8:35 am	Available at PO Box	GEIGERTOWN, PA 19523
January 23, 2017 , 8:25 am	Sorting Complete	GEIGERTOWN, PA 19523
January 23, 2017 , 7:00 am	Arrived at USPS Facility	WERNERSVILLE, PA 19565
January 23, 2017 , 6:57 am	Arrived at Unit	WERNERSVILLE, PA 19565
January 22, 2017 , 8:53 am	In Transit to Destination	
January 22, 2017 , 4:58 am	Departed USPS Facility	HARRISBURG, PA 17107
January 21, 2017 , 8:53 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

JOANNA FURNACE
c/o Mark Zerr
P.O. Box 36
Geigertown, PA 19523

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Joanna Store Telephone: 610-286-5197
Contact name:	Teresa Moyer
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Teresa Moyer at Joanna Store on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:44 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204895856 Delivered

Your package has been delivered

Tracking # 778204895856

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:39 am

c/o Teresa Moyer
Joanna Store
1102 Elverson Road
MORGANTOWN, PA 19543
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204895856
Status:	Delivered: 01/19/2017 10:39 AM Signed for By: P.HUYETT
Reference:	112IC05958, 16
Signed for by:	P.HUYETT
Delivery location:	MORGANTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:44 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

JOANNA STORE
c/o Teresa Moyer
1102 Elverson Road
Morgantown, PA 19543

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Ken Grill Recreation Asson Telephone: 610-777-9322
Contact name:	Randy Hauk
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Randy Hauk at Ken Grill Recreation Assn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 24, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7736

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com*®.

READING, PA 19607

OFFICIAL USE

Certified Mail Fee	$3.30
$	$0.00
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
$	
Total Postage and Fees	$4.87
$	

0205
21

Postmark Here
JAN 19
01/19/2017

Sent To
Street and Ap
City, State, Z

KEN GRILL RECREATION ASSN.
c/o RANDY HAUK
P.O. BOX 113
SHILLINGTON, PA 19607

PS Form 38

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237736

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 24, 2017 , 4:48 pm	**Delivered**	**READING, PA 19607**
Your item was delivered at 4:48 pm on January 24, 2017 in READING, PA 19607.		
January 23, 2017 , 9:34 am	Available for Pickup	READING, PA 19607
January 22, 2017 , 7:25 pm	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:53 am	In Transit to Destination	
January 21, 2017 , 8:53 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

KEN GRILL RECREATION ASSN
c/o Randy Hauk
P.O. Box 113
Shillington, PA 19607

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Keystone Restaurant	Telephone: 814-886-4533
Contact name:	Gary and Jay Ritchey	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Gary and Jay Ritchey at Keystone Restaurant on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7811

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

EBENSBURG, PA 15931

OFFICIAL USE

Certified Mail Fee $3.30

Extra Services & Fees *(check box, add fee as appropriate)*
- ☐ Return Receipt (hardcopy) $0.00
- ☐ Return Receipt (electronic) $0.00
- ☐ Certified Mail Restricted Delivery $0.00
- ☐ Adult Signature Required $0.00
- ☐ Adult Signature Restricted Delivery $

Postage $1.57

Total Postage and Fees $4.87

Postmark Here

01/19/2017

0205

ELLICOTT STATION 14203

Sent To KEYSTONE RESTAURANT

Street and A c/o GARY AND JAY RITCHEY

City, State, P.O. BOX 277

EDENSBURG, PA 15931

PS Form 3 ions

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237811

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 25, 2017 , 1:38 pm	**Delivered**	**EBENSBURG, PA 15931**
Your item was delivered at 1:38 pm on January 25, 2017 in EBENSBURG, PA 15931.		
January 21, 2017 , 9:12 am	Available for Pickup	EBENSBURG, PA 15931
January 21, 2017 , 6:00 am	Departed USPS Facility	JOHNSTOWN, PA 15904
January 20, 2017 , 11:44 am	Arrived at USPS Destination Facility	JOHNSTOWN, PA 15904
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

KEYSTONE RESTAURANT
c/o Gary And Jay Ritchey
P.O. Box 277
Ebensburg, PA 15931

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Kingdom Hall Mount Joy	Telephone: 717-653-8501
Contact name:	Ralph Watters	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ralph Watters at Kingdom Hall Mount Joy on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:54 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778207054978 Delivered

Your package has been delivered

Tracking # 778207054978

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:48 am

c/o Ralph Watters
Kingdom Hall Mount Joy
861 Milton Grove Rd
MOUNT JOY, PA 17552
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778207054978
Status:	Delivered: 01/19/2017 09:48 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	MOUNT JOY, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:53 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

KINGDOM HALL MOUNT JOY
c/o Ralph Watters
861 Milton Grove Rd
Mount Joy, PA 17552

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	La Cantina Italian Restaurant Telephone: 610-777-5646
Contact name:	Salvatore Russo
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Salvatore Russo at La Cantina Italian Restaurant on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:58 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204940392 Delivered

Your package has been delivered

Tracking # 778204940392

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:55 am

c/o Salvatore Russo
La Cantina Italian Restaurant
4312 New Holland Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204940392
Status:	Delivered: 01/19/2017 10:55 AM Signed for By: K.SWEIGART
Door Tag number:	DT104558854823
Reference:	112IC05958, 16
Signed for by:	K.SWEIGART
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:58 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

LA CANTINA ITALIAN RESTAURANT
c/o Salvatore Russo
4312 New Holland Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	La Porta Ristorante	Telephone: 610-358-5104
Contact name:	Hugh Donahue	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Hugh Donahue at La Porta Ristorante on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:01 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206343582 Delivered

Your package has been delivered

Tracking # 778206343582

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:57 am

c/o Hugh Donahue
La Porta Ristorante
1192 N. Middletown Road
MEDIA, PA 19063
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206343582
Status:	Delivered: 01/19/2017 09:57 AM Signed for By: K.KORANCNG
Reference:	112IC05958, 16
Signed for by:	K.KORANCNG
Delivery location:	MEDIA, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:01 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

LA PORTA RISTORANTE
c/o Hugh Donahue
1192 N. Middletown Road
Media, PA 19063

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Lane Enterprises	Telephone: 717-249-8342
Contact name:	Gary Hinkelman	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Gary Hinkelman at Lane Enterprises on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:27 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206081059 Delivered

Your package has been delivered

Tracking # 778206081059

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:22 am

c/o Gary Hinkelman
Lane Enterprises
1244 Claremont Rd
CARLISLE, PA
17013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206081059
Status:	Delivered: 01/19/2017 10:22 AM Signed for By: T.RTHROME
Reference:	112IC05958, 16
Signed for by:	T.RTHROME
Delivery location:	CARLISLE, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:27 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

LANE ENTERPRISES
c/o Gary Hinkelman
1244 Claremont Rd
Carlisle, PA 17013

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Lebanon Val Bible Church	Telephone: 717-867-4403
Contact name:	Deacon Board Chairman	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Deacon Board Chairman at Lebanon Val Bible Church on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:23 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206726477 Delivered

Your package has been delivered

Tracking # 778206726477

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:20 am

c/o Deacon Board Chairman
Lebanon Val Bible Church
1482 Horseshoe Pike
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206726477
Status:	Delivered: 01/19/2017 09:20 AM Signed for By: T.STANKOVICH
Reference:	112IC05958, 16
Signed for by:	T.STANKOVICH
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:22 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

LEBANON VAL BIBLE CHURCH
c/o Att: Deacon Board Chairman
1482 Horseshoe Pike
Lebanon, PA 17042

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Lebanon Water Auth	Telephone: 717-865-2191
Contact name:	Jonathan Beers	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Jonathan Beers at Lebanon Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

No impact email received from Bob Sentz on 9/26/16.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:30 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275848526 Delivered

Your package has been delivered

Tracking # 777275848526

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 1:27 pm

Jonathan Beers
Lebanon Water Authority
2311 Ridgeview Road
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275848526
Status:	Delivered: 09/21/2016 1:27 PM Signed for By: L.COOLEY
Reference:	112IC052958, 16
Signed for by:	L.COOLEY
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:29 PM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.


LEBANON CITY WATER AUTHORITY
Maple St
Walnut St
Chestnut St
Poplar St
Elm St
Cumberland St
Lebanon Ave
King St
Prescott Rd
Tunnel Rd
Quentin Rd
Lancaster Ave
Cornwall Rd
Oak St
Church St
Locust St
Pine St
Linden St
Willow St
Penn St
Fairview Rd
Mt Zion Rd
Weavertown Rd
Rexmont Rd
Royal Rd
Colebrookdale Rd
Morgantown Rd
Boyertown Pike
Schaefer Rd
Stiger Ln
W Main St
E Main St
Freeman Dr
Alden St
Beyer St
Antiyachten Rd
Burkholder Rd
Bethel Rd
Old Bethel Rd
Old Swede Rd
Old Morgantown Rd
Old Boyertown Rd
Old Reading Rd
Old Colebrookdale Rd
Old Schaefer Rd
Old Rexmont Rd
Old Lancaster Ave
Old Cornwall Rd
Old Quentin Rd
Old Tunnel Rd
Old Penn St
Old Fairview Rd
Old Mt Zion Rd
Old Weavertown Rd
Old Linden St
Old Willow St
Old Walnut St
Old Chestnut St
Old Maple St
Old King St
Old Prescott Rd
Old Oak St
Old Church St
Old Locust St
Old Pine St
Old Elm St
Old Poplar St
Old Cumberland St
Old Lebanon Ave
Old Main St
Old Alden St
Old Beyer St
Old Freeman Dr
Old Stiger Ln
Old Schaefer Rd
Old Rexmont Rd
Old Antiyachten Rd
Old Burkholder Rd
Old Bethel Rd
Old Swede Rd
Old Morgantown Rd
Old Boyertown Rd
Old Reading Rd
Old Colebrookdale

TETRA TECH

Contact Report

To:	Lilly Muni Water Works	Telephone: 814-886-7227
Contact name:	Paul Sklodawski	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Paul Sklodawski at Lilly Muni Water Works on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

TETRA TECH

January 18th, 2017

LILLY MUNI WATER WORKS
c/o Paul Sklodawski
417 Cleveland St
Lilly, PA 15938

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 12:23 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205879021 Delivered

Your package has been delivered

Tracking # 778205879021

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 12:19 pm

c/o Paul Sklodawski
Lilly Muni Water Works
417 Cleveland St
LILLY, PA 15938
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205879021
Status:	Delivered: 01/19/2017 12:19 PM Signed for By: Signature Release on file
Reference:	112IC05958, 16
Signed for by:	Signature Release on file
Delivery location:	LILLY, PA
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:23 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

Contact Report

To:	Little Acres Mhp	Telephone: 724-863-1388
Contact name:	Cary Ruffner	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Cary Ruffner at Little Acres Mhp on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery attemps on Septemeber 21, 22, and 23, 2016. Returned to sender due to inability to reach recipient for signature.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, October 19, 2016 12:31 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777471229476 Delivered

Your package has been delivered

Tracking # 777471229476

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 10/19/2016 12:29 pm

Little Acres Mobile Home Park
11070 Greer Street
NORTH
HUNTINGDON, PA 15642
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777471229476
Status:	Delivered: 10/19/2016 12:29 PM Signed for By: S.RUFFNER
Door Tag number:	DT104221052694
Reference:	112IC05958, 16
Signed for by:	S.RUFFNER
Delivery location:	NORTH HUNTINGDON, PA
Delivered to:	Residence
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
	Residential Delivery
Standard transit:	10/17/2016 by 8:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:31 AM CDT on 10/19/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

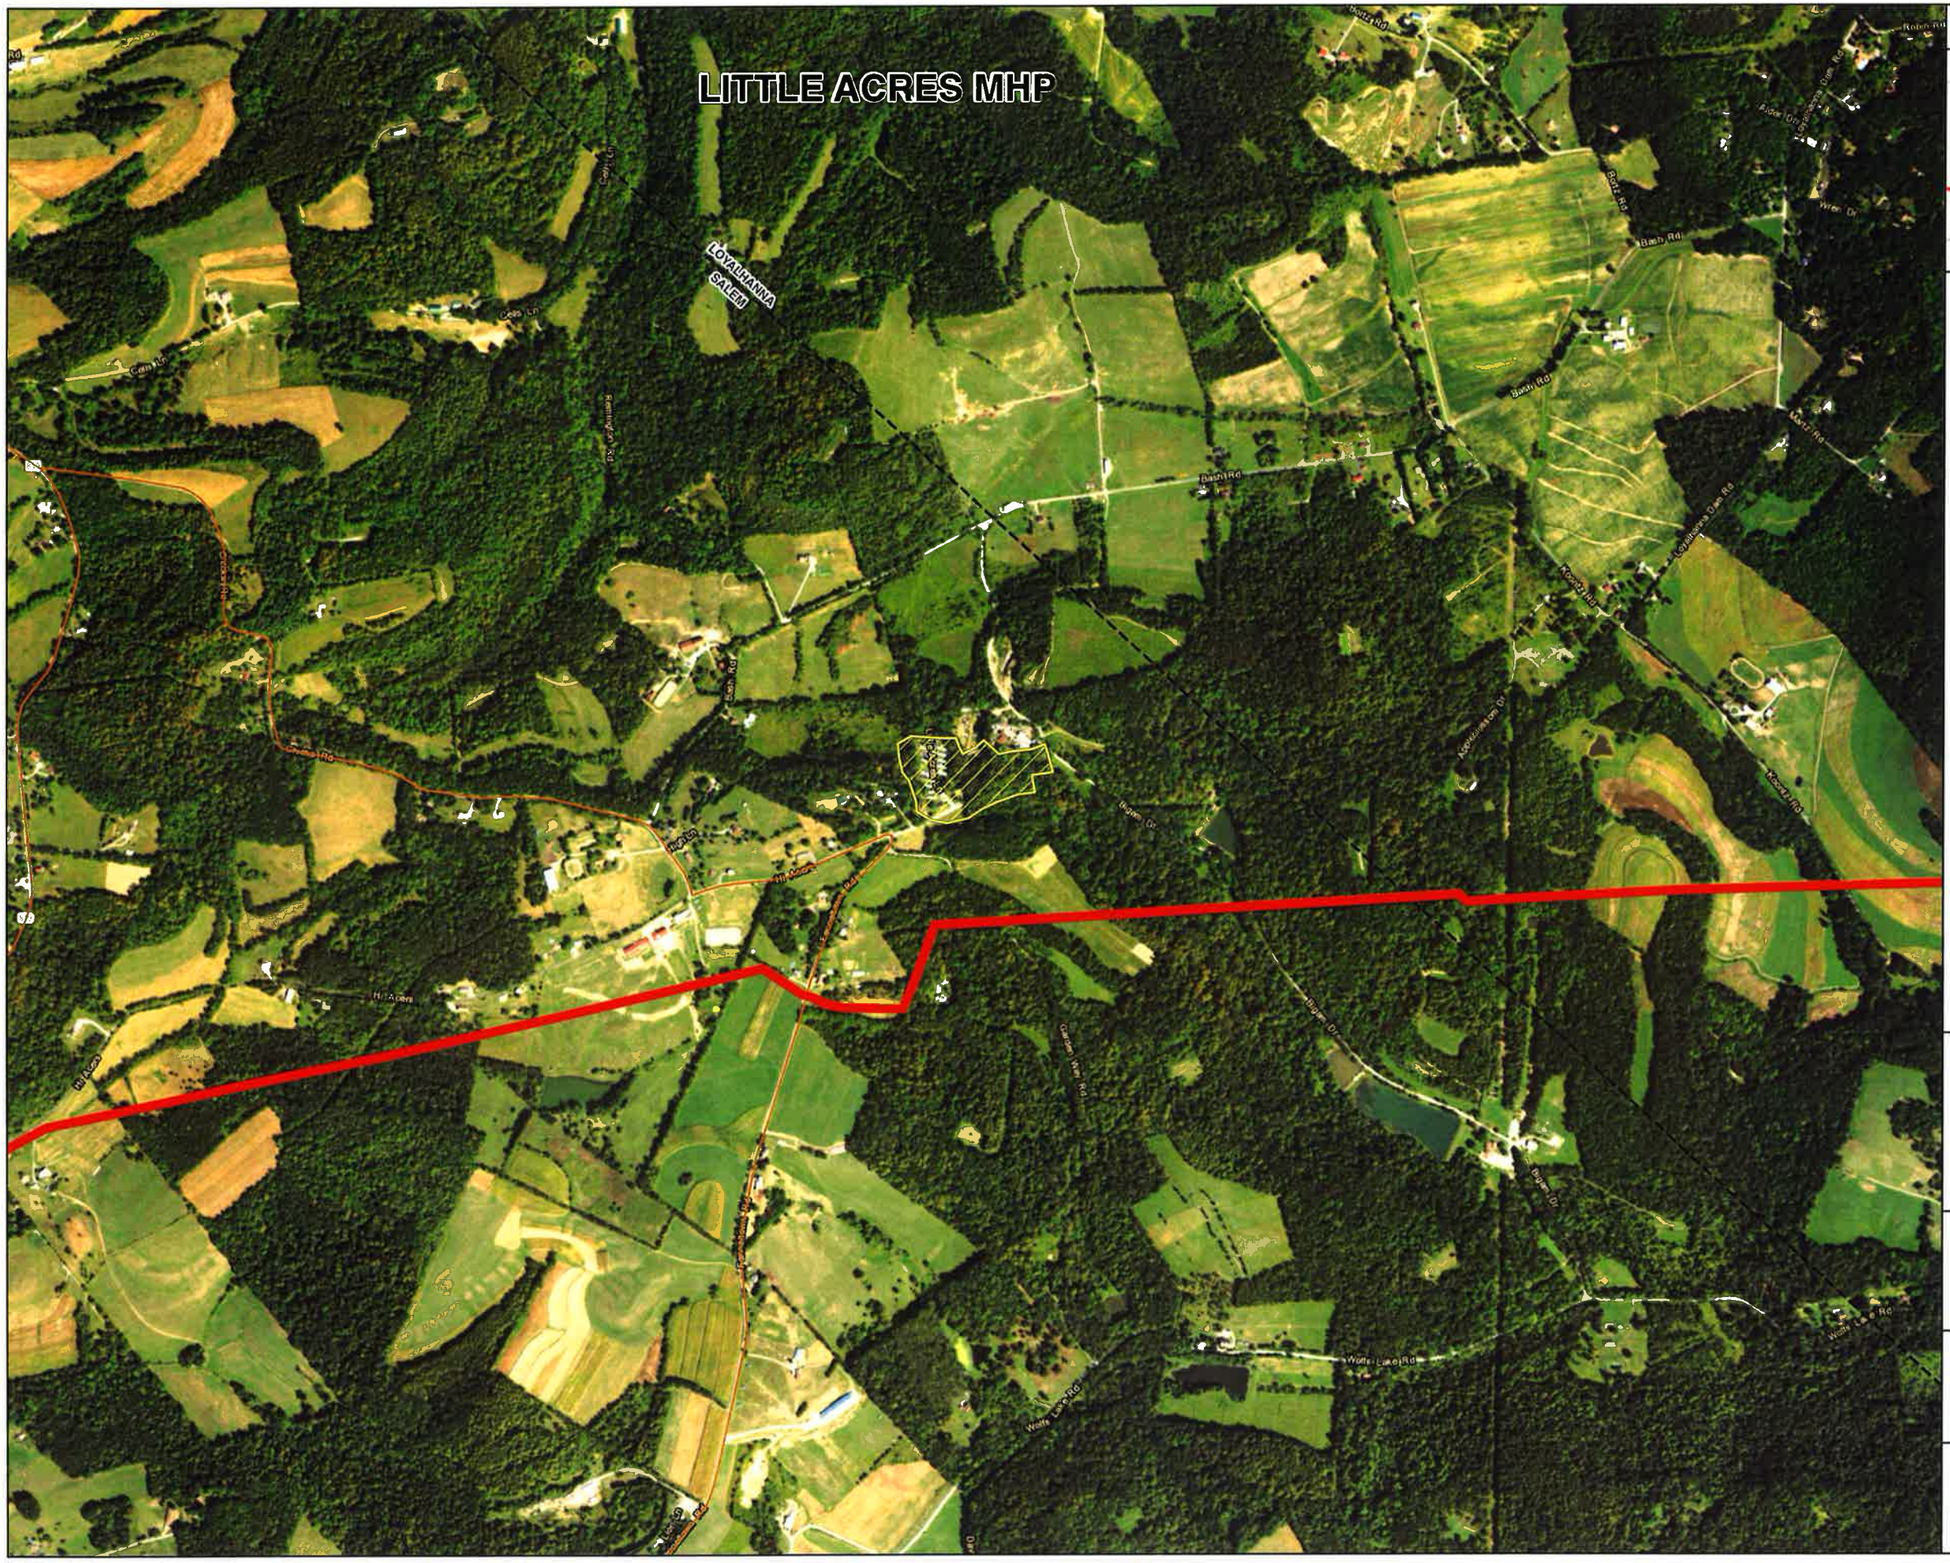

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report


To:	Loags Corner Mobile Home Park	Telephone: 610-286-5183
Contact name:	Alvin Horning	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Alvin Horning at Loags Corner Mobile Home Park on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 23, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Loags Corner Mobile Home Park – PWS Delivery Confirmation

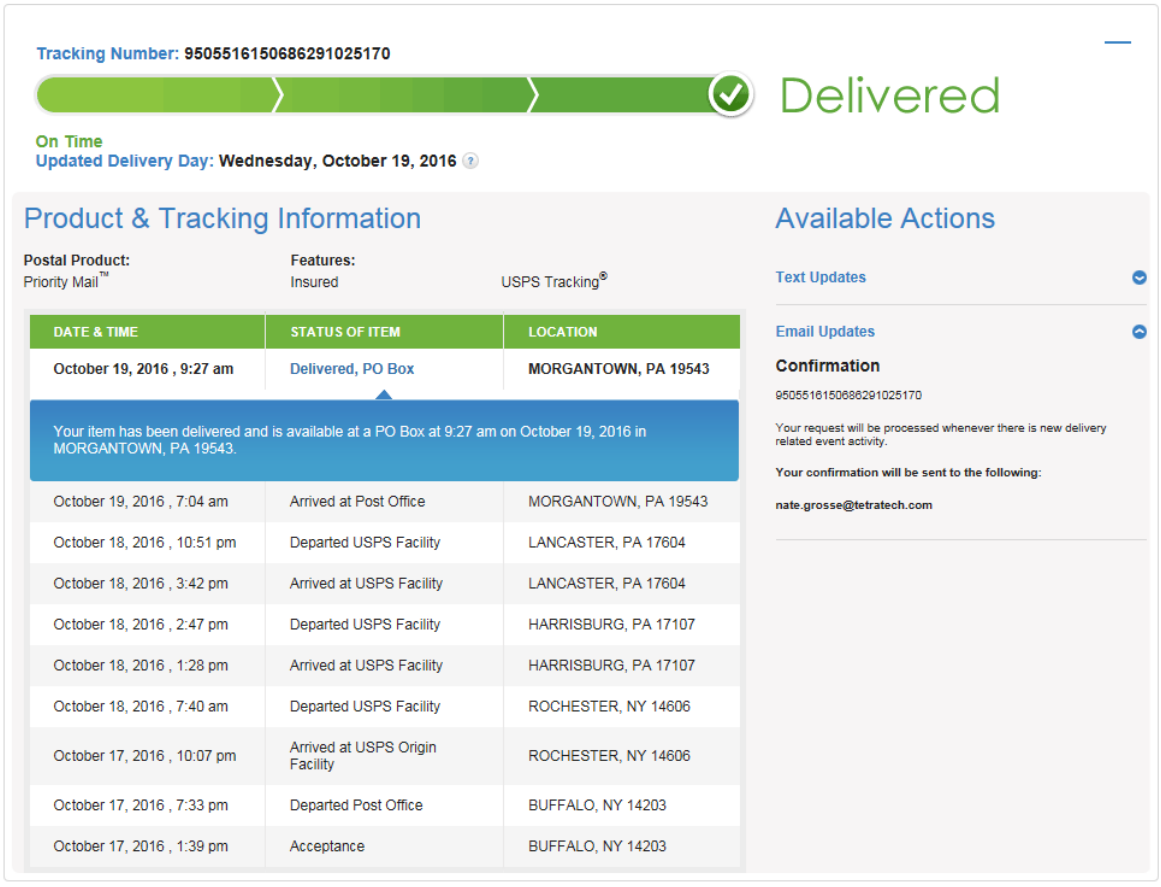

Tracking Number: 9505516150686291025170

Delivered

On Time
Updated Delivery Day: Wednesday, October 19, 2016

Product & Tracking Information

Postal Product:
Priority Mail™

Features:
Insured
USPS Tracking®

DATE & TIME	STATUS OF ITEM	LOCATION
October 19, 2016 , 9:27 am	Delivered, PO Box	MORGANTOWN, PA 19543
	Your item has been delivered and is available at a PO Box at 9:27 am on October 19, 2016 in MORGANTOWN, PA 19543.	
October 19, 2016 , 7:04 am	Arrived at Post Office	MORGANTOWN, PA 19543
October 18, 2016 , 10:51 pm	Departed USPS Facility	LANCASTER, PA 17604
October 18, 2016 , 3:42 pm	Arrived at USPS Facility	LANCASTER, PA 17604
October 18, 2016 , 2:47 pm	Departed USPS Facility	HARRISBURG, PA 17107
October 18, 2016 , 1:28 pm	Arrived at USPS Facility	HARRISBURG, PA 17107
October 18, 2016 , 7:40 am	Departed USPS Facility	ROCHESTER, NY 14606
October 17, 2016 , 10:07 pm	Arrived at USPS Origin Facility	ROCHESTER, NY 14606
October 17, 2016 , 7:33 pm	Departed Post Office	BUFFALO, NY 14203
October 17, 2016 , 1:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Confirmation

9505516150686291025170

Your request will be processed whenever there is new delivery related event activity.

Your confirmation will be sent to the following:

nate.grosse@tetratech.com



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 1,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Mangia Mangia	Telephone: 570-689-3794
Contact name:	Natale Amato	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Natale Amato at Mangia Mangia on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:46 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206256855 Delivered

Your package has been delivered

Tracking # 778206256855

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:43 am

c/o Natale Amato
Mangia Mangia
2981 Elizabethtown Road
HERSHEY, PA 17033
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206256855
Status:	Delivered: 01/19/2017 09:43 AM Signed for By: S.SPAIN
Reference:	112IC05958, 16
Signed for by:	S.SPAIN
Delivery location:	HERSHEY, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:46 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MANGIA MANGIA
c/o Natale Amato
2981 Elizabethtown Road
Hershey, PA 17033

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Manor GC Telephone: 610-678-9597
Contact name:	Michael Heckman
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Michael Heckman at Manor GC on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:41 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204961324 Delivered

Your package has been delivered

Tracking # 778204961324

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:35 am

c/o Michael Heckman
Manor Gc
153 Bran Road
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204961324
Status:	Delivered: 01/19/2017 10:35 AM Signed for By: H.HECKMAN
Reference:	112IC05958, 16
Signed for by:	H.HECKMAN
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:41 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MANOR GC
c/o Michael Heckman
153 Bran Road
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Maple Grove Park Telephone: 610-856-7200
Contact name:	Mark Stauffer
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Mark Stauffer at Maple Grove Park on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:06 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778204997553 Delivered

Your package has been delivered

Tracking # 778204997553

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:59 am

c/o Mark Stauffer
Maple Grove Park
30 Stauffer Park Lane
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778204997553
Status:	Delivered: 01/19/2017 09:59 AM Signed for By: A.BEAGLE
Reference:	112IC05958, 16
Signed for by:	A.BEAGLE
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:05 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MAPLE GROVE PARK
c/o Mark Stauffer
30 Stauffer Park Lane
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Marsh Creek State Park	Telephone: 610-458-5180
Contact name:	Lorry Nygard	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Lorry Nygard at Marsh Creek State Park on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:13 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205980164 Delivered

Your package has been delivered

Tracking # 778205980164

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:10 am

c/o Lorry Nygard
Marsh Creek State Park
675 Park Road
DOWNINGTOWN, PA 19335
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205980164
Status:	Delivered: 01/19/2017 10:10 AM Signed for By: G.STRONK
Reference:	112IC05958, 16
Signed for by:	G.STRONK
Delivery location:	DOWNINGTOWN, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:13 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MARSH CREEK STATE PARK
c/o Lorry Nygard
675 Park Road
Downingtown, PA 19335

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Mun Auth of Westmoreland County-McKeesport	Telephone: 412-678-6065
Contact name:	Sarah Restivo	
From:	Josh Baird (Tt)	
Date:	February 4, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Sarah Restivo at Mun Auth of Westmoreland County-McKeesport on February 4th, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on February 6th, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: EL621497560US

Scheduled Delivery Day: Monday, February 6, 2017, 3:00 pm
Money Back Guarantee
Signed for By: WAIVED // GREENSBURG, PA 15601 // 8:09 am

Product & Tracking Information

Postal Product:
Priority Mail Express 2-Day™

Features:
Insured
Up to $100 insurance included
Restrictions Apply
PO to Addressee

DATE & TIME	STATUS OF ITEM	LOCATION
February 6, 2017 , 8:09 am	**Delivered, PO Box**	**GREENSBURG, PA 15601**
Your item has been delivered and is available at a PO Box at 8:09 am on February 6, 2017 in GREENSBURG, PA 15601. Waiver of signature was exercised at time of delivery.		
February 6, 2017 , 6:15 am	Arrived at Post Office	GREENSBURG, PA 15601
February 5, 2017 , 11:17 pm	Arrived at USPS Destination Facility	PITTSBURGH, PA 15290
February 5, 2017 , 5:20 pm	In Transit to Destination	
February 4, 2017 , 5:20 pm	Arrived at USPS Origin Facility	ROCHESTER, NY 14692
February 4, 2017 , 2:19 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
February 4, 2017 , 11:32 am	Acceptance	BUFFALO, NY 14203

Available Actions

Proof of Delivery

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard. No tracking numbers necessary.

Sign up for My USPS ›

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

February 4th, 2017

Mun Auth of Westmoreland County-McKeesport
c/o Sarah Restivo
P.O. Box 730
Greensburg, PA 15601

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by February 14th, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned.**

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Meadowbrook Mhp	Telephone: 717-774-8887
Contact name:	Ryan Flynn	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ryan Flynn at Meadowbrook Mhp on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:18 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275895977 Delivered

Your package has been delivered

Tracking # 777275895977

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:15 am

Ryan Flynn
Meadowbrook MHP
184 Meadowbrook Court
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275895977
Status:	Delivered: 09/21/2016 11:15 AM Signed for By: J.PEREZ
Reference:	112IC05958, 16
Signed for by:	J.PEREZ
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Residence
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
	Residential Delivery
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:17 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.


MEADOWBROOK MHP
CUMBERLAND COUNTY
YORK COUNTY
FAIRVIEW
LOWER ALLEN
Sheepford Rd
Rudytown Rd
Old Forge Rd
Thompsons Ln
Bethel Church Rd
Stiles Rd
Nuss Rd
Pleasant View Dr
Pine Tree Dr
Oak Dr
Meyers Dr
Lindenhurst Rd
Carlisle Rd
Valley Rd
Stone Hill Rd
Whitetail Rd
Hunt Dr
Chrysanthemum Cir
Fairway Dr
Bayberry Cir
Oak Ridge Rd
Old Sheep Rd
Nuss Ln
Rudytown Rd
Bethel Church Rd
Old Forge Rd
Sheepford Rd
Thompsons Ln
Sheepford Rd
Old Forge Rd
Old Forge Rd
Old Forge

TETRA TECH

Contact Report

To:	Middlecreek Wildlife Mgmt Area	Telephone: 717-733-1512
Contact name:	Jim Binder	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Jim Binder at Middlecreek Wildlife Mgmt Area on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7798

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com®*.

KLEINFELTERSVILLE, PA 17039

OFFICIAL USE

Certified Mail Fee	$3.30
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
Total Postage and Fees	$4.87

0205
21

Postmark Here

01/19/2017

Sent To
Street and A
City, State, Z

MIDDLECREEK WILDLIFE MGMT. AREA
c/o JIM BINDER
P.O. BOX 110
KLEINFELTERSVILLE, PA 17039

PS Form 3
ions

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237798

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 24, 2017 , 2:11 pm	**Delivered**	**KLEINFELTERSVILLE, PA 17039**
Your item was delivered at 2:11 pm on January 24, 2017 in KLEINFELTERSVILLE, PA 17039.		
January 24, 2017 , 5:29 am	In Transit to Destination	
January 22, 2017 , 10:29 pm	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:54 am	In Transit to Destination	
January 21, 2017 , 8:54 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

HELPFUL LINKS
Contact Us
Site Index
FAQs

ON ABOUT.USPS.COM
About USPS Home
Newsroom
USPS Service Updates
Forms & Publications
Government Services
Careers

OTHER USPS SITES
Business Customer Gateway
Postal Inspectors
Inspector General
Postal Explorer
National Postal Museum
Resources for Developers

LEGAL INFORMATION
Privacy Policy
Terms of Use
FOIA
No FEAR Act EEO Data

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

January 18th, 2017

MIDDLECREEK WILDLIFE MGMT AREA
c/o Jim Binder
P.O.Box 110
Kleinfeltersville, PA 17039

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Middlesex Twp Muni Auth	Telephone: 717-243-0674
Contact name:	Rory L. Morrison	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Rory L. Morrison at Middlesex Twp Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:52 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275911749 Delivered

Your package has been delivered

Tracking # 777275911749

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 12:49 pm

Rory L. Morrison
Middlesex Twp Muni. Authority
350 N. Middlesex Road, Suite 2
CARLISLE, PA 17013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275911749
Status:	Delivered: 09/21/2016 12:49 PM Signed for By: R.KOCH
Reference:	112IC05958, 16
Signed for by:	R.KOCH
Delivery location:	CARLISLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:51 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

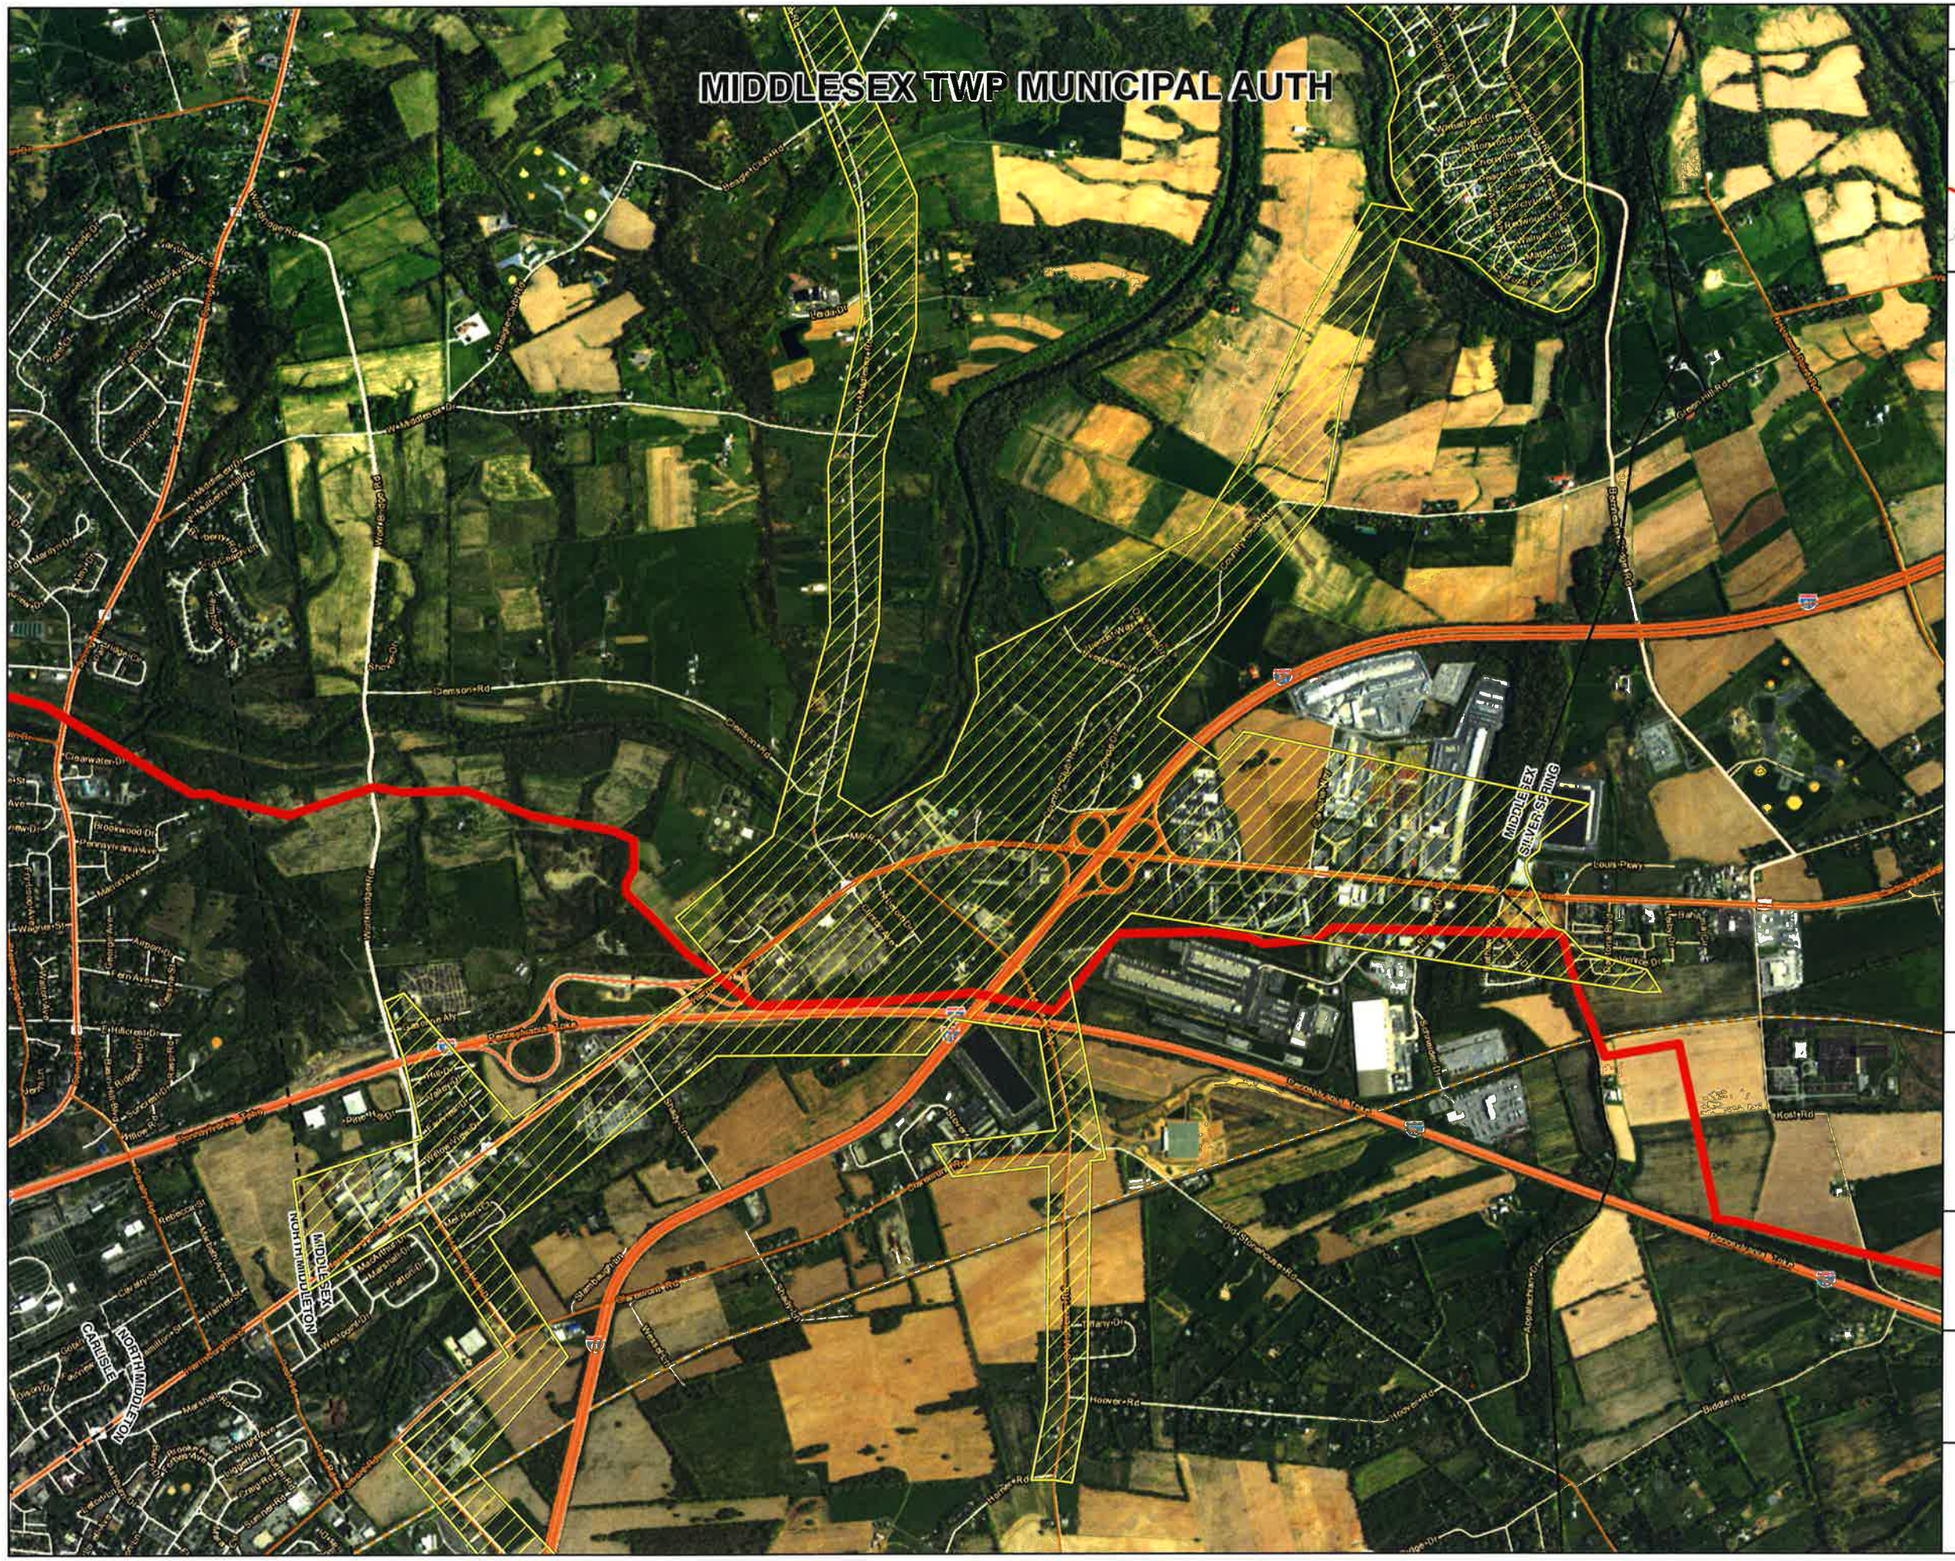

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Middletown Boro Water Auth	Telephone: 717-948-3055
Contact name:	Daniel Standish	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Daniel Standish at Middletown Boro Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:48 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275924061 Delivered

Your package has been delivered

Tracking # 777275924061

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 10:43 am

Daniel Standish
Middletown Boro. Water Authority
453 South Lawrence Street
MIDDLETOWN, PA 17057
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275924061
Status:	Delivered: 09/21/2016 10:43 AM Signed for By: W.SHAEFFER
Reference:	112IC05958, 16
Signed for by:	W.SHAEFFER
Delivery location:	MIDDLETOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:48 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

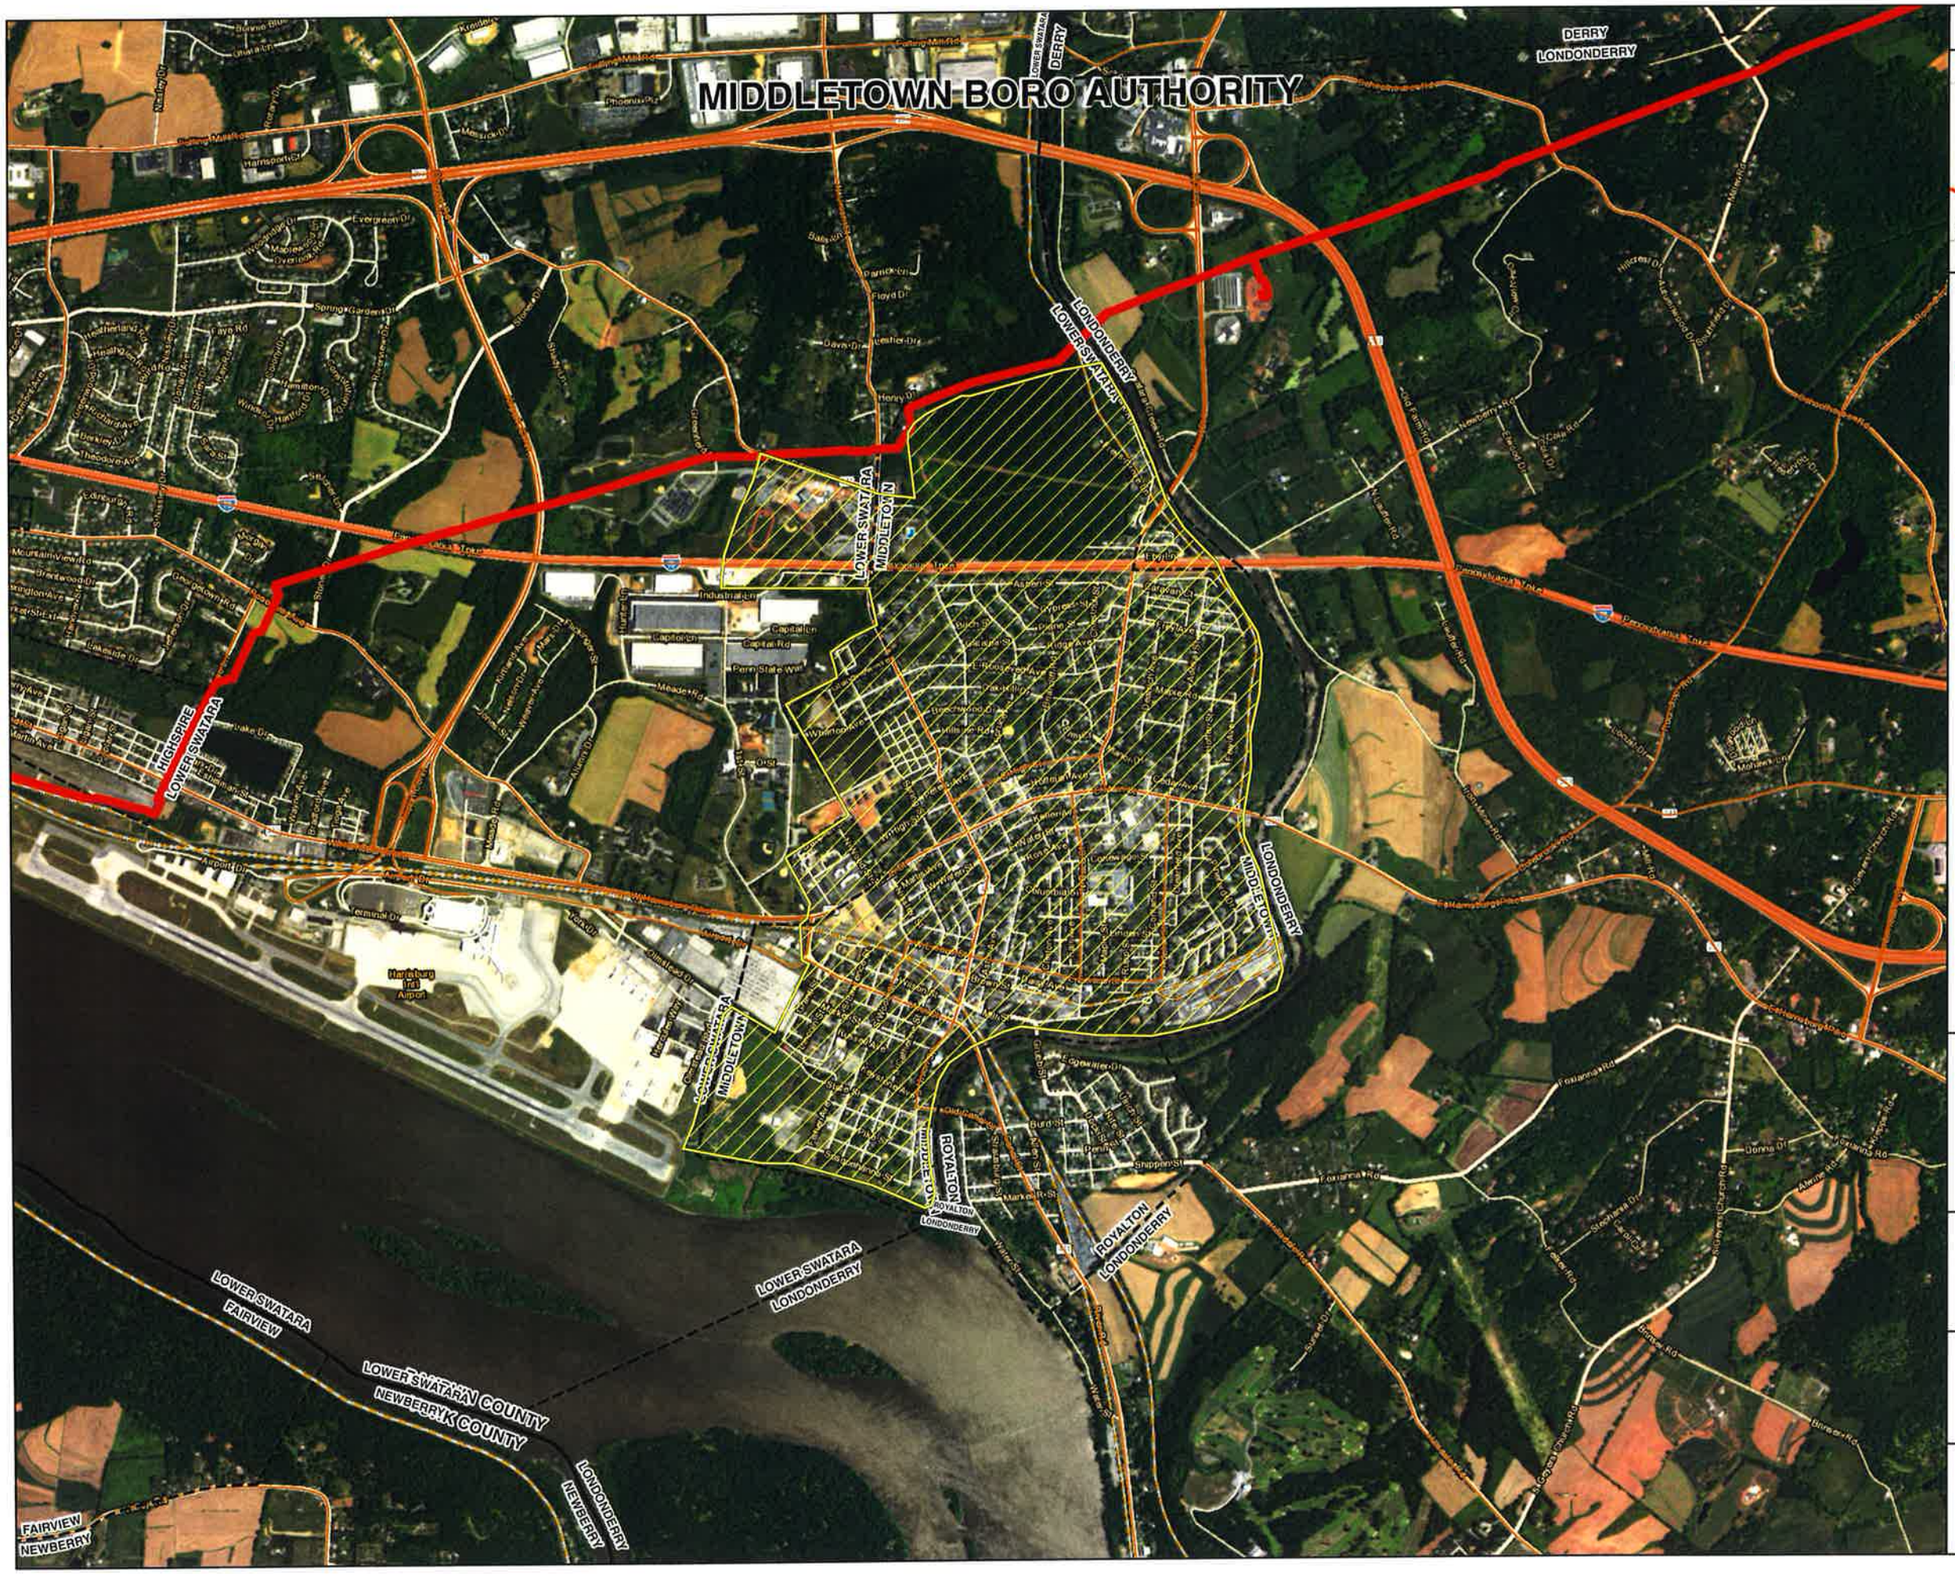

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:
Sunoco Pipeline L.P.

Prepared By:
TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Mohnton Fish & Game Assn Telephone: 610-775-3470
Contact name:	Barbara Reisch
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Barbara Reisch at Mohnton Fish & Game Assn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 1:28 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205018820 Delivered

Your package has been delivered

Tracking # 778205018820

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 1:25 pm

c/o Barbara Reisch
Mohnton Fish & Game Assn
100 Gun Club Lane
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205018820
Status:	Delivered: 01/19/2017 1:25 PM Signed for By: D.NAUGLE
Door Tag number:	DT104558953083
Reference:	112IC05958, 16
Signed for by:	D.NAUGLE
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:28 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MOHNTON FISH & GAME ASSN
c/o Barbara Reisch
100 Gun Club Lane
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Morgantown Prop Telephone: 610-913-7516
Contact name:	Frank Eisenhauer
From:	Josh Baird (Tt)
Date:	January 17, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Frank Eisenhauer at Morgantown Prop on January 17, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 18, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Wednesday, January 18, 2017 10:09 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778194829254 Delivered

Your package has been delivered

Tracking # 778194829254

Ship date:
Tue, 1/17/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 1/18/2017 10:05 am

Frank Eisenhauer
Morgantown Prop
75 Grace Blvd, Building D
MORGANTOWN, PA 19543
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778194829254
Status:	Delivered: 01/18/2017 10:05 AM Signed for By: R.RAQUET
Reference:	112IC05958, 16
Signed for by:	R.RAQUET
Delivery location:	MORGANTOWN, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/18/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:08 AM CST on 01/18/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MORGANTOWN PROP
c/o Frank Eisenhauer
75 Grace Blvd. Building D
Morgantown, PA 19543

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Mountain View Apartments	Telephone: 717-484-0973
Contact name:	Robert Nass	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Robert Nass at Mountain View Apartments on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Bob Nass left a voicemail for Tetra Tech on January 19, 2017 confirming he received the FedEx shipment. He also indicated he is a partner of Sunoco and owns approximately 40 acres in the area near the country club. The map he received does not denote the area where he is. He requested a correct map so he can comment on it. His contact information is robertanass@gmail.com, 904-614-2244.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:01 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206667990 Delivered

Your package has been delivered

Tracking # 778206667990

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:58 am

c/o Robert Nass
Mountain View Apartments
905 Biscayne Blvd
Suite 1
DELAND, FL 32724
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206667990
Status:	Delivered: 01/19/2017 09:58 AM Signed for By: H.SWAN
Reference:	112IC05958, 16
Signed for by:	H.SWAN
Delivery location:	DELAND, FL
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:01 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

MOUNTAIN VIEW APARTMENTS
c/o Robert Nass
905 Biscayne Blvd Suite 1
Deland, FL 32724

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	N. Middleton Water Auth	Telephone: 717-243-8269
Contact name:	E. Lee Koch	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to E. Lee Koch at N. Middleton Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:16 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275936709 Delivered

Your package has been delivered

Tracking # 777275936709

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 11:06 am

E Lee Koch
N. Middleton Water Authority
240 Clearwater Drive
CARLISLE, PA 17013
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275936709
Status:	Delivered: 09/21/2016 11:06 AM Signed for By: B.MILLER
Reference:	112IC05958, 16
Signed for by:	B.MILLER
Delivery location:	CARLISLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:16 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Nolde Environmental Ed Ctr Telephone: 610-796-3699
Contact name:	Lisa Miller – Center Manager
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Lisa Miller at Nolde Environmental Ed Ctr on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 1:09 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205364128 Delivered

Your package has been delivered

Tracking # 778205364128

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 1:07 pm

c/o Lisa Miller, Center Manager
Nolde Environmental Ed Ctr
2910 New Holland Road
READING, PA 19607
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205364128
Status:	Delivered: 01/19/2017 1:07 PM Signed for By: A.KISSINGER
Reference:	100-NRS-T29725, 12
Signed for by:	A.KISSINGER
Delivery location:	READING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:08 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

NOLDE ENVIRONMENTAL ED CTR
c/o Lisa Miller, Center Manager
2910 New Holland Road
Reading, PA 19607

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	North Lanc Co Game & Fish Assn	Telephone: 717-949-6977
Contact name:	Lon Ensinger	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Lon Ensinger at North Lanc Co Game & Fish Assn on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:05 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206688690 Delivered

Your package has been delivered

Tracking # 778206688690

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 10:56 am

c/o Lon Ensinger
North Lanc Co Game & Fish Assn
180 Forest Road
DENVER, PA 17517
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206688690
Status:	Delivered: 01/19/2017 10:56 AM Signed for By: B.ENSINGER
Door Tag number:	DT104524556657
Reference:	112IC05958, 16
Signed for by:	B.ENSINGER
Delivery location:	DENVER, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:05 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

NORTH LANC CO GAME & FISH ASSN
c/o Lon Ensinger
180 Forest Road
Denver, PA 17517

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	PA Amer Water Co - Indiana Telephone: 724-465-6600
Contact name:	Sherri Medivitz
From:	Josh Baird (Tt)
Date:	September 20, 2016
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Sherri Medivitz at PA Amer Water Co - Indiana on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 2:03 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276007027 Delivered

Your package has been delivered

Tracking # 777276007027

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 2:00 pm

Sherri Medivitz
PA American Water Co - Indiana
1034 Waterworks Road
INDIANA, PA 15701
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276007027
Status:	Delivered: 09/21/2016 2:00 PM Signed for By: H.MCANULTY
Reference:	112IC05958, 16
Signed for by:	H.MCANULTY
Delivery location:	INDIANA, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 1:02 PM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

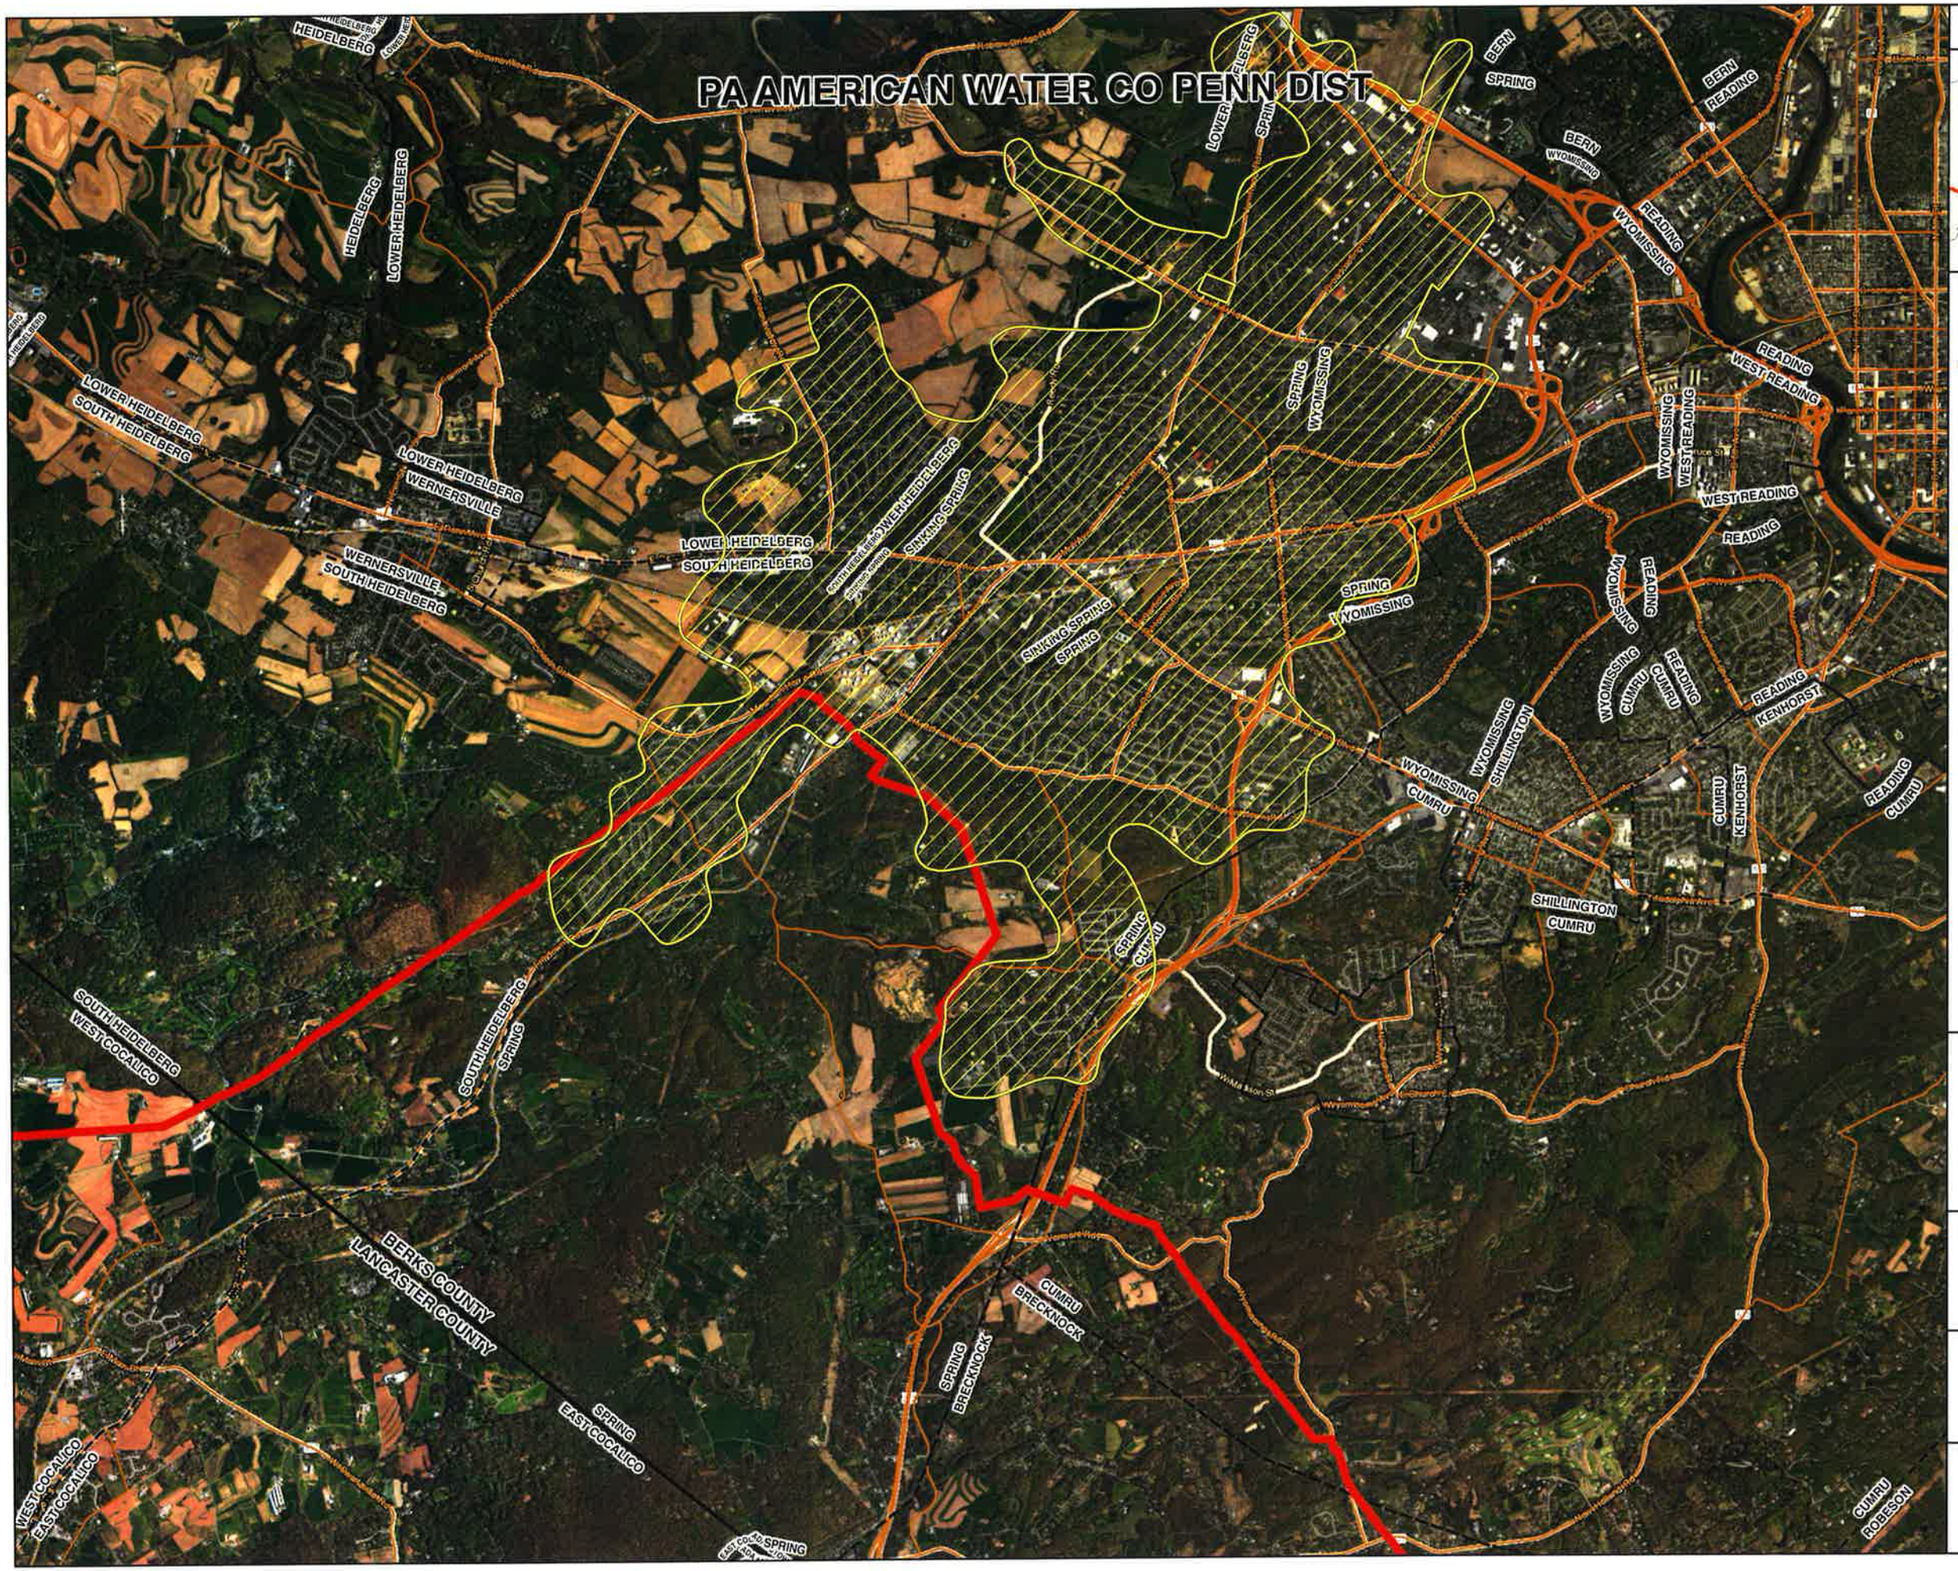

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:
Sunoco Pipeline L.P.

Prepared By:
TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	PA Amer Water Co - Pittsburgh	Telephone: 724-437-0102
Contact name:	Not available	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to PA Amer Water Co – Pittsburgh on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:55 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275992341 Delivered

Your package has been delivered

Tracking # 777275992341

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US

Delivered

Delivery date:
Wed, 9/21/2016 11:47 am

PA Amer. Water Co - Pittsburgh
560 Horning Road
BETHEL PARK, PA 15102
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275992341
Status:	Delivered: 09/21/2016 11:47 AM Signed for By: E.BELLMAN
Reference:	112IC05958, 16
Signed for by:	E.BELLMAN
Delivery location:	BETHEL PARK, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:54 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

PA AMERICAN WATER CO PITTSBURGH DIST

ALLEGHENY COUNTY
WASHINGTON COUNTY
WESTMORELAND COUNTY
FAYETTE COUNTY

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 15,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	PA Amer Water Co West	Telephone: 717-774-7460
Contact name:	Shawn Wiley	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Shawn Wiley at PA Amer Water Co West on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:39 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275978212 Delivered

Your package has been delivered

Tracking # 777275978212

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:36 am

Shawn Wiley
PA Amer. Water Co - West
275 Steigerwalt Hollow Road
NEW CUMBERLAND, PA 17070
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275978212
Status:	Delivered: 09/21/2016 11:36 AM Signed for By: T.THOTTO
Reference:	112IC05958, 16
Signed for by:	T.THOTTO
Delivery location:	NEW CUMBERLAND, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Direct Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:38 AM CDT on 09/21/2016.

All weights are estimated.


To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

PA AMERICAN WATER CO HERSHEY DIST

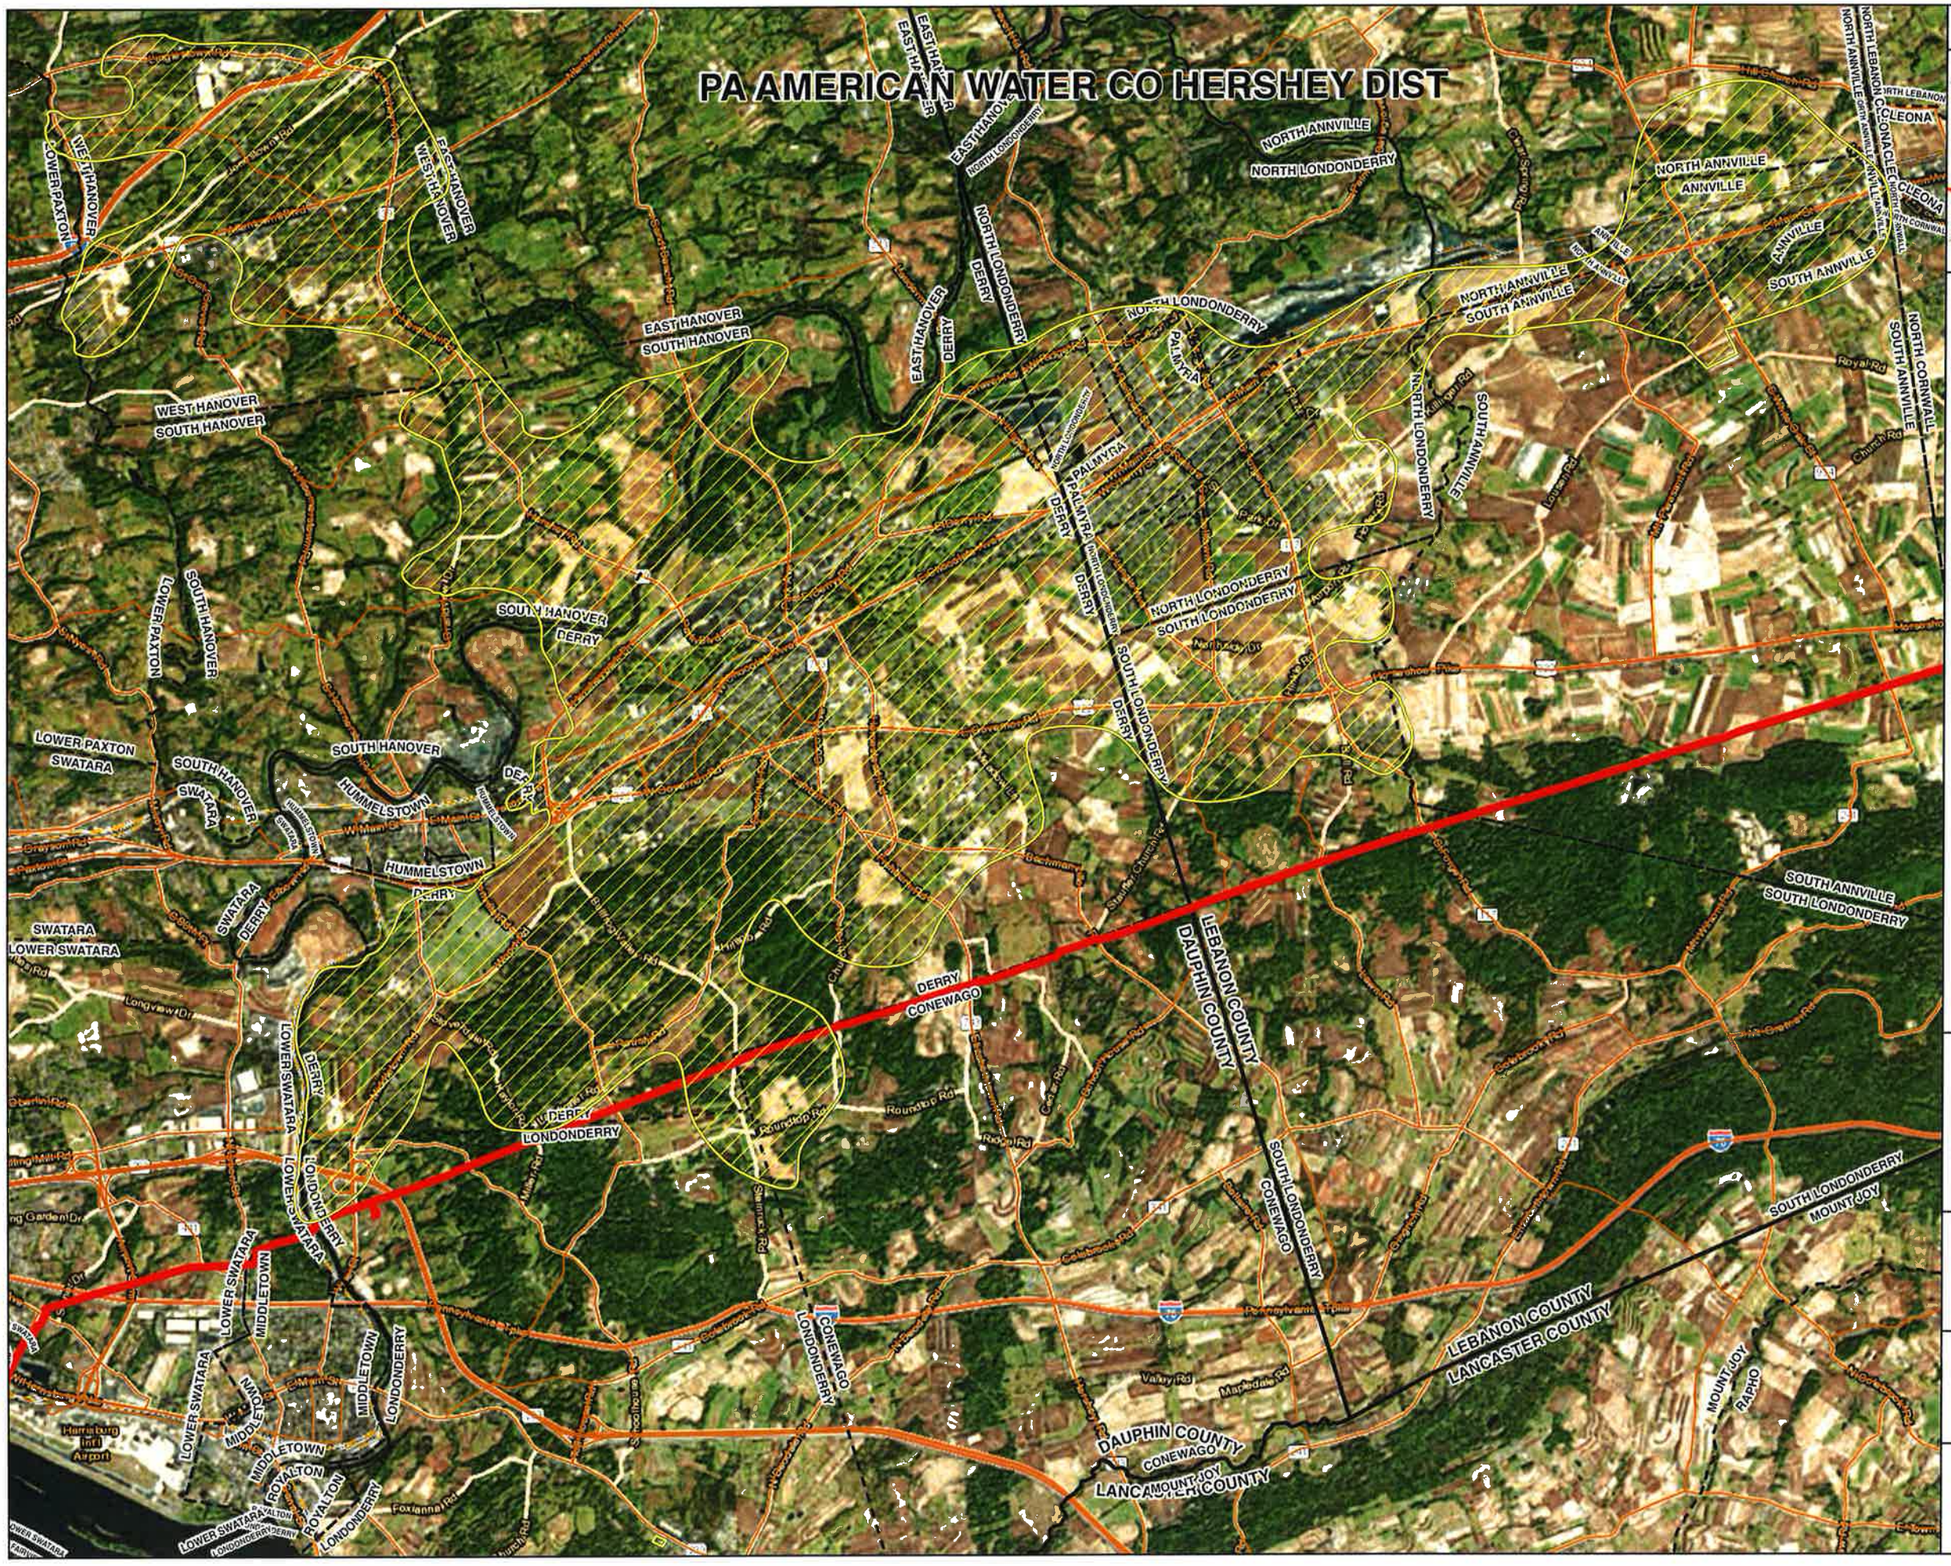

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 9,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	PA Amer Water Co	Telephone: 717-533-5627
Contact name:	Justin Brame	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Justin Brame at PA Amer Water Co on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:48 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777275949238 Delivered

Your package has been delivered

Tracking # 777275949238

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:45 am

Justin Brame
PA Amer. Water Company
200 East Canal Street
HUMMELSTOWN, PA 17036
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777275949238
Status:	Delivered: 09/21/2016 11:45 AM Signed for By: T.PATRICK
Reference:	112IC05958, 16
Signed for by:	T.PATRICK
Delivery location:	HUMMELSTOWN, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:47 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

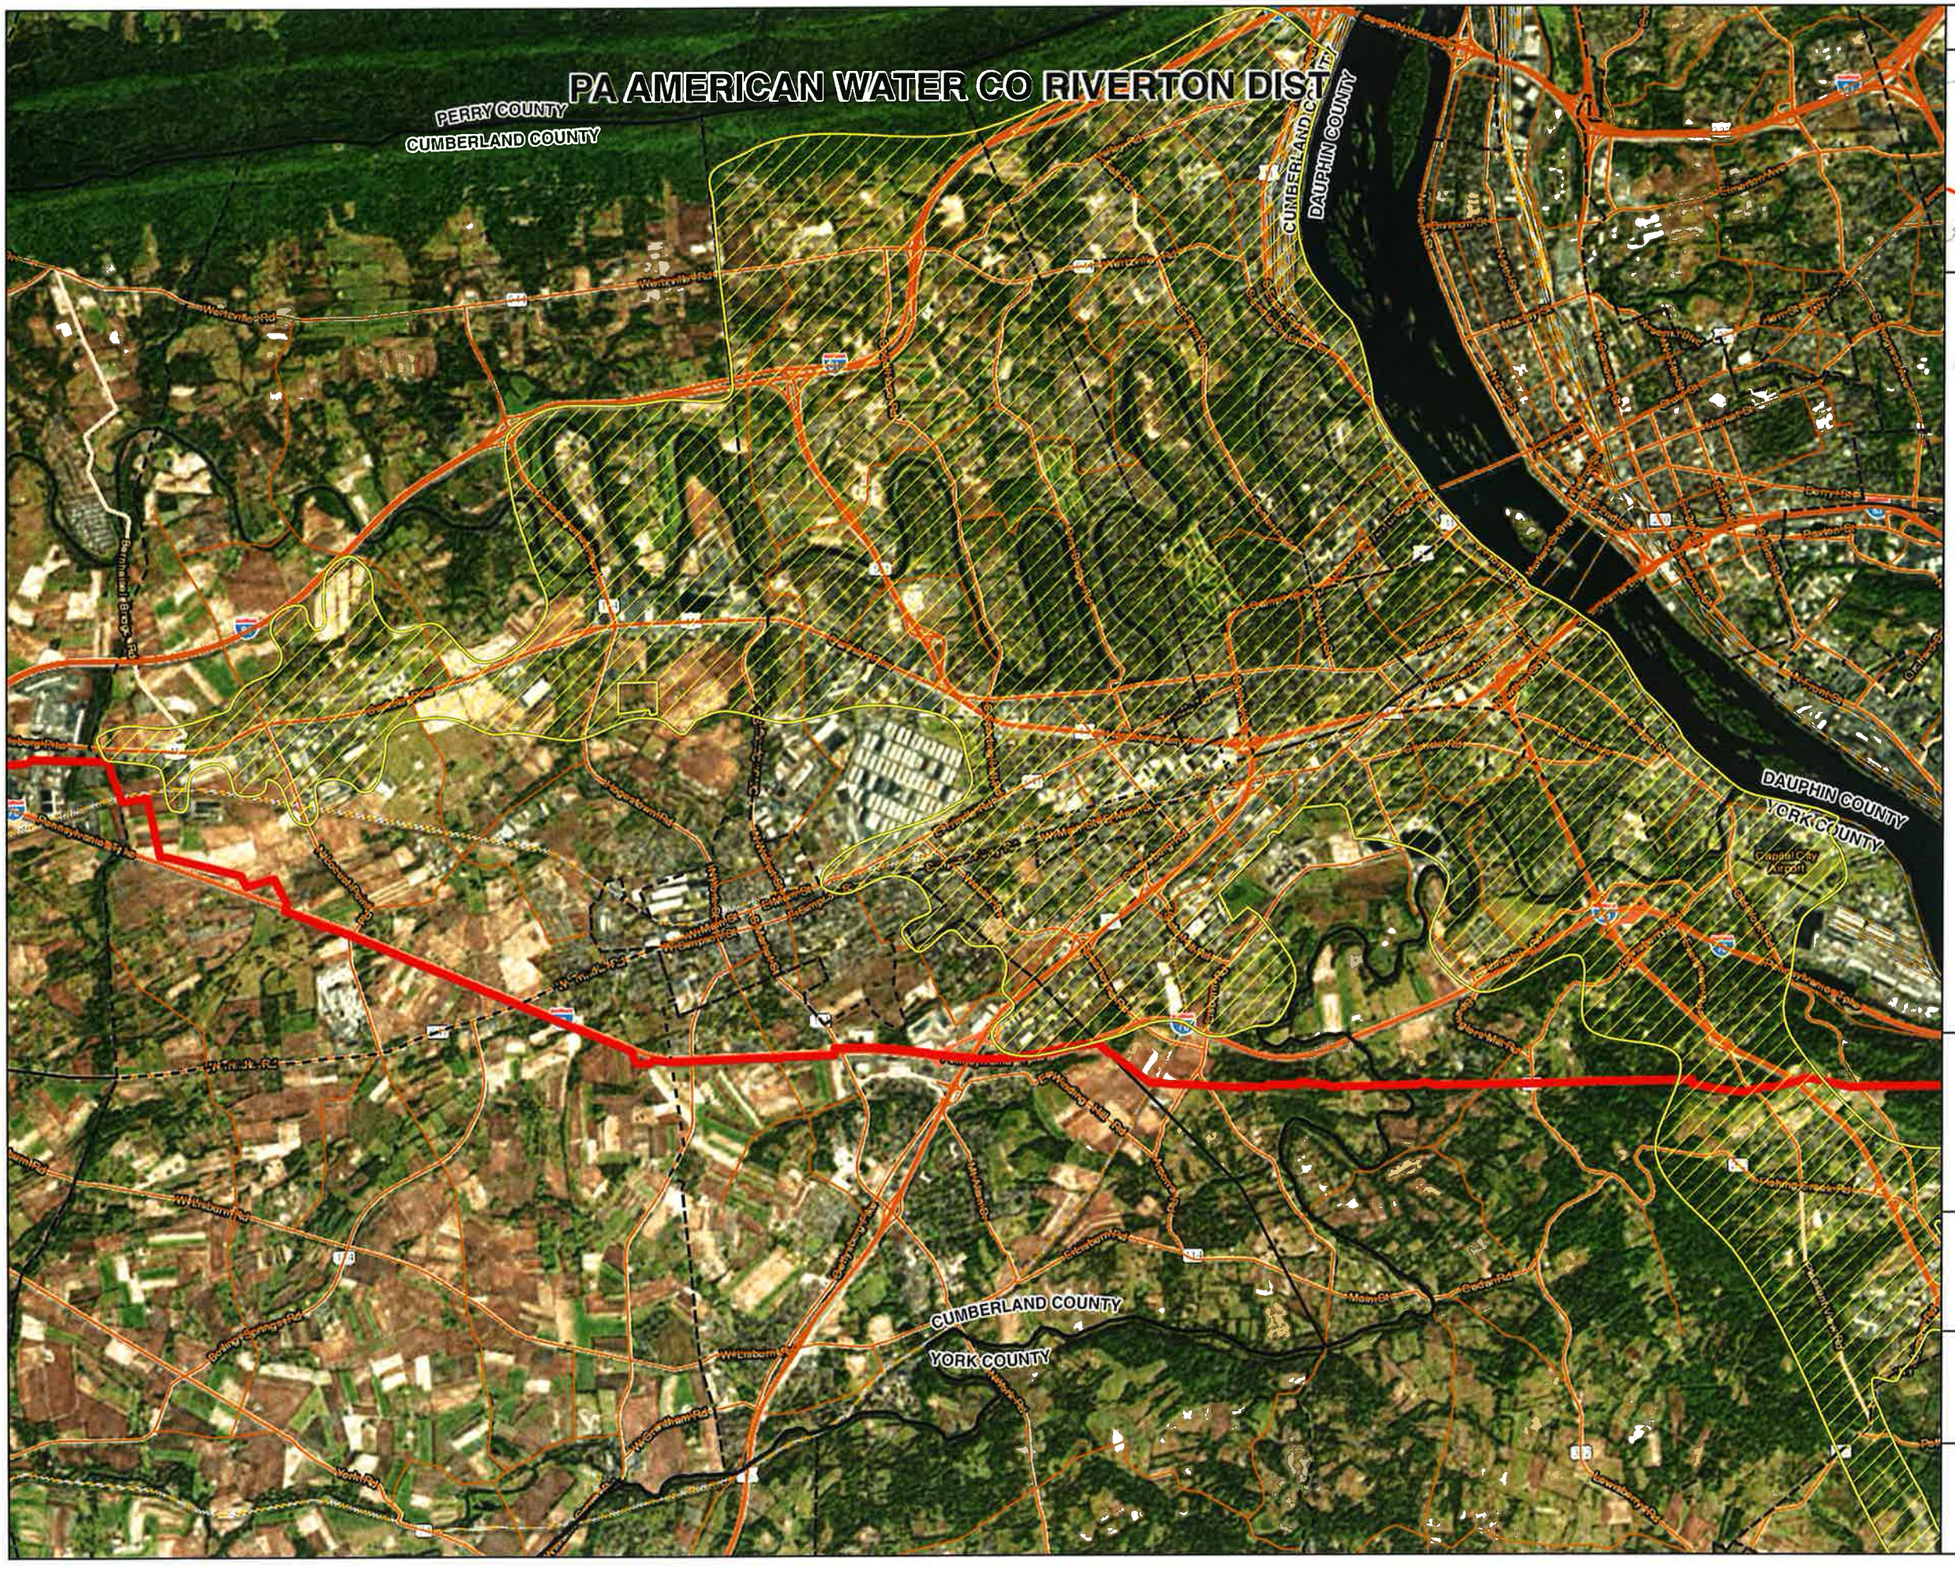

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 9,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Pathways Telephone: 610-459-9177
Contact name:	Gene Laird
From:	Josh Baird (Tt)
Date:	September 20, 2016
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Gene Laird at Pathways on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 1:05 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276017473 Delivered

Your package has been delivered

Tracking # 777276017473

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 1:02 pm

Gene Laird
Pathways
519 Station Road
WAWA, PA 19063
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276017473
Status:	Delivered: 09/21/2016 1:02 PM Signed for By: K.BONES
Reference:	112IC05958, 16
Signed for by:	K.BONES
Delivery location:	WAWA, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required
	Deliver Weekday

Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:05 PM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

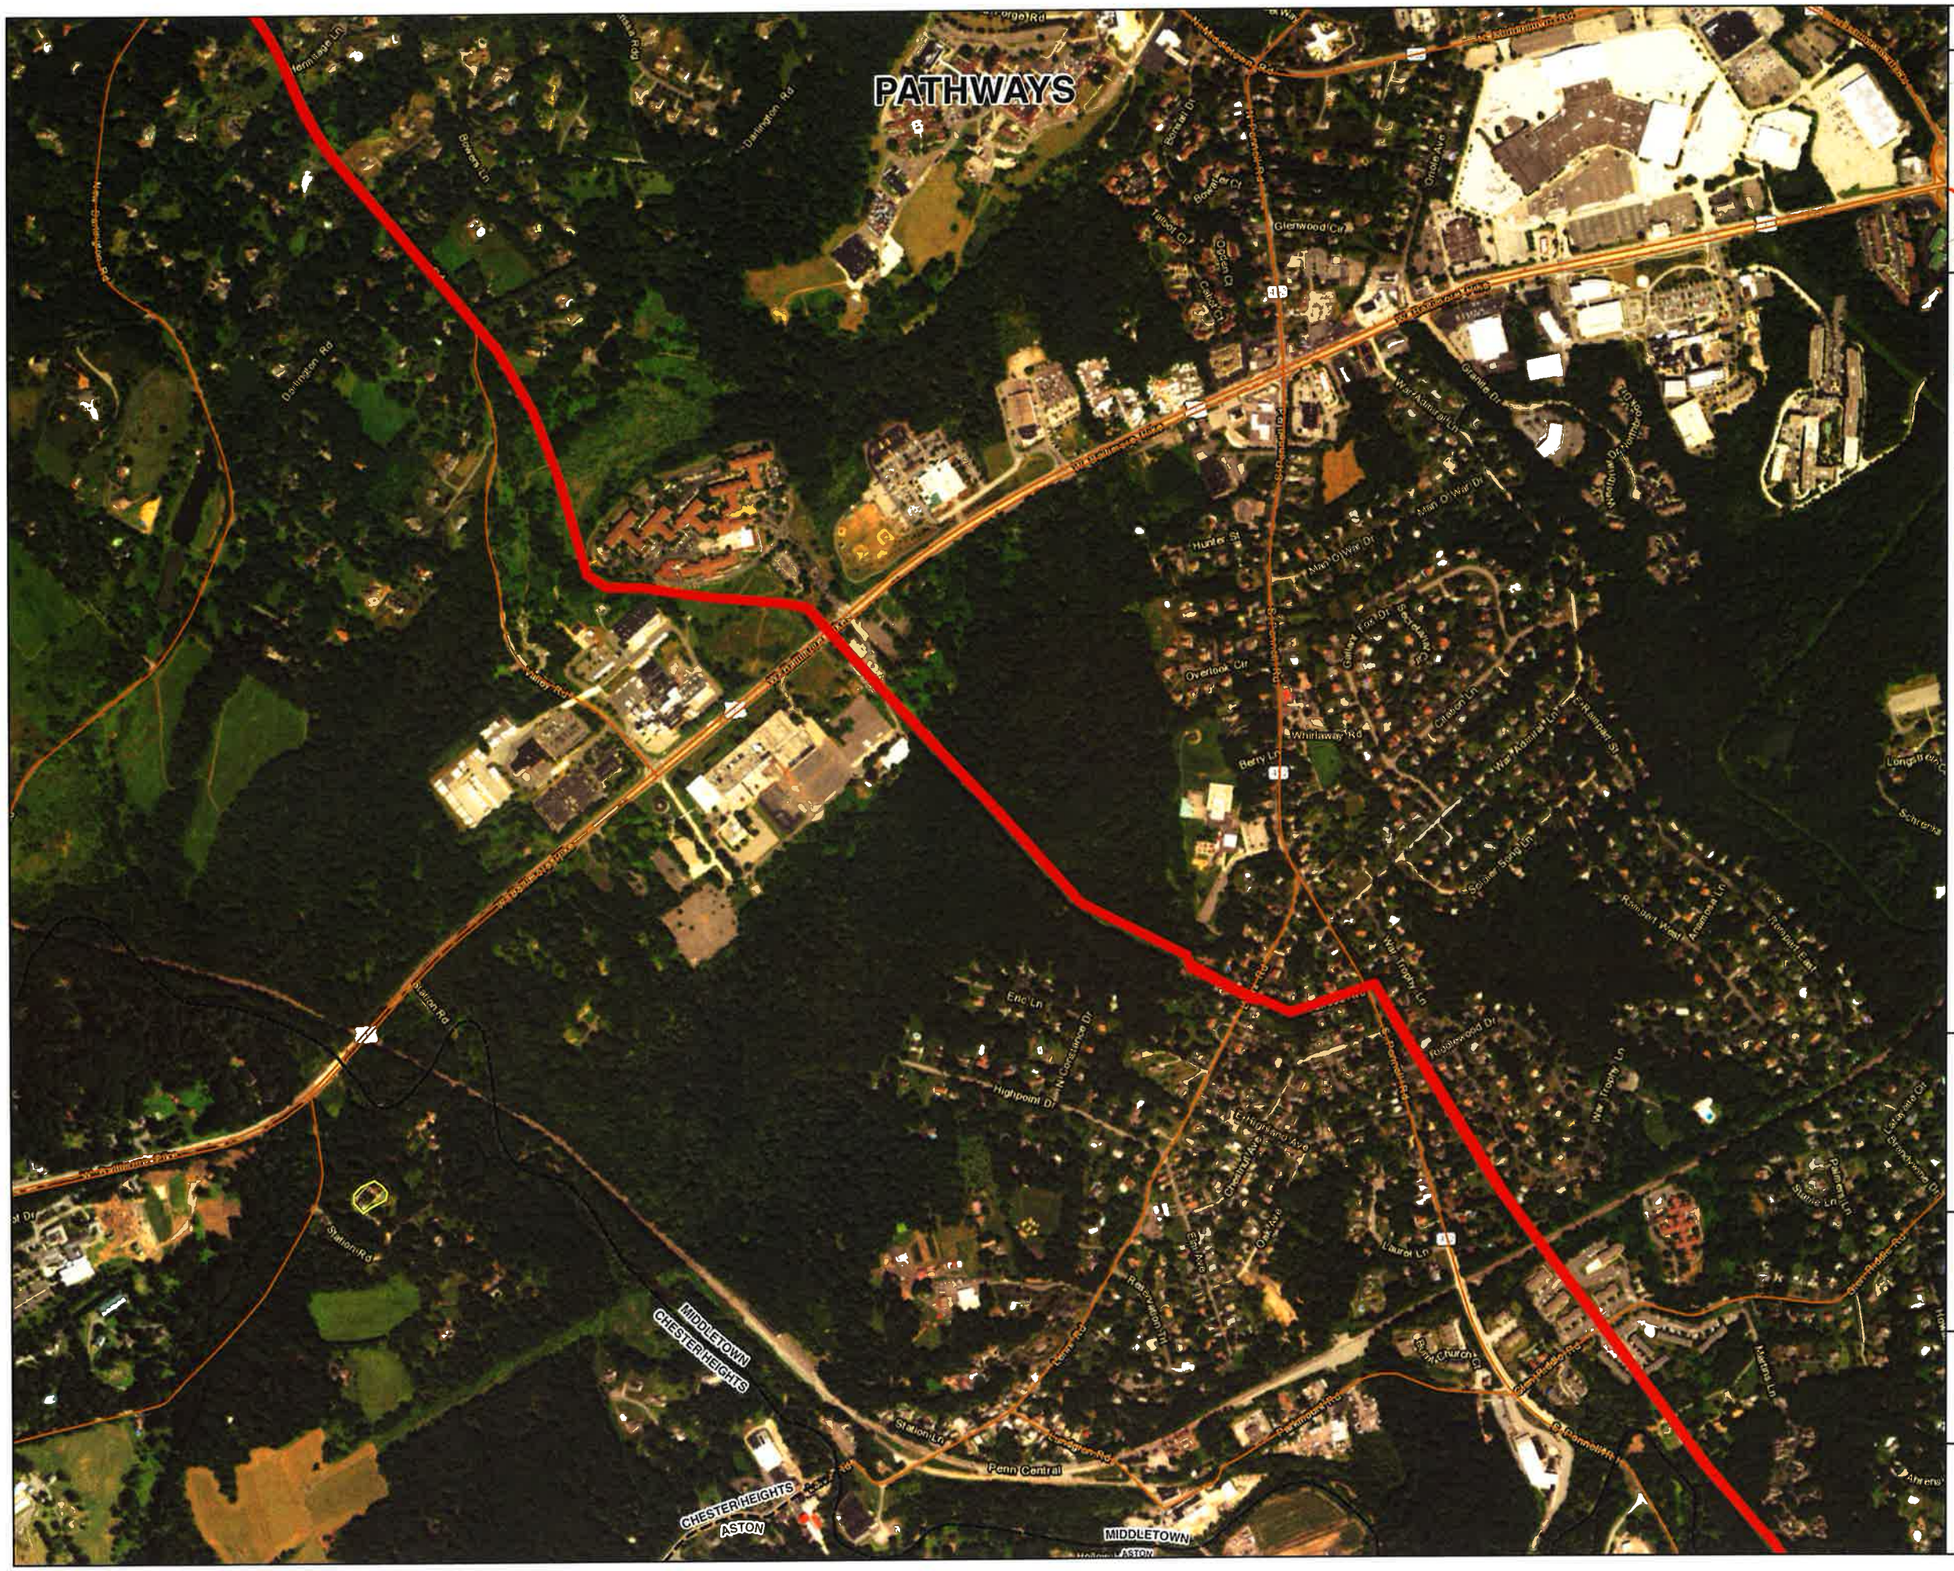

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:


TETRA TECH

Date:


9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

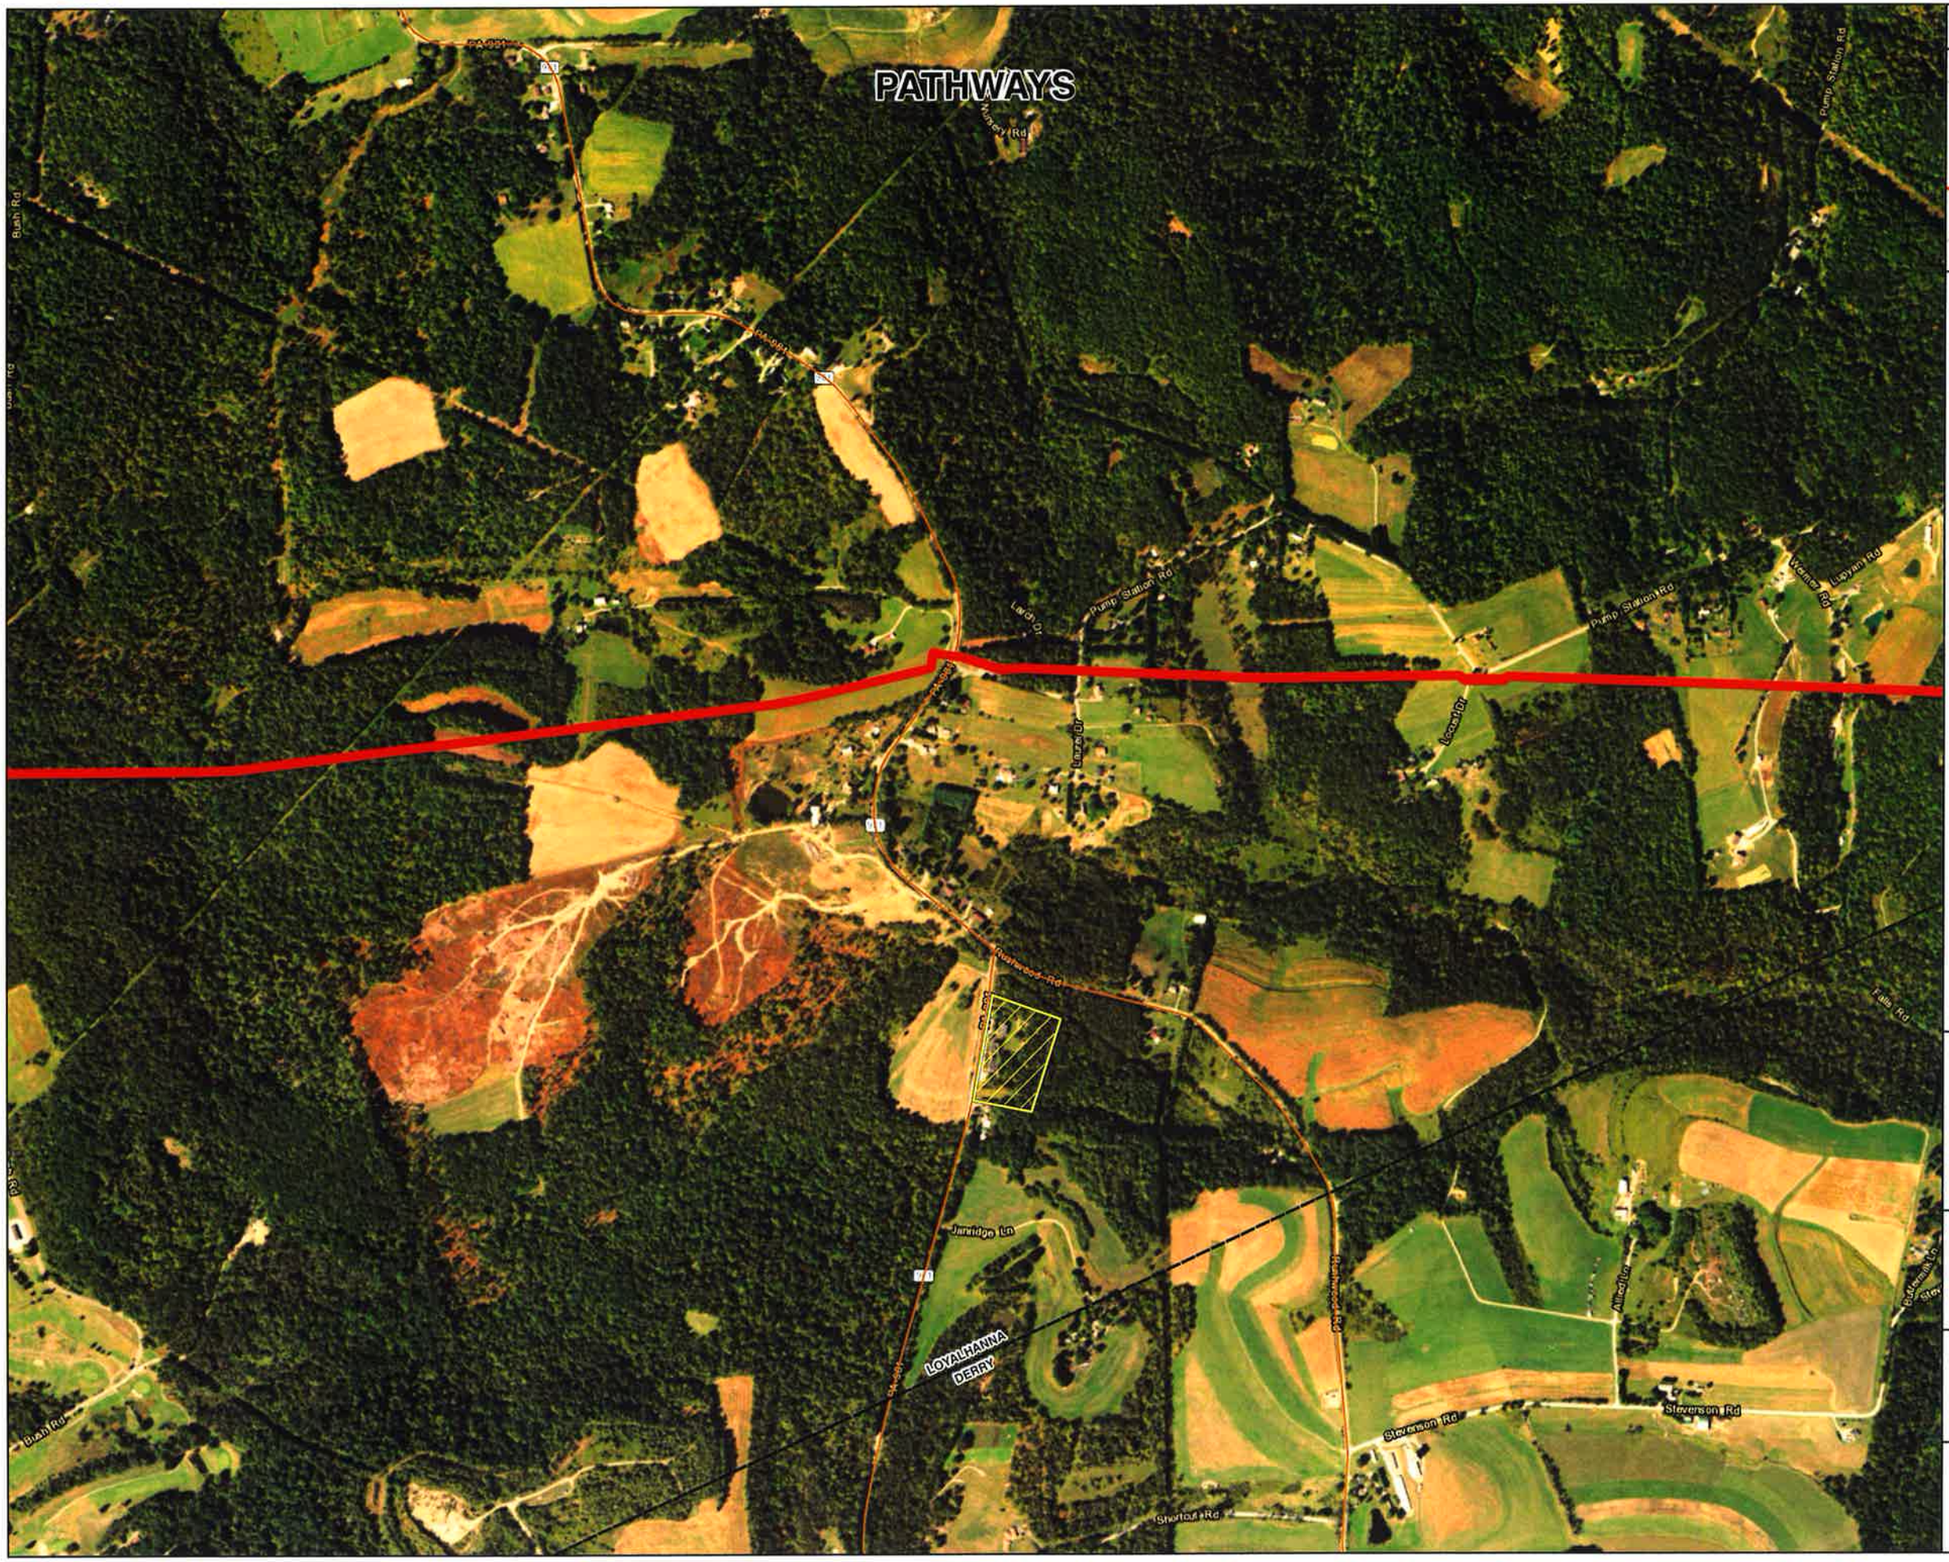

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Paw Penn District Telephone: 610-404-1540
Contact name:	Jennifer Milakeve
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Jennifer Milakeve at Paw Penn District on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:02 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205414516 Delivered

Your package has been delivered

Tracking # 778205414516

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:56 am

c/o Jennifer Milakeve
Paw Penn District
660 Lincoln Road
BIRDSBORO, PA 19508
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205414516
Status:	Delivered: 01/19/2017 09:56 AM Signed for By: M.HOFFMAN
Reference:	112IC05958, 16
Signed for by:	M.HOFFMAN
Delivery location:	BIRDSBORO, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:01 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

PAW PENN DISTRICT
c/o Jennifer Milakeve
660 Lincoln Road
Birdsboro, PA 19508

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Peter J. Camiel Service Plaza	Telephone: 610-286-0255
Contact name:	Michale Grafton	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Michale Grafton at Peter J. Camiel Service Plaza on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7712

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at *www.usps.com*®.

ELVERSON, PA 19520

OFFICIAL USE

Certified Mail Fee	$3.30
$	
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$ $0.00
☐ Return Receipt (electronic)	$ $0.00
☐ Certified Mail Restricted Delivery	$ $0.00
☐ Adult Signature Required	$ $0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
$	
Total Postage and Fees	$4.87
$	

0205
21

Postmark Here

ELVERSON STATION 19520

01/19/2017

Sent To
Street and
City, State
PS Form

PETER J. CAMIEL SERVICE PLAZA
c/o MICHALE GRAFTON
P.O. BOX 274
EAST NANTMEAL, PA 19520

tions

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237712

Updated Delivery Day: Tuesday, January 24, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 24, 2017 , 3:06 pm	**Delivered**	**ELVERSON, PA 19520**
Your item was delivered at 3:06 pm on January 24, 2017 in ELVERSON, PA 19520.		
January 24, 2017 , 8:53 am	Available for Pickup	ELVERSON, PA 19520
January 24, 2017 , 7:39 am	Arrived at Unit	ELVERSON, PA 19520
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

PETER J. CAMIEL SERVICE PLAZA
c/o Michale Grafton
P.O. Box 274
East Nantmeal, PA 19520

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Phat Alberts Telephone: 717-653-8501
Contact name:	Segio Oneglia
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Segio Oneglia at Phat Alberts on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Friday, January 20, 2017 12:57 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778207113890 Delivered

Your package has been delivered

Tracking # 778207113890

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Fri, 1/20/2017 12:54 pm

c/o Segio Oneglia
Phat Alberts
761 Lewisberry Rd
LEWISBERRY, PA 17339
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778207113890
Status:	Delivered: 01/20/2017 12:54 PM Signed for By: C.SERGIO
Reference:	112IC05958, 16
Signed for by:	C.SERGIO
Delivery location:	LEWISBERRY, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:56 AM CST on 01/20/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

PHAT ALBERTS
c/o Segio Oneglia
761 Lewisberry Rd
Lewisberry, PA 17339

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Pine Garden Apartments	Telephone: 724-875-0882
Contact name:	Paul Miller	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Paul Miller at Pine Garden Apartments on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 12:01 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276027382 Delivered

Your package has been delivered

Tracking # 777276027382

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:59 am

Paul Miller
Pine Garden Apartments
11 Glenview Drive
GREENSBURG, PA 15601
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276027382
Status:	Delivered: 09/21/2016 11:59 AM Signed for By: P.MILLER
Reference:	112IC05958, 16
Signed for by:	P.MILLER
Delivery location:	GREENSBURG, PA
Delivered to:	Residence
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
	Residential Delivery
Standard transit:	9/21/2016 by 8:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:00 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

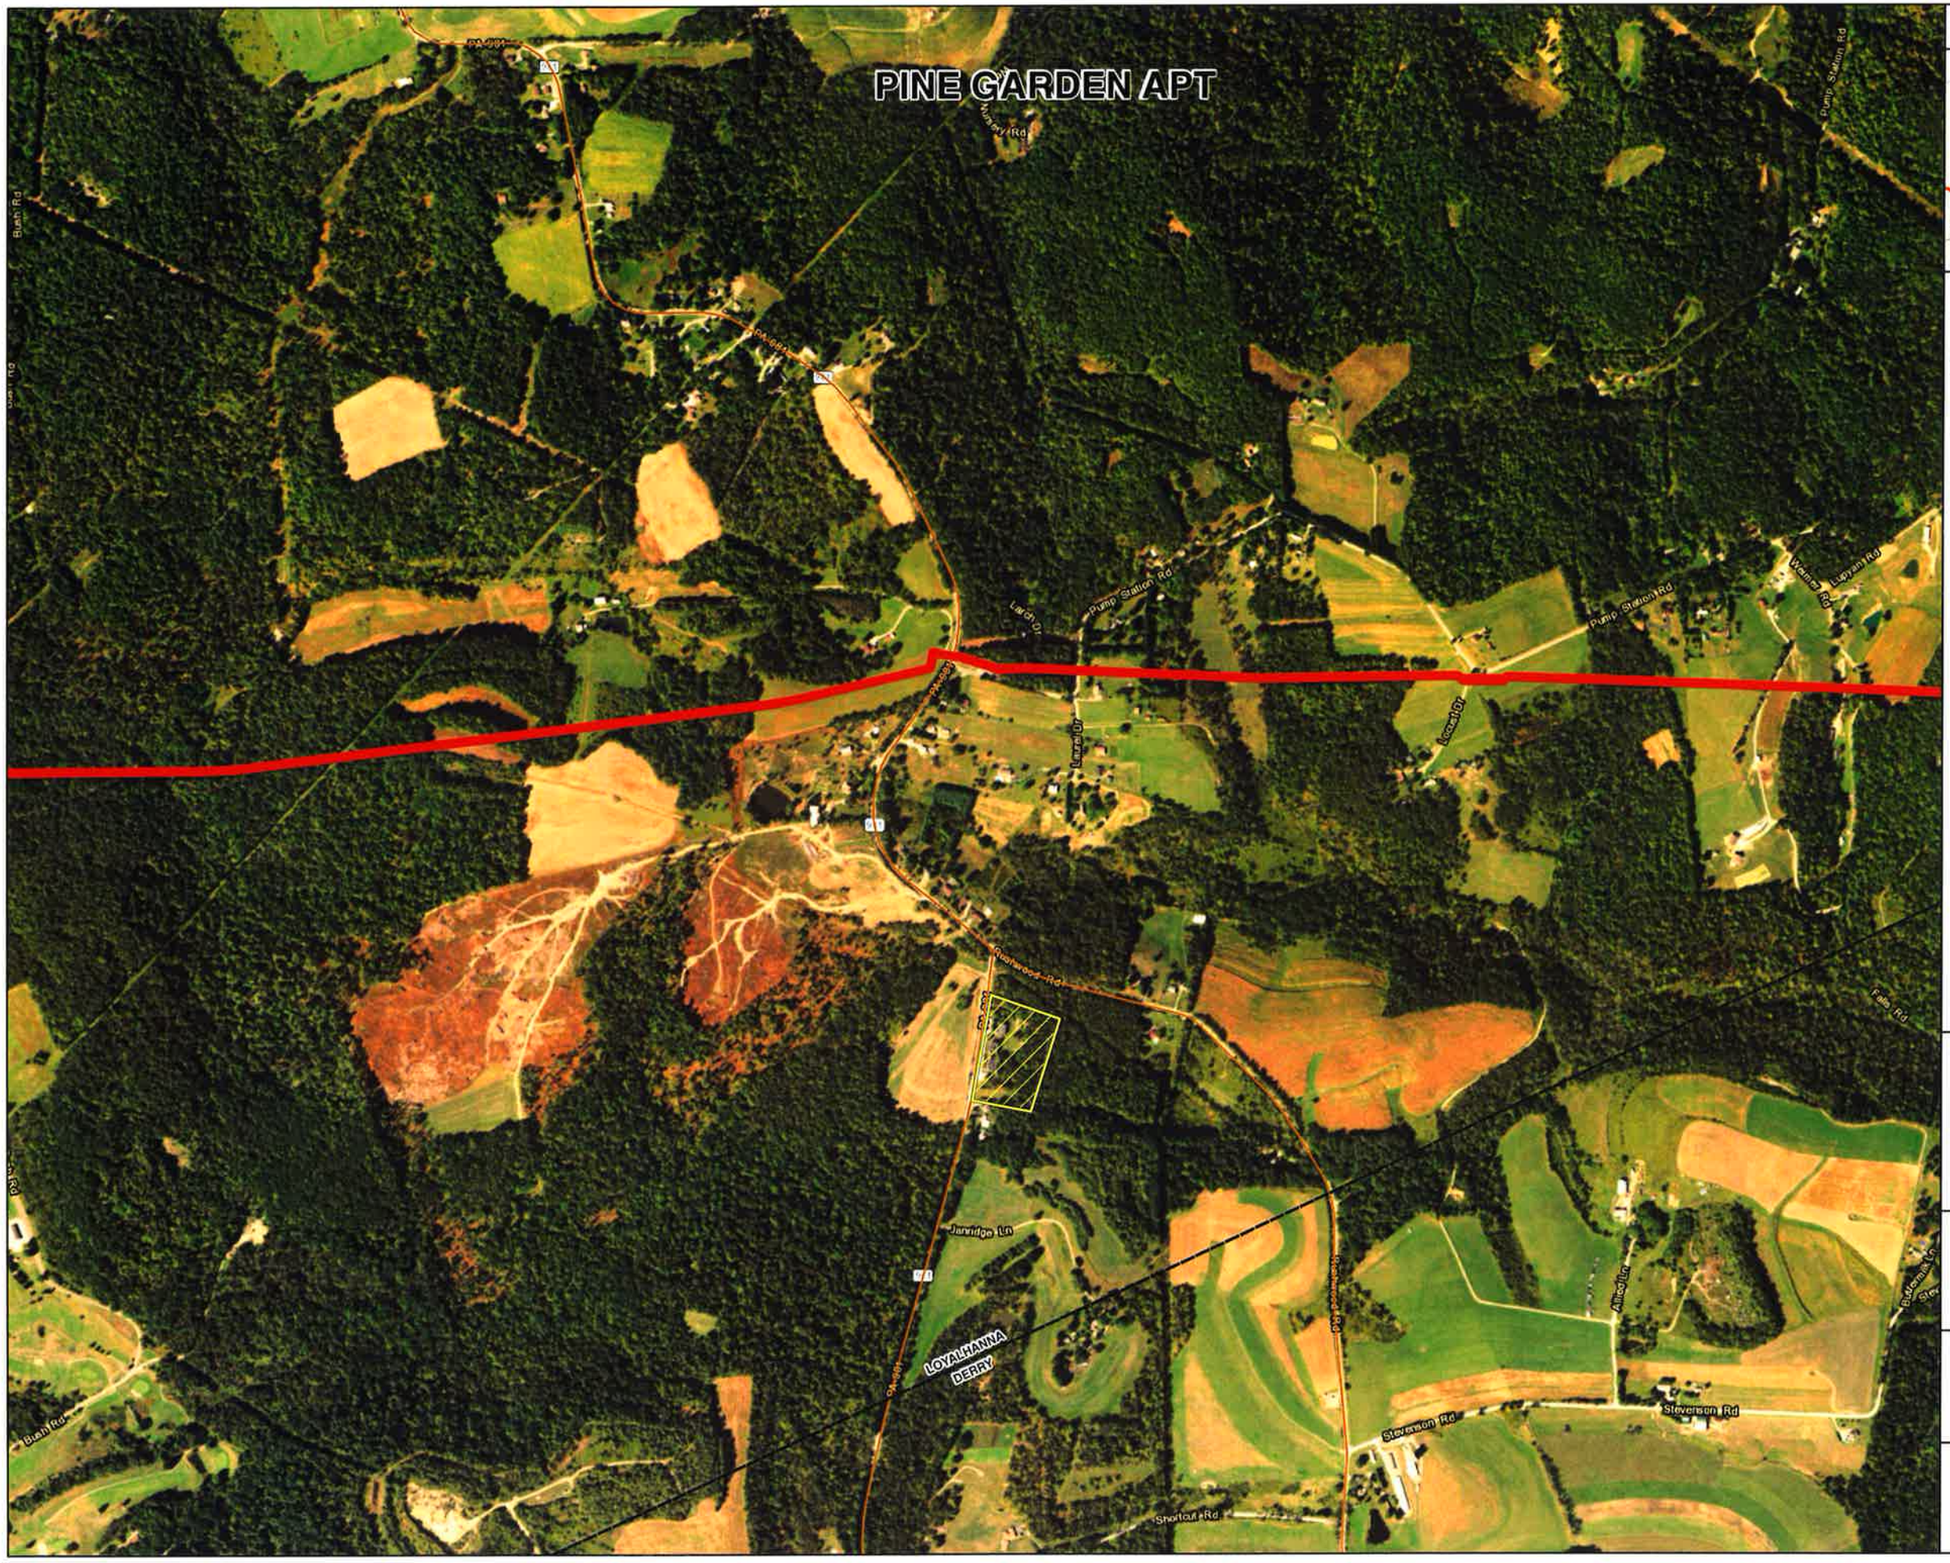

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Pine Ridge County Park	Telephone: 724-463-8636
Contact name:	Henry Freed	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Henry Freed at Pine Ridge County Park on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 11:22 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206526313 Delivered

Your package has been delivered

Tracking # 778206526313

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 11:18 am

c/o Ed Paterson, Park Supt
Pine Ridge County Park
1128 Blue Spruce Road
INDIANA, PA 15701
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206526313
Status:	Delivered: 01/19/2017 11:18 AM Signed for By: V.VANHORN
Reference:	112IC05958, 16
Signed for by:	V.VANHORN
Delivery location:	INDIANA, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:21 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

PINE RIDGE COUNTY PARK
c/o Ed Paterson, Park Supt
1128 Blue Spruce Road
Indiana, PA 15701

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Plains LPG Services LP	Telephone: 717-949-3469
Contact name:	Michael Schaefer	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Michael Schaefer at Plains LPG Services LP on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7781

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at www.usps.com®.

SCHAEFFERSTOWN, PA 17088

OFFICIAL USE

Certified Mail Fee	$3.30
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$0.00
☐ Return Receipt (electronic)	$0.00
☐ Certified Mail Restricted Delivery	$0.00
☐ Adult Signature Required	$0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
Total Postage and Fees	$4.87

0205
21

Postmark Here

SCHAEFFERSTOWN STATION
01/19/2017

Sent To PLAINS LPG SERVICES LP
Street and Apt. c/o MICHAEL SCHAEFER
City, State, ZIP P.O. BOX 486
SCHAEFFERSTOWN, PA 17088

PS Form 3800

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237781

Updated Delivery Day: Tuesday, January 24, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 24, 2017 , 9:25 am	**Delivered**	**SCHAEFFERSTOWN, PA 17088**
Your item was delivered at 9:25 am on January 24, 2017 in SCHAEFFERSTOWN, PA 17088.		
January 23, 2017 , 9:57 am	Available for Pickup	SCHAEFFERSTOWN, PA 17088
January 23, 2017 , 9:57 am	Arrived at Unit	SCHAEFFERSTOWN, PA 17088
January 22, 2017 , 10:29 pm	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:54 am	In Transit to Destination	
January 21, 2017 , 8:54 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 20, 2017 , 2:39 pm	In Transit to Destination	
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

PLAINS LPG SERVICES LP
c/o Michael Schaefer
Po Box 486
Schaefferstown, PA 17088

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Quentin Water Co	Telephone: 717-274-5514
Contact name:	William White	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to William White at Quentin Water Co on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Thursday, September 22, 2016 12:22 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276051170 Delivered

Your package has been delivered

Tracking # 777276051170

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 9/22/2016 12:20 pm

William White
Quentin Water Company
100 South Zinns Mill Road
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276051170
Status:	Delivered: 09/22/2016 12:20 PM Signed for By: P.WHITE
Reference:	112IC05958, 16
Signed for by:	P.WHITE
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	Your Packaging
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Indirect Signature Required
	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:22 AM CDT on 09/22/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

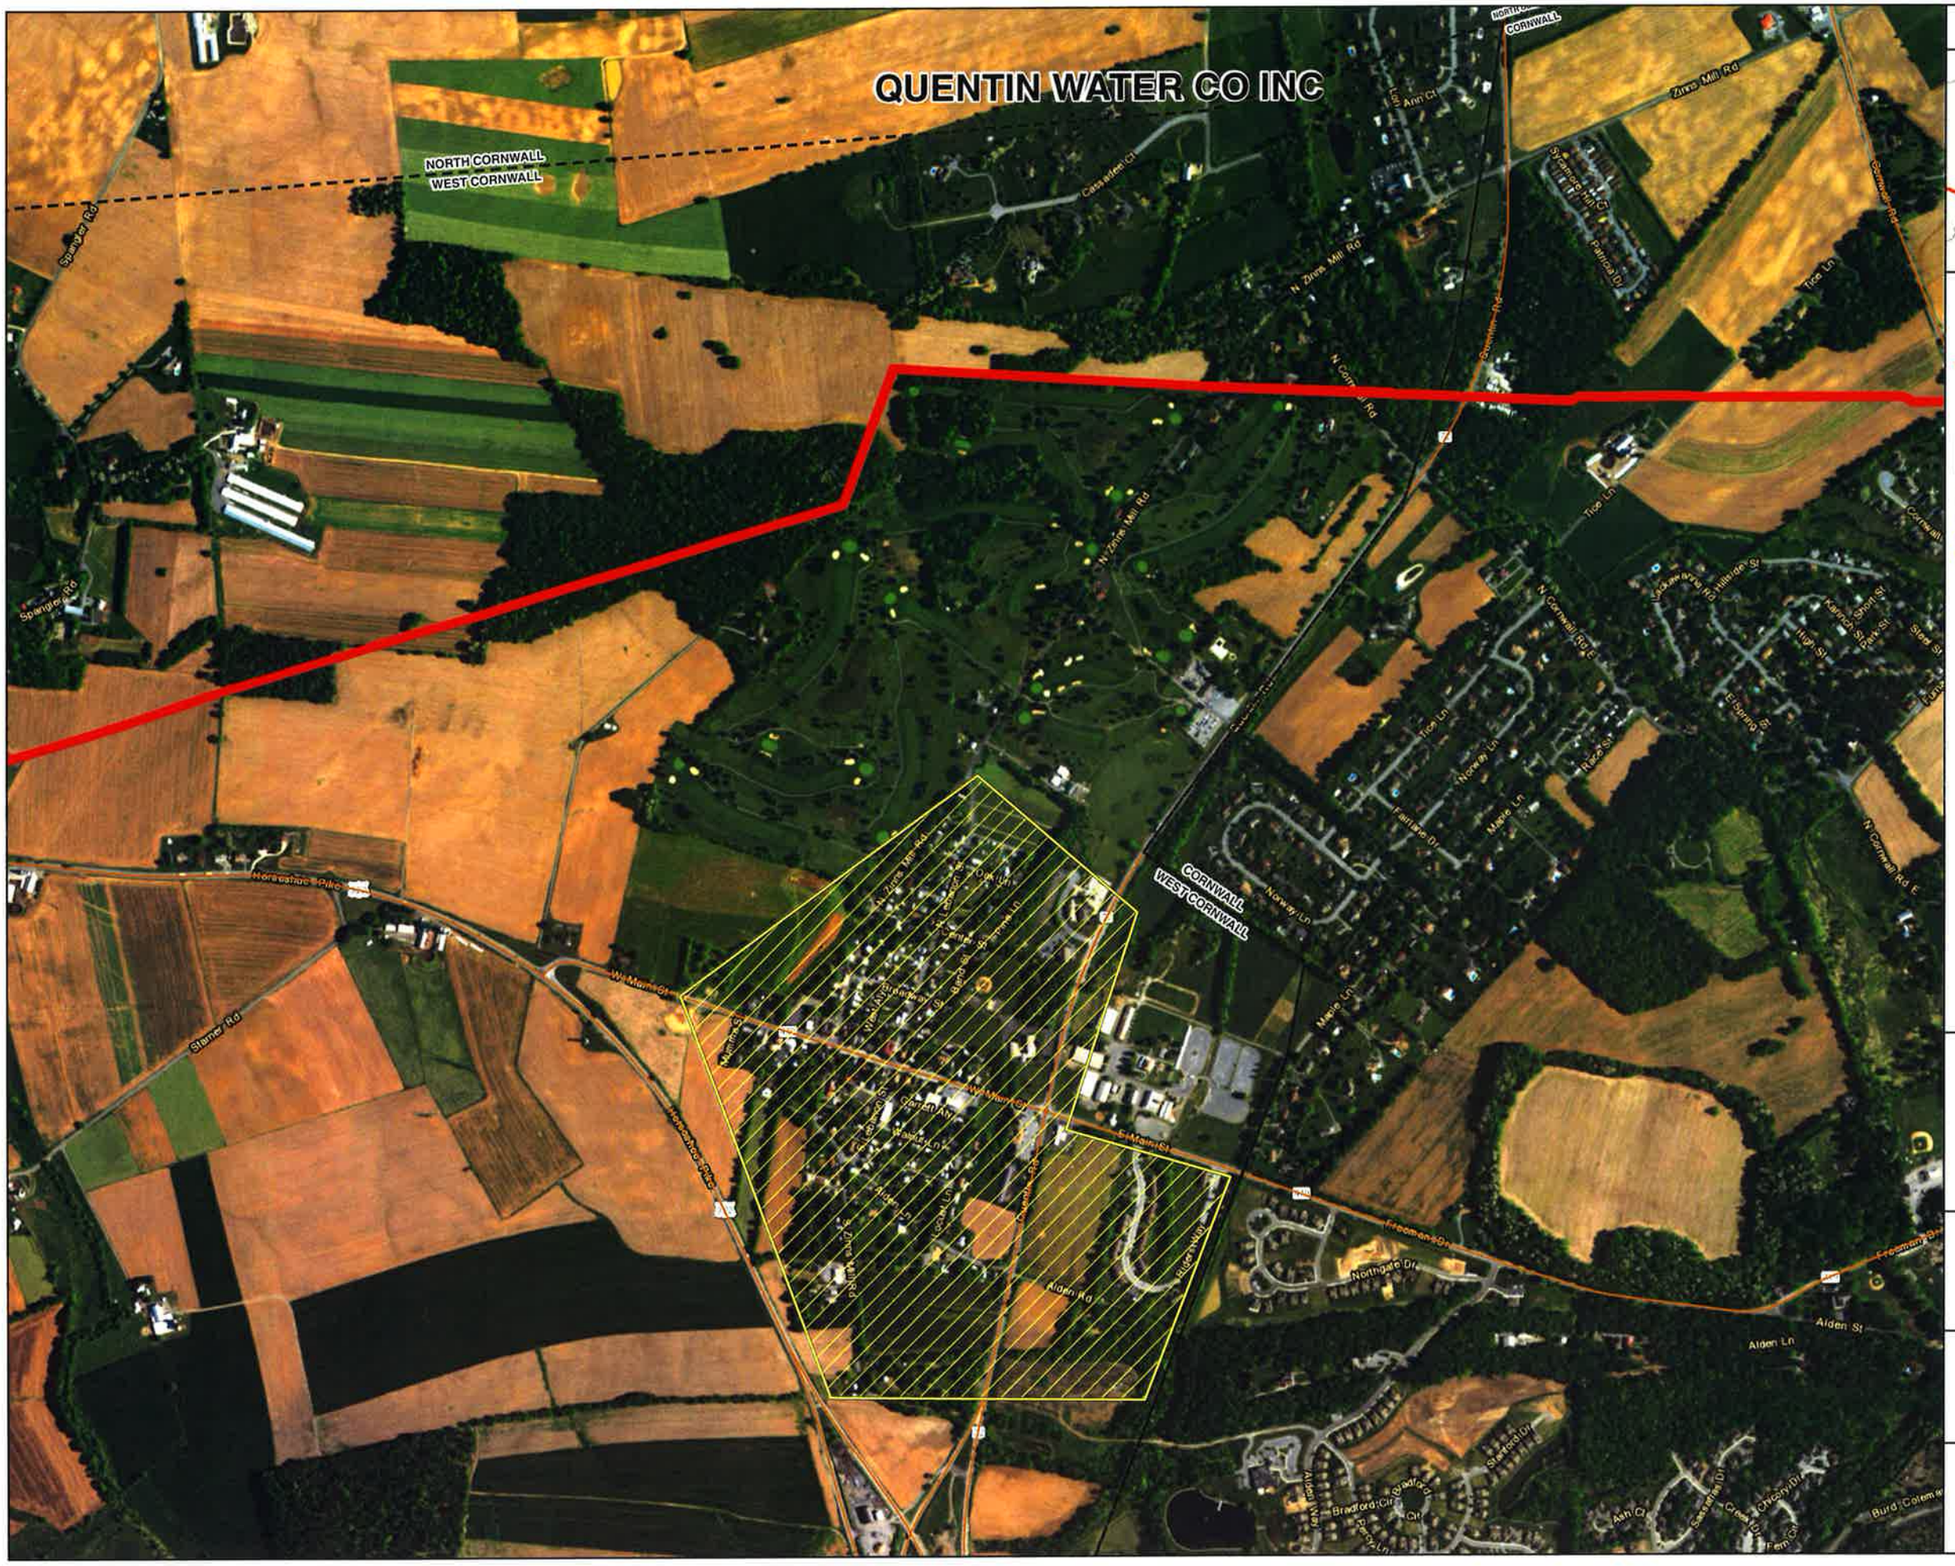

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 1,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Raystown Lake Army Corps Eng	Telephone: 814-658-3405
Contact name:	Nicholas Krupa	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Nicholas Krupa at Raystown Lake Army Corps Eng on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 1:41 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206441457 Delivered

Your package has been delivered

Tracking # 778206441457

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 1:36 pm

Raystown Lake Army Corps Eng
6145 Seven Points Rd
HESSTON, PA 16647
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206441457
Status:	Delivered: 01/19/2017 1:36 PM Signed for By: D.MCCLAIN
Reference:	112IC05958, 16
Signed for by:	D.MCCLAIN
Delivery location:	HESSTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:41 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

RAYSTOWN LAKE ARMY CORPS ENG
c/o
6145 Seven Points Rd
Hesston, PA 16647

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Raystown Lake Corp 7 Pts Plant	Telephone: 814-658-3405
Contact name:	Nicholas Krupa	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Nicholas Krupa at Raystown Lake Corp 7 Pts Plant on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Nick Krupa has reviewed the Environmental Assessment prepared for the Section 408 USACE permit. He and the USACE are aware of the full scope of the Project.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 3:34 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206802417 Delivered

Your package has been delivered

Tracking # 778206802417

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 3:32 pm

c/o Ammon and Katie Stoltzfus
Wildwood Family Cg
1901 Luxemburg Rd
LYKENS, PA 17048
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206802417
Status:	Delivered: 01/19/2017 3:32 PM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	LYKENS, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 2:34 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

RAYSTOWN LAKE CORP 7 PTS PLANT
c/o Nicholas Krupa
6145 Seven Points Rd
Hesston, PA 16647

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,



Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Rutters Farm Store #20	Telephone: 717-771-5970
Contact name:	Tim Rutter	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Tim Rutter at Rutters Farm Store #20 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:18 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206282430 Delivered

Your package has been delivered

Tracking # 778206282430

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:12 am

c/o Tim Rutter
Rutters Farm Store #20
2295 Susquehanna Trail Suite C
YORK, PA 17404
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206282430
Status:	Delivered: 01/19/2017 09:12 AM Signed for By: D.SIDESINGER
Reference:	112IC05958, 16
Signed for by:	D.SIDESINGER
Delivery location:	YORK, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:18 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

RUTTERS FARM STORE #20
c/o Tim Rutter
2295 Susquehanna Trail Suite C
York, PA 17404

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Greater Johnstown Water Auth - Saltlick	Telephone: 814-533-4300
Contact name:	Ed Cernic	
From:	Josh Baird (Tt)	
Date:	February 4, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Ed Cernic at Greater Johnstown Water Auth-Saltlick on February 4th, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on February 6, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: EL621497573US

Scheduled Delivery Day: Monday, February 6, 2017, 3:00 pm
Money Back Guarantee
Signed for By: WAIVED // JOHNSTOWN, PA 15907 // 6:01 am

Product & Tracking Information

Postal Product:
Priority Mail Express 2-Day™

Features:
Insured
PO to Addressee

DATE & TIME	STATUS OF ITEM	LOCATION
February 6, 2017 , 6:01 am	**Delivered, PO Box**	**JOHNSTOWN, PA 15907**
Your item has been delivered and is available at a PO Box at 6:01 am on February 6, 2017 in JOHNSTOWN, PA 15907. Waiver of signature was exercised at time of delivery.		
February 6, 2017 , 4:43 am	Arrived at Post Office	JOHNSTOWN, PA 15901
February 6, 2017 , 2:46 am	Arrived at USPS Destination Facility	JOHNSTOWN, PA 15904
February 5, 2017 , 11:17 pm	Arrived at USPS Destination Facility	PITTSBURGH, PA 15290
February 5, 2017 , 5:20 pm	In Transit to Destination	
February 4, 2017 , 5:20 pm	Arrived at USPS Origin Facility	ROCHESTER, NY 14692
February 4, 2017 , 2:19 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
February 4, 2017 , 11:32 am	Acceptance	BUFFALO, NY 14203

Available Actions

Proof of Delivery

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard. No tracking numbers necessary.

Sign up for My USPS ›

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

February 4th, 2017

Greater Johnstown Water Auth-Saltlick
c/o Ed Cernic
P.O. Box 1407 640 Franklin St
Johnstown, PA 15907

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by February 14th, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned.**

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Seven Points Bait & Grocery	Telephone: 814-658-3718
Contact name:	Gordon Norris	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Gordon Norris at Seven Points Bait & Grocery on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

On January 30, 2017, Seven Points Bait & Grocery called Josh Baird to express that they have no issue with the Project.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com



U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at www.usps.com®.

HESSTON, PA 16647

OFFICIAL USE

Certified Mail Fee $3.30 — $0.00

Extra Services & Fees (check box, add fee as appropriate)
- Return Receipt (hardcopy) $0.00
- Return Receipt (electronic) $0.00
- Certified Mail Restricted Delivery $0.00
- Adult Signature Required $0.00
- Adult Signature Restricted Delivery $

Postage $1.78

Total Postage and Fees $5.08

Postmark Here

01/19/2017

0205 21

Sent To SEVEN POINTS BAIT & GROCERY
Street an c/o GORDON NORRIS
City, Stat P.O. BOX 88
HESSTON, PA 16647

PS Form ... uctions

7016 2140 0001 1523 7804

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237804

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 23, 2017 , 10:17 am	**Delivered, Individual Picked Up at Post Office**	**HESSTON, PA 16647**
Your item was picked up at the post office at 10:17 am on January 23, 2017 in HESSTON, PA 16647.		
January 21, 2017 , 9:12 am	Available for Pickup	HESSTON, PA 16647
January 21, 2017 , 9:10 am	Available at PO Box	HESSTON, PA 16647
January 21, 2017 , 9:00 am	Sorting Complete	HESSTON, PA 16647
January 21, 2017 , 8:12 am	Arrived at Unit	HESSTON, PA 16647
January 21, 2017 , 6:00 am	Departed USPS Facility	JOHNSTOWN, PA 15904
January 20, 2017 , 11:44 am	Arrived at USPS Destination Facility	JOHNSTOWN, PA 15904
January 19, 2017 , 9:31 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

HELPFUL LINKS
Contact Us
Site Index
FAQs

ON ABOUT.USPS.COM
About USPS Home
Newsroom
USPS Service Updates
Forms & Publications
Government Services
Careers

OTHER USPS SITES
Business Customer Gateway
Postal Inspectors
Inspector General
Postal Explorer
National Postal Museum
Resources for Developers

LEGAL INFORMATION
Privacy Policy
Terms of Use
FOIA
No FEAR Act EEO Data

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

January 18th, 2017

SEVEN POINTS BAIT & GROCERY
c/o Gordon Norris
Po Box 88
Hesston, PA 16647

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	SGL Carbon Group LLC Telephone: 610-670-4095
Contact name:	Laverne Ramberger
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Laverne Ramberger at SGL Carbon Group LLC on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:31 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205453215 Delivered

Your package has been delivered

Tracking # 778205453215

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:42 am

c/o Laverne Ramberger
Sgl Carbon Group Llc
796 Fritztown Road
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205453215
Status:	Delivered: 01/19/2017 09:42 AM Signed for By: J.BRUBAKER
Reference:	112IC05958, 16
Signed for by:	J.BRUBAKER
Delivery location:	SINKING SPRING, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:30 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SGL CARBON GROUP LLC
c/o Laverne Ramberger
796 Fritztown Road
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Shillington Muni Auth	Telephone: 610-777-1338
Contact name:	Mike Mountz	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Mike Mountz at Shillington Muni Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 1:09 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777474076188 Delivered

Your package has been delivered

Tracking # 777474076188

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Mon, 10/17/2016 1:06 pm

Shillington Muni. Authority
2 East Lancaster Avenue
SHILLINGTON, PA 19607
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777474076188
Status:	Delivered: 10/17/2016 1:06 PM Signed for By: L.WAKELY
Reference:	112IC05958, 16
Signed for by:	L.WAKELY
Delivery location:	SHILLINGTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
Standard transit:	10/17/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:09 PM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

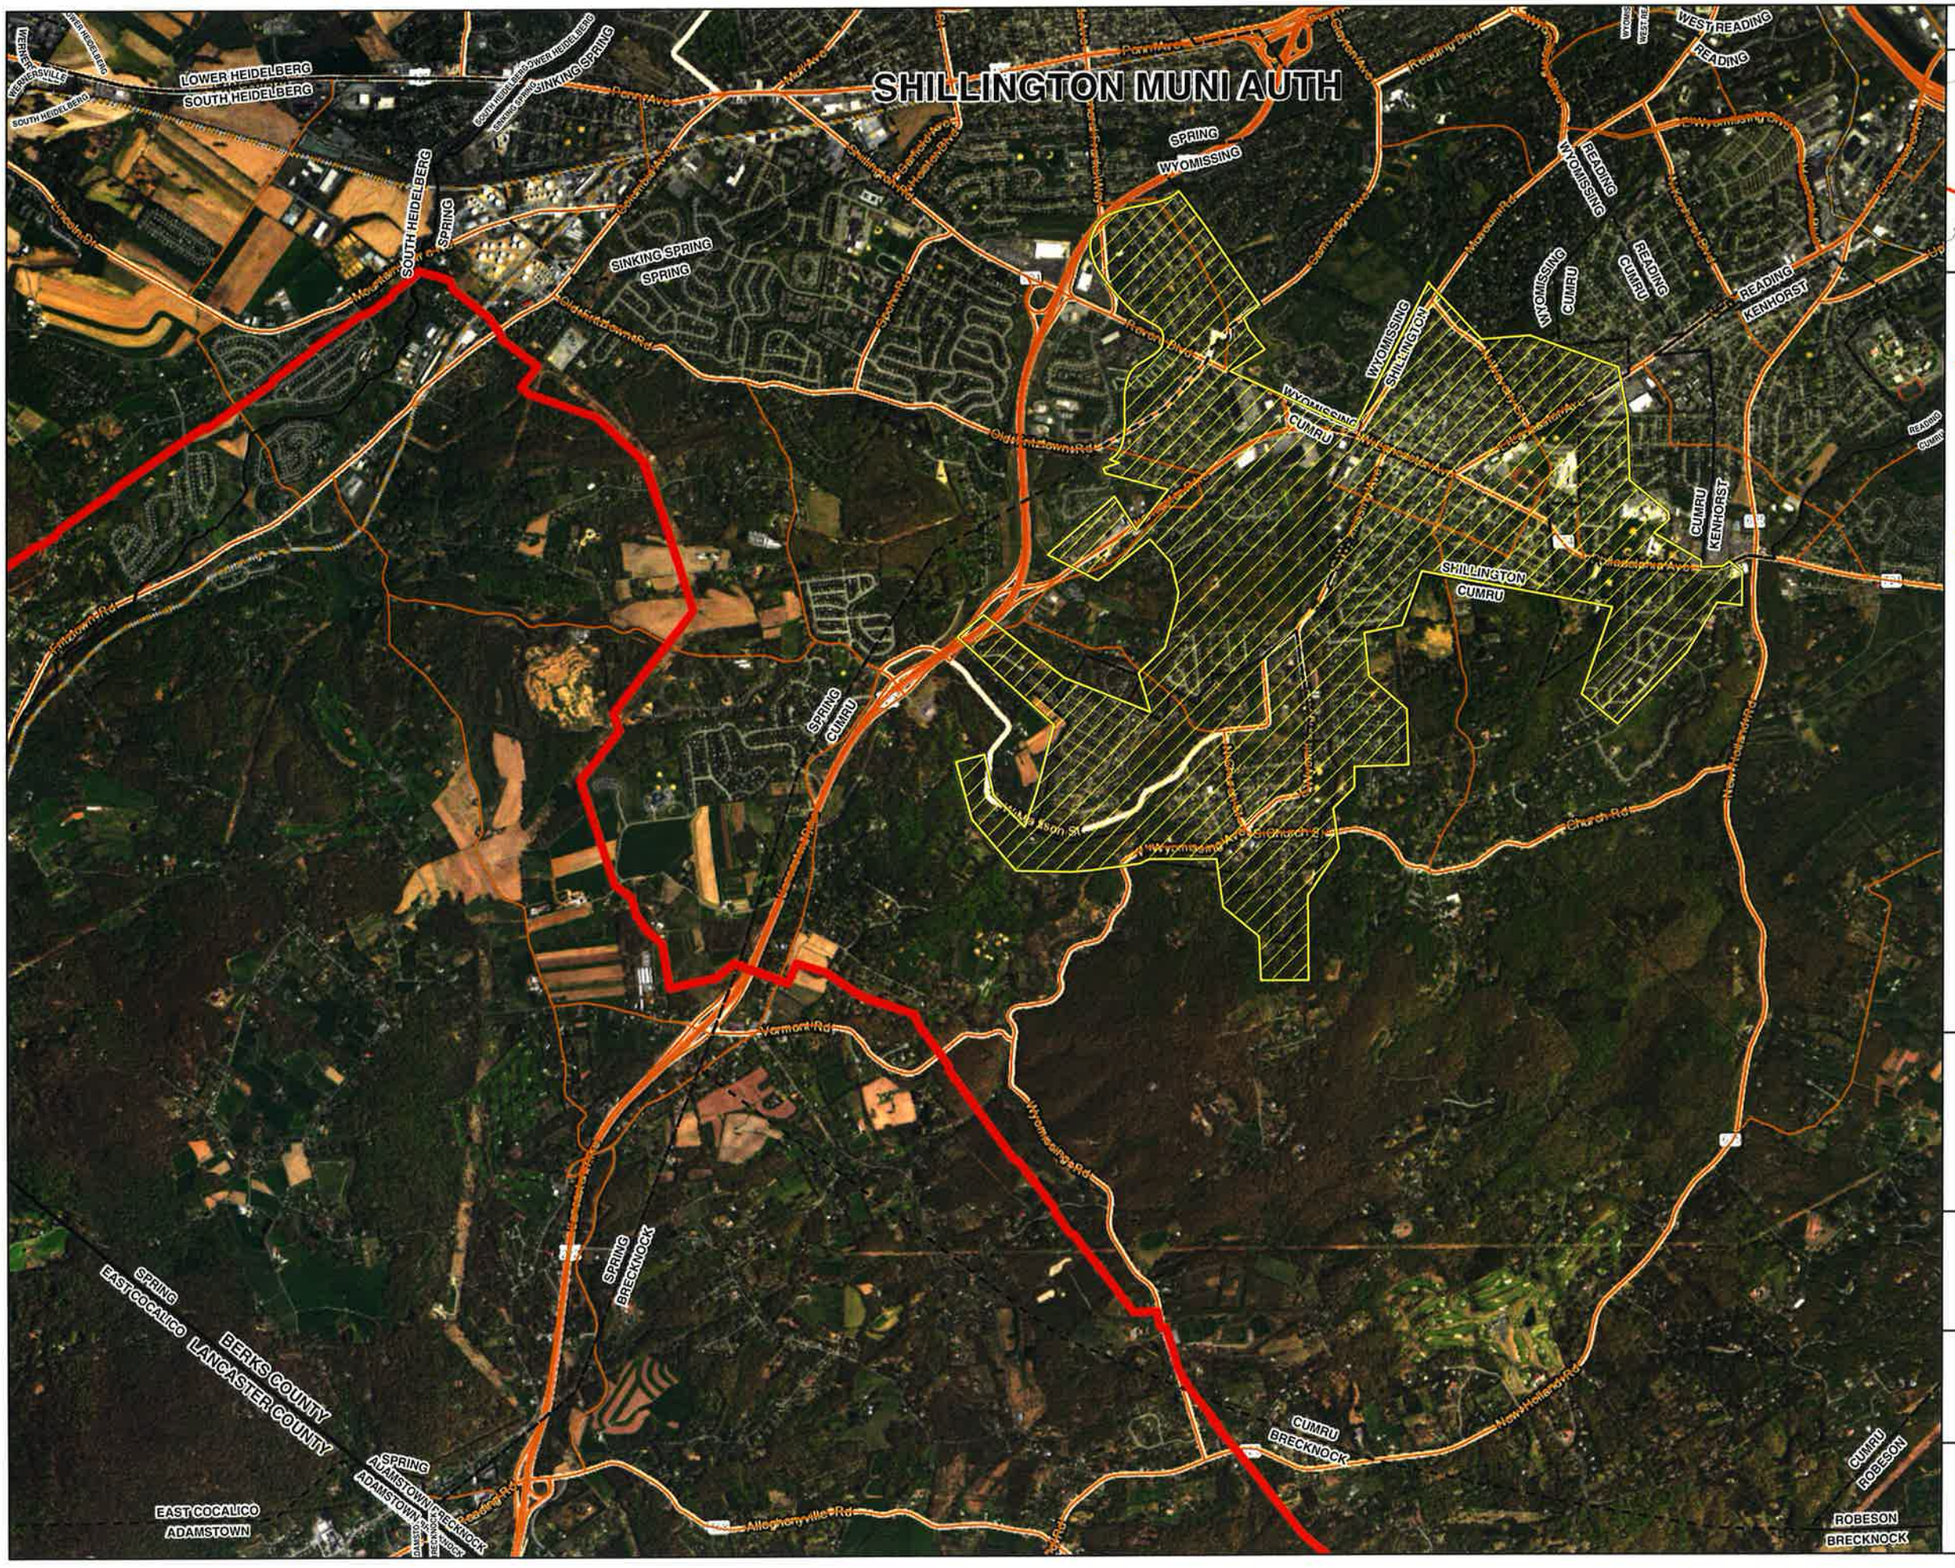

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Sinking Spring Family YMCA	Telephone: 610-678-0484
Contact name:	Brett Mayer	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Brett Mayer at Sinking Spring YMCA on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:53 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205490459 Delivered

Your package has been delivered

Tracking # 778205490459

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:49 am

c/o Brett Mayer
Sinking Spring Family YMCA
4920 Penn Ave
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205490459
Status:	Delivered: 01/19/2017 09:49 AM Signed for By: D.STUMP
Reference:	112IC05958, 16
Signed for by:	D.STUMP
Delivery location:	SINKING SPRING, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:52 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SINKING SPRING FAMILY YMCA
c/o Brett Mayer
4920 Penn Ave
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Sleepy Hollow Athletic Club Telephone: 610-856-7516
Contact name:	Dean Stine
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Dean Stine at Sleepy Hollow Athletic Club on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 20, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Friday, January 20, 2017 9:45 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205515504 Delivered

Your package has been delivered

Tracking # 778205515504

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Fri, 1/20/2017 9:39 am

c/o Dean Stine
Sleepy Hollow Athletic Club
482 Westley Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205515504
Status:	Delivered: 01/20/2017 09:39 AM Signed for By: Signature Release on file
Door Tag number:	DT104451231678
Reference:	112IC05958, 16
Signed for by:	Signature Release on file
Delivery location:	MOHNTON, PA
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:44 AM CST on 01/20/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SLEEPY HOLLOW ATHLETIC CLUB
c/o Dean Stine
482 Westley Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Sleepy Hollow Pool Telephone: 610-856-1418
Contact name:	Dean Stine
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Dean Stine at Sleepy Hollow Pool on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 20, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Friday, January 20, 2017 9:45 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205515504 Delivered

Your package has been delivered

Tracking # 778205515504

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Fri, 1/20/2017 9:39 am

c/o Dean Stine
Sleepy Hollow Pool
482 Westley Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205515504
Status:	Delivered: 01/20/2017 09:39 AM Signed for By: Signature Release on file
Door Tag number:	DT104451231678
Reference:	112IC05958, 16
Signed for by:	Signature Release on file
Delivery location:	MOHNTON, PA
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:44 AM CST on 01/20/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SLEEPY HOLLOW POOL
c/o Dean Stine
482 Westley Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Smitty's Eats N Treats	Telephone: 814-644-3791
Contact name:	Lori Heaton	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Lori Heaton at Smitty's Eats N Treats on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:29 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206457033 Delivered

Your package has been delivered

Tracking # 778206457033

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:24 am

c/o Lori Heaton
Smitty S Eats N Treats
2300 Highland Avenue
HUNTINGDON, PA 16652
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206457033
Status:	Delivered: 01/19/2017 10:24 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	HUNTINGDON, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 12:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:28 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SMITTY S EATS N TREATS
c/o Lori Heaton
2300 Highland Ave
Huntingdon, PA 16652

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	South Mountain YMCA Telephone: 610-670-2267
Contact name:	Nathan Brant
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Nathan Brant at South Mountain YMCA on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 23, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

7016 2140 0001 1523 7729

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at www.usps.com®.
WERNERSVILLE, PA 19565

OFFICIAL USE

Certified Mail Fee	$3.30
$	$0.00
Extra Services & Fees (check box, add fee as appropriate)	
☐ Return Receipt (hardcopy)	$ $0.00
☐ Return Receipt (electronic)	$ $0.00
☐ Certified Mail Restricted Delivery	$ $0.00
☐ Adult Signature Required	$ $0.00
☐ Adult Signature Restricted Delivery	$
Postage	$1.57
$	
Total Postage and Fees	$4.87
$	

0205
21

Postmark Here

01/19/2017

Sent To: SOUTH MOUNTAIN YMCA
Street and Apt.: c/o NATHAN BRANT
City, State, ZIP: P.O. BOX 147
PS Form 380: WERNERSVILLE, PA 19565

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237729

On Time
Updated Delivery Day: Monday, January 23, 2017

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 23, 2017 , 8:58 am	Available for Pickup	**WERNERSVILLE, PA 19565**
Your item arrived at the WERNERSVILLE, PA 19565 post office at 8:58 am on January 23, 2017 and is ready for pickup.		
January 23, 2017 , 8:35 am	Available at PO Box	WERNERSVILLE, PA 19565
January 23, 2017 , 8:25 am	Sorting Complete	WERNERSVILLE, PA 19565
January 23, 2017 , 6:57 am	Arrived at Unit	WERNERSVILLE, PA 19565
January 23, 2017 , 1:08 am	Departed USPS Destination Facility	HARRISBURG, PA 17107
January 22, 2017 , 8:53 am	In Transit to Destination	
January 21, 2017 , 8:53 am	Arrived at USPS Destination Facility	HARRISBURG, PA 17107
January 21, 2017 , 4:27 am	In Transit to Destination	
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

TETRA TECH

January 18th, 2017

SOUTH MOUNTAIN YMCA
c/o Nathan Brant
P.O. Box 147
Wernersville, PA 19565

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Speedway 6760	Telephone: 717-938-1428
Contact name:	Sarah Palmer	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Sarah Palmer at Speedway 6760 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:20 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778207131616 Delivered

Your package has been delivered

Tracking # 778207131616

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:17 am

c/o Sarah Palmer
Speedway 6760
500 Speedway Drive
ENON, OH 45323
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778207131616
Status:	Delivered: 01/19/2017 09:17 AM Signed for By: M.BLANKE
Reference:	112IC05958, 16
Signed for by:	M.BLANKE
Delivery location:	ENON, OH
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:20 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SPEEDWAY 6760
c/o Sarah Palmer
500 Speedway Drive
Enon, OH 45323

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	St Benedict Church Telephone: 610-856-1006
Contact name:	Rev Philip Rodgers
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Rev Philip Rodgers at St Benedict Church on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:26 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205559683 Delivered

Your package has been delivered

Tracking # 778205559683

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:21 am

c/o Rev Philip Rodgers
St Benedict Ch
2020 Chestnuthill Road
MOHNTON, PA 19540
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205559683
Status:	Delivered: 01/19/2017 10:21 AM Signed for By: J.HAUCK
Reference:	112IC05958, 16
Signed for by:	J.HAUCK
Delivery location:	MOHNTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:26 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

ST BENEDICT CH
c/o Rev Philip Rodgers
2020 Chestnuthill Road
Mohnton, PA 19540

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH


Contact Report

To:	Steelco Well #2 Telephone: 610-678-6411
Contact name:	Neil Nevitt
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Neil Nevitt at Steelco Well #2 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017 however the company was out of business.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

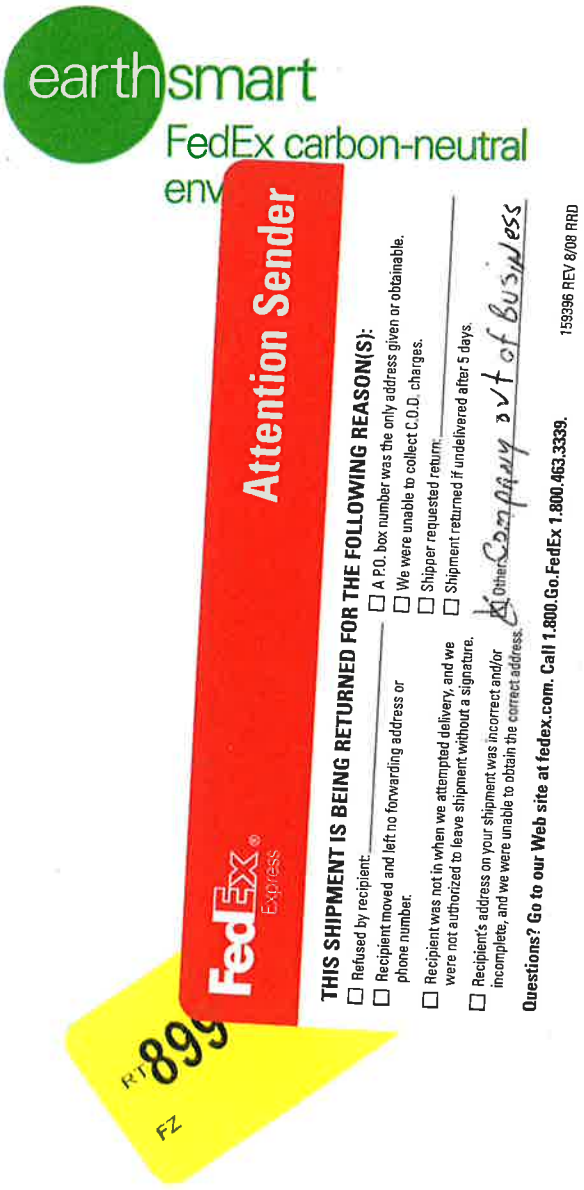



Part # 156297V-435 RIT2 APV EXP 08/17 •

Align bottom of peel-and-stick airbill or pouch here.

TETRA TECH

January 18th, 2017

STEELCO WELL #2
c/o Neil Nevitt
601 Fritztown Rd
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Steelco Telephone: 610-678-6411
Contact name:	Mike Endler
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Mike Endler at Steelco on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017 however the company was out of business.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

earthsmart
FedE
envel

INT 899 1 10:30 A 9527 01.19
FZ

FedEx Express

Attention Sender

THIS SHIPMENT IS BEING RETURNED FOR THE FOLLOWING REASON(S):

- ☐ Refused by recipient: _____
- ☐ Recipient moved and left no forwarding address or phone number.
- ☐ Recipient was not in when we attempted delivery, and we were not authorized to leave shipment without a signature.
- ☐ Recipient's address on your shipment was incorrect and/or incomplete, and we were unable to obtain the correct address.
- ☐ A P.O. box number was the only address given or obtainable.
- ☐ We were unable to collect C.O.D. charges.
- ☐ Shipper requested return: _____
- ☐ Shipment returned if undelivered after 5 days.
- ☒ Other Company out of Business

Questions? Go to our Web site at fedex.com. Call 1.800.Go.FedEx 1.800.463.3339.

159396 REV 8/08 RRD

Part # 15829FV-435 RIT2 APV EXP 08/17

ORIGIN ID:BUFA (716) 849-9419
JOSH BAIRD
TETRA TECH - HOME
301 ELLICOTT STREET

BUFFALO, NY 14203
UNITED STATES US

SHIP DATE: 18JAN17
ACTWGT: 0.50 LB
CAD: 5212059/INET3790

BILL SENDER

TO **C/O MIKE ENDLER**
STEELCO
601 FRITZTOWN RD

SINKING SPRING PA 19608

(716) 849-9419
INV:
PO:

REF: 112IC05958. 16
DEPT:

FedEx Express

TRK# 0201 **7782 0557 9527**

THU - 19 JAN 10:30A
PRIORITY OVERNIGHT

EQ RDGA

19608
PA-US ABE

TETRA TECH

January 18th, 2017

STEELCO
c/o Mike Endler
601 Fritztown Rd
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Steelton Boro Water Auth	Telephone: 717-939-0425
Contact name:	Doug Brown	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Doug Brown at Steelton Boro Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 10:59 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276063200 Delivered

Your package has been delivered

Tracking # 777276063200

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Wed, 9/21/2016 10:56 am

Doug Brown
Steelton Boro. Water Authority
123 N. Front Street
STEELTON, PA 17113
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276063200
Status:	Delivered: 09/21/2016 10:56 AM Signed for By: M.POWELL
Reference:	112IC05958, 16
Signed for by:	M.POWELL
Delivery location:	STEELTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:59 AM CDT on 09/21/2016.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.



Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Steve Heins Grocery Store	Telephone: 717-533-5222
Contact name:	Susan Hein	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Susan Hein at Steve Heins Grocery Store on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:43 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206313638 Delivered

Your package has been delivered

Tracking # 778206313638

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:40 am

c/o Susan Hein
Steve Heins Grocery Store
2985 Elizabethtown Rd.
HERSHEY, PA 17033
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206313638
Status:	Delivered: 01/19/2017 09:40 AM Signed for By: A.DAUBENSCHMIDT
Reference:	112IC05958, 16
Signed for by:	A.DAUBENSCHMIDT
Delivery location:	HERSHEY, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:43 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

STEVE HEINS GROCERY STORE
c/o Susan Hein
2985 Elizabethtown Rd.
Hershey, PA 17033

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Suez Water Telephone: 717-561-1103
Contact name:	Chad Bingaman
From:	Josh Baird (Tt)
Date:	September 20, 2016
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Chad Bingaman at Suez Wate on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:18 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276074470 Delivered

Your package has been delivered

Tracking # 777276074470

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:11 am

Chad Bingaman
Suez Water
4211 East Park Circle
HARRISBURG, PA 17111
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276074470
Status:	Delivered: 09/21/2016 11:11 AM Signed for By: K.MCCONNELL
Reference:	112IC05958, 16
Signed for by:	K.MCCONNELL
Delivery location:	HARRISBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:18 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

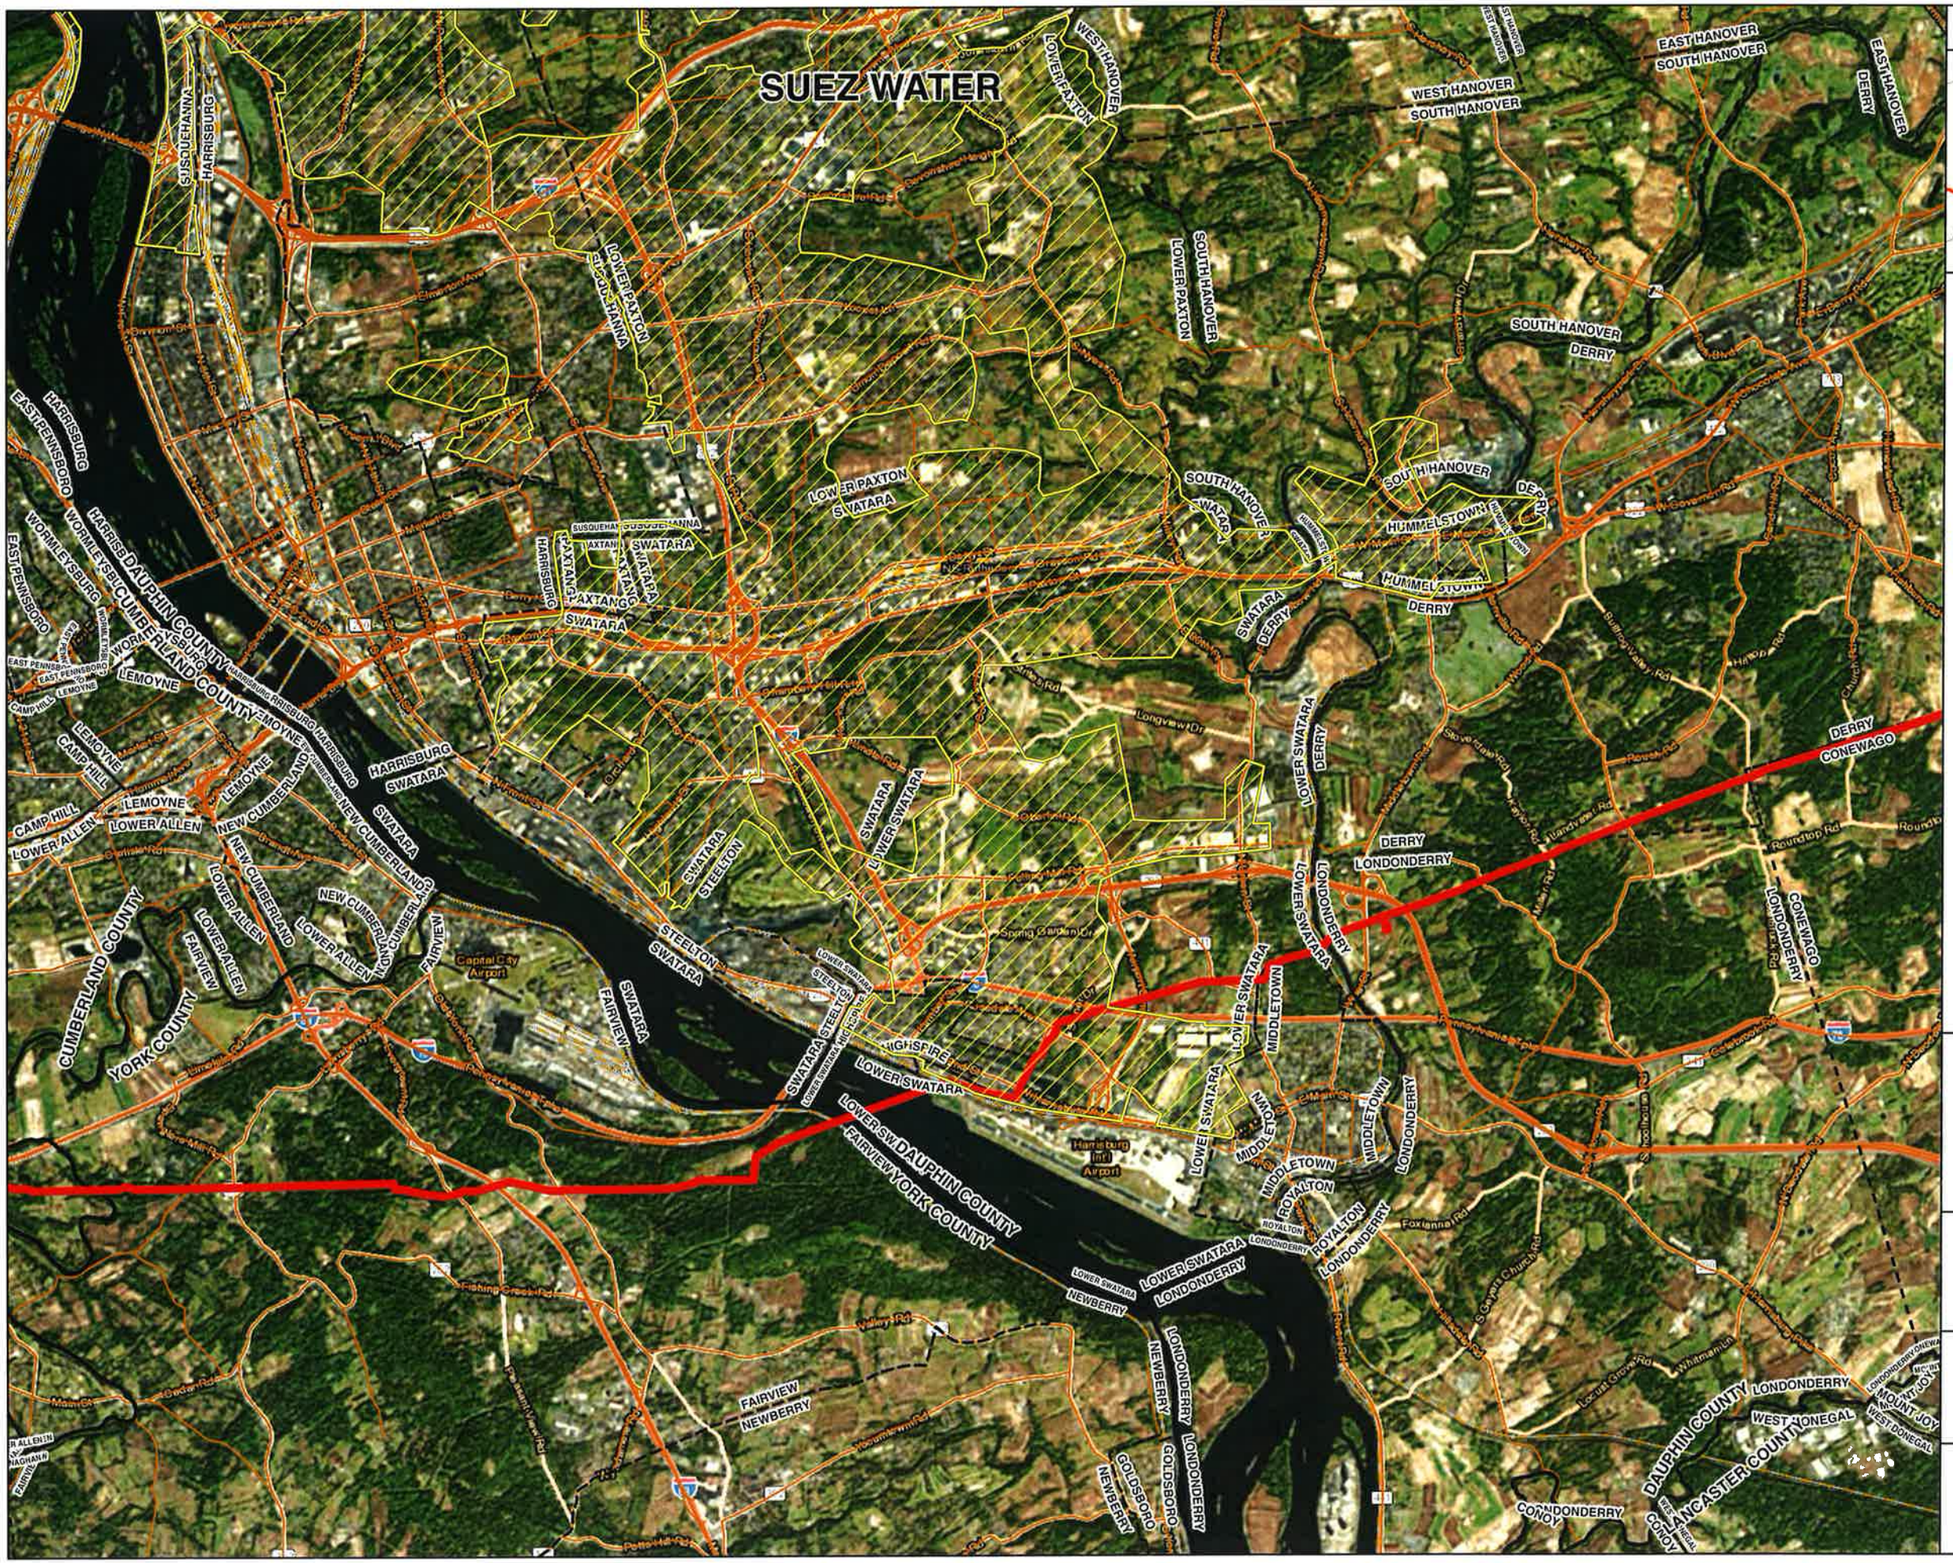

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 9,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:
9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Sunoco Food Shop Telephone: 610-678-3550
Contact name:	Arana Singh
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Arana Singh at Sunoco Food Shop on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017. On January 24, 2017 an email was received from Katherin Selch expressing no impact, however they also expressed a desire to be kept informed as the Project progressed.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:31 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205660153 Delivered

Your package has been delivered

Tracking # 778205660153

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:56 am

co Arana Singh
Sunoco Food Shop
904 Kate Drive
SINKING SPRING, PA 19608
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205660153
Status:	Delivered: 01/19/2017 09:56 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	SINKING SPRING, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:30 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SUNOCO FOOD SHOP
c/o Arana Singh
904 Kate Drive
Sinking Spring, PA 19608

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Sweetwater Farm B and B	Telephone: 610-459-4711
Contact name:	Chris Le Vine	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Chris Le Vine at Sweetwater Farm B and B on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:23 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206363106 Delivered

Your package has been delivered

Tracking # 778206363106

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:20 am

c/o Chris Le Vine
Sweetwater Farm A and B
50 Sweetwater Road
GLEN MILLS, PA 19342
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206363106
Status:	Delivered: 01/19/2017 09:20 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	GLEN MILLS, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:23 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

SWEETWATER FARM B AND B
c/o Chris Le Vine
50 Sweetwater Road
Glen Mills, PA 19342

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	The Pines Telephone: 724-468-9923
Contact name:	Alexander W. Orlowski
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Alexander W. Orlowski at The Pines on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 10:43 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206902409 Delivered

Your package has been delivered

Tracking # 778206902409

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 10:42 am

c/o Alexander W Orlowski
The Pines
Rd 4, Box 231
GREENSBURG, PA 15601
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206902409
Status:	Delivered: 01/19/2017 10:42 AM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	GREENSBURG, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 9:43 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

THE PINES
c/o Alexander W Orlowski
Rd 4, Box 231
Greensburg, PA 15601

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Thousand Trails	Telephone: 717-867-5515
Contact name:	Kim Miller	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Kim Miller at Thousand Trails on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:17 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206749467 Delivered

Your package has been delivered

Tracking # 778206749467

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 9:12 am

c/o Kim Miller
Thousand Trails
493 S. Mt Plaesant Rd
LEBANON, PA 17042
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206749467
Status:	Delivered: 01/19/2017 09:12 AM Signed for By: J.SPANGLER
Reference:	112IC05958, 16
Signed for by:	J.SPANGLER
Delivery location:	LEBANON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:16 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

THOUSAND TRAILS
c/o Kim Miller
493 S Mt Pleasant Rd
Lebanon, PA 17042

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Trading Post Market	Telephone: 717-776-3082
Contact name:	Michelle Baia	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Michelle Baia at Trading Post Market on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 1:53 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206101260 Delivered

Your package has been delivered

Tracking # 778206101260

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 1:46 pm

c/o Michelle Baia
Trading Post Market
672 Bloserville Rd
NEWVILLE, PA 17241
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206101260
Status:	Delivered: 01/19/2017 1:46 PM Signed for By: R.LEHMAN
Reference:	112IC05958, 16
Signed for by:	R.LEHMAN
Delivery location:	NEWVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:52 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

TRADING POST MARKET
c/o Michelle Baia
672 Bloserville Rd
Newville, PA 17241

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Turkey Hill Mini Mkt 115 Telephone: 717-299-8908
Contact name:	Jerry Book – Facilities Manager
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Jerry Book at Turkey Hills Mini Mkt 115 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017. On January 24, 2017 an email was received from Katherin Selch expressing no impact, however they also expressed a desire to be kept informed as the Project progressed.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 9:56 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205702201 Delivered

Your package has been delivered

Tracking # 778205702201

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 9:48 am

c/o Jerry Book, Facilities Manager
Turkey Hill Mini Mkt 115
257 Centerville Road
LANCASTER, PA 17603
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205702201
Status:	Delivered: 01/19/2017 09:48 AM Signed for By: T.AOWLER
Reference:	112IC05958, 16
Signed for by:	T.AOWLER
Delivery location:	LANCASTER, PA
Delivered to:	Shipping/Receiving
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday

Standard transit:	1/19/2017 by 10:30 am

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 8:55 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

TURKEY HILL MINI MKT 115
c/o Jerry Book, Facilities Manager
257 Centerville Road
Lancaster, PA 17603

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Twin Valley Field House Telephone: 610-286-8652
Contact name:	Keith Heckman – Dir Phys PLT
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Keith Heckman at Twin Valley Field House on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 12:47 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205732800 Delivered

Your package has been delivered

Tracking # 778205732800

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 12:42 pm

c/o Keith Heckman
Twin Valley Field House
4851 N Twin Valley Rd
ELVERSON, PA 19520
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205732800
Status:	Delivered: 01/19/2017 12:42 PM Signed for By: L.MILLER
Reference:	112IC05958, 16
Signed for by:	L.MILLER
Delivery location:	ELVERSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:47 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

TWIN VALLEY FIELD HOUSE
c/o Keith Heckman-Dir Phys Plt
4851 N Twin Valley Rd
Elverson, PA 19520

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Twin Valley Middle School Telephone: 610-286-8679
Contact name:	Keith Heckman – Dir Phys PLT
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Keith Heckman at Twin Valley Middle School on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 12:47 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205732800 Delivered

Your package has been delivered

Tracking # 778205732800

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 12:42 pm

c/o Keith Heckman
Twin Valley Middle School
4851 N Twin Valley Rd
ELVERSON, PA 19520
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205732800
Status:	Delivered: 01/19/2017 12:42 PM Signed for By: L.MILLER
Reference:	112IC05958, 16
Signed for by:	L.MILLER
Delivery location:	ELVERSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:47 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

TWIN VALLEY MIDDLE SCHOOL
c/o Keith Heckman-Dir Phys Plt
4851 N Twin Valley Rd
Elverson, PA 19520

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,



Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Twin Valley Senior High School Telephone: 610-286-8679
Contact name:	Keith Heckman – Dir Phys PLT
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Keith Heckman at Twin Valley Senior High School on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 12:47 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205732800 Delivered

Your package has been delivered

Tracking # 778205732800

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Thu, 1/19/2017 12:42 pm

c/o Keith Heckman Twin Valley Senior High School
4851 N Twin Valley Rd
19520
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205732800
Status:	Delivered: 01/19/2017 12:42 PM Signed for By: L.MILLER
Reference:	112IC05958, 16
Signed for by:	L.MILLER
Delivery location:	ELVERSON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:47 AM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

TWIN VALLEY SENIOR HIGH SCHOOL
c/o Keith Heckman-Dir Phys Plt
4851 N Twin Valley Rd
Elverson, PA 19520

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	United Water Pa Mechanicsburg	Telephone: 707-561-1103
Contact name:	John D. Hollenbach	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to John D. Hollenbach at United Water Pa Mechanicsburg on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Wednesday, September 21, 2016 11:18 AM
To: Laviolette, Carrie
Subject: FedEx Shipment 777276121516 Delivered

Your package has been delivered

Tracking # 777276121516

Ship date:
Tue, 9/20/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Wed, 9/21/2016 11:11 am

John D. Hollenbach
United Water PA
Mechanicsburg
4211 East Park Circle
HARRISBURG, PA 17111
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777276121516
Status:	Delivered: 09/21/2016 11:11 AM Signed for By: K.MCCONNELL
Reference:	112IC05958, 16
Signed for by:	K.MCCONNELL
Delivery location:	HARRISBURG, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Direct Signature Required

	Deliver Weekday
Standard transit:	9/21/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 10:18 AM CDT on 09/21/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

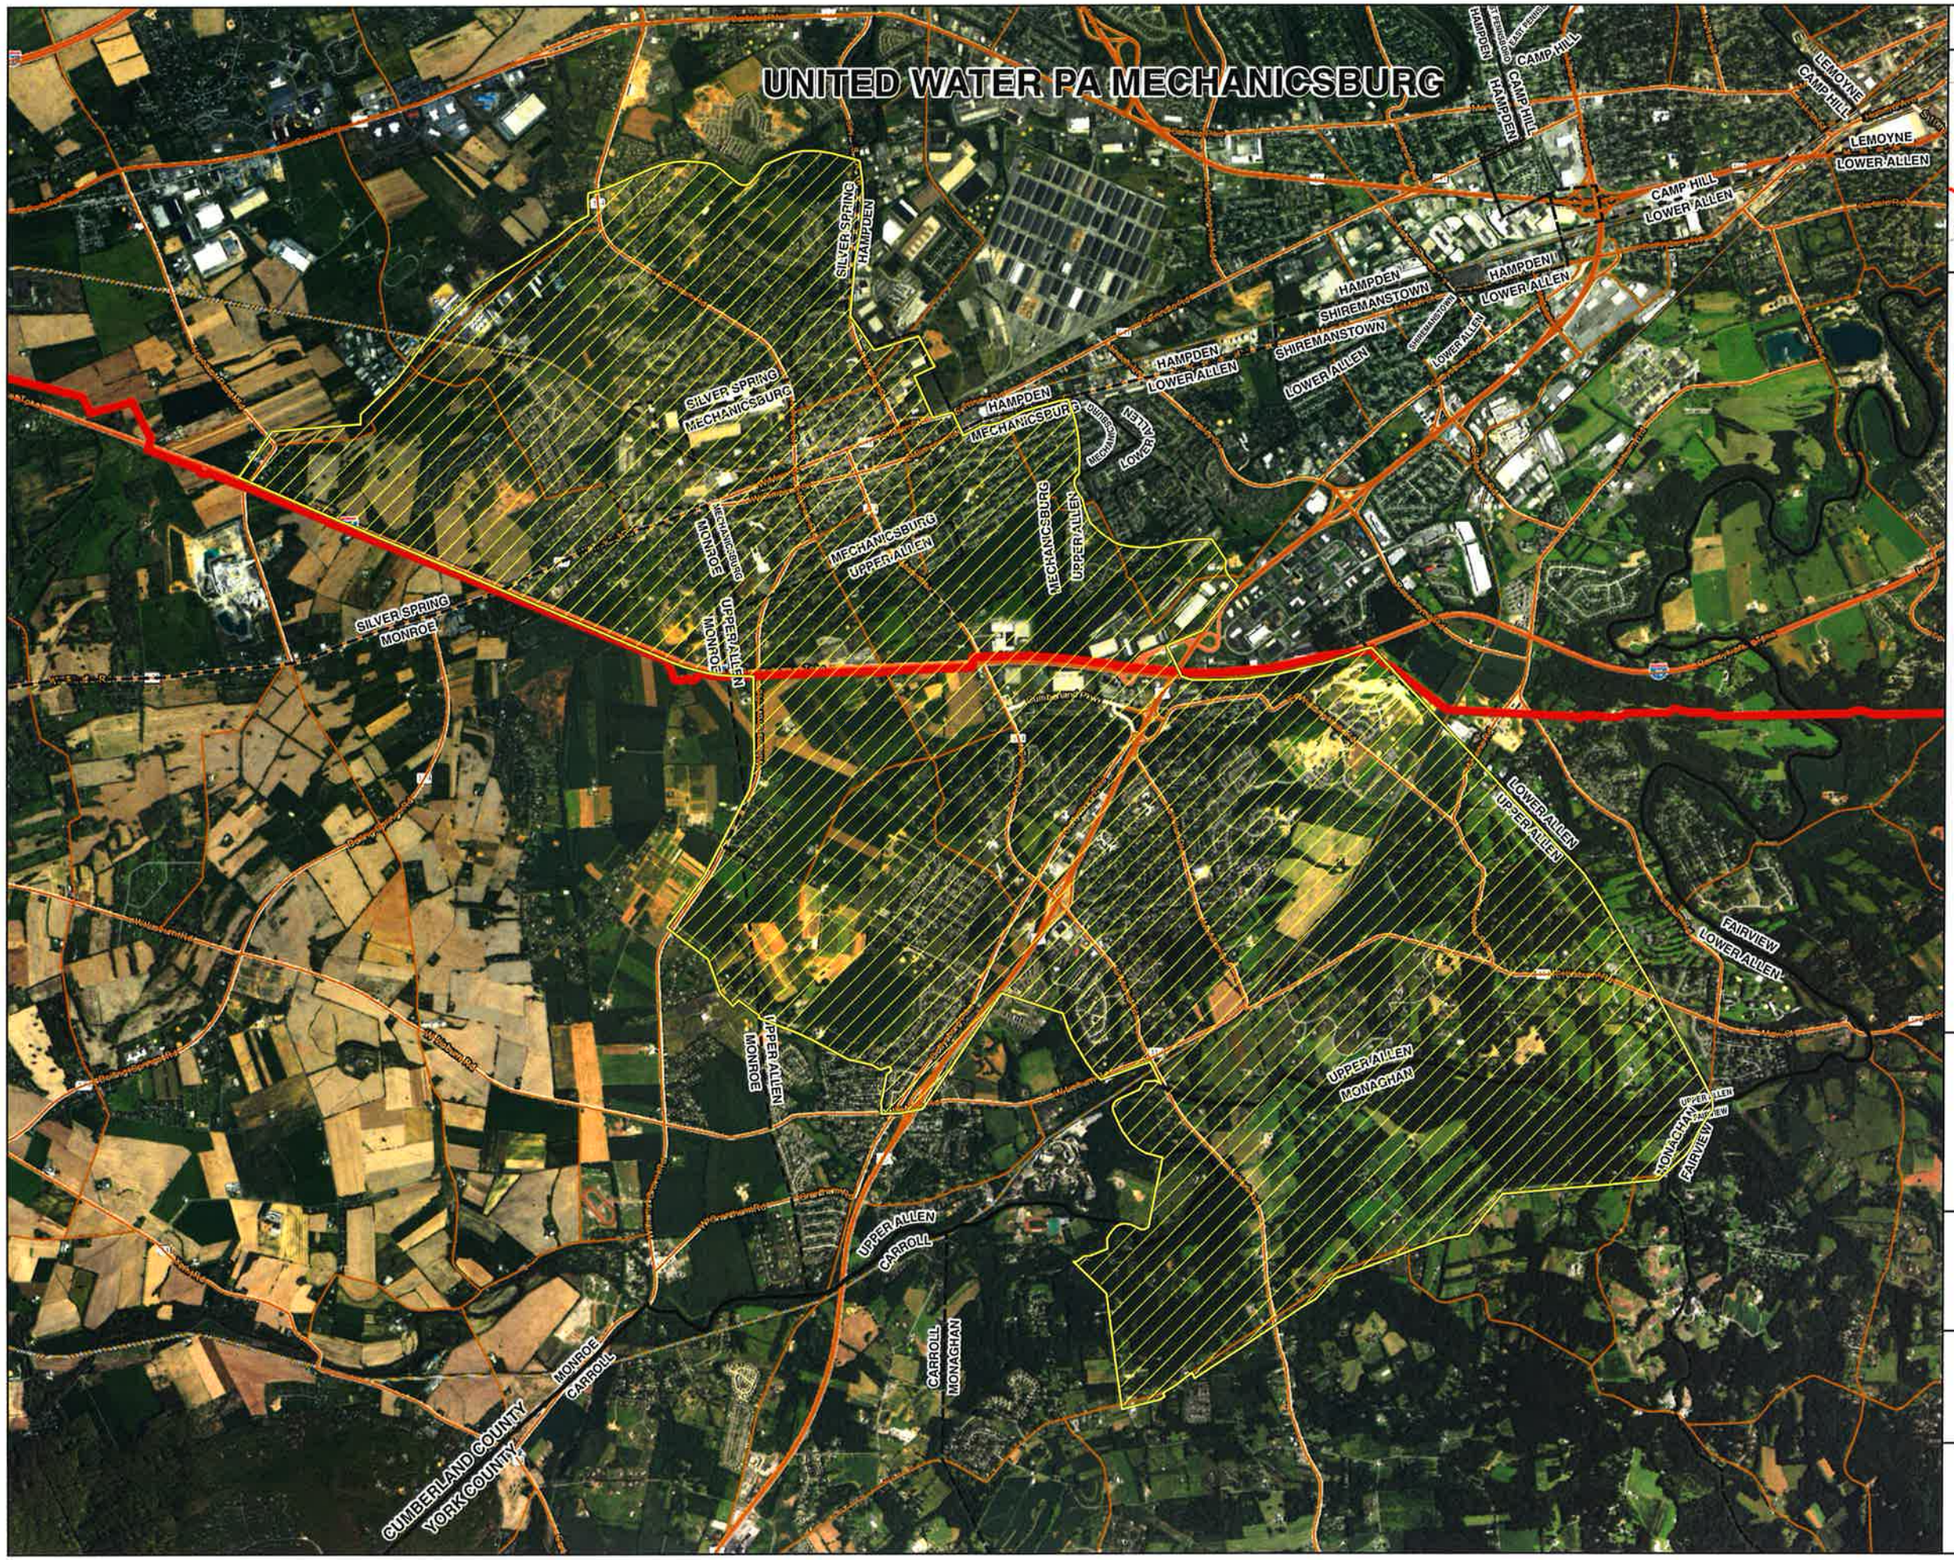

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH


Contact Report

To:	VFW Post No 8724 Telephone: 814-695-9703
Contact name:	Arlene wilt
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Arlene Wilt at VFW Post No 8724 on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 27, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

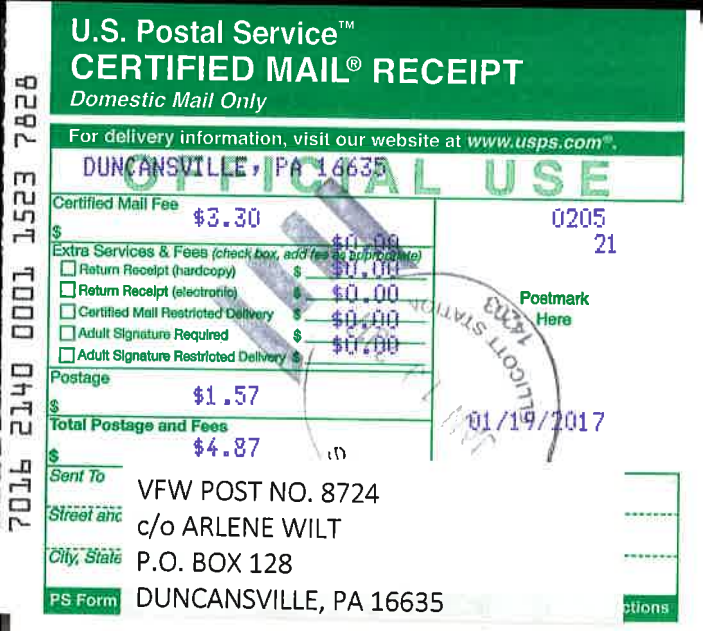

U.S. Postal Service™
CERTIFIED MAIL® RECEIPT
Domestic Mail Only

For delivery information, visit our website at www.usps.com®.

DUNCANSVILLE, PA 16635

OFFICIAL USE

Certified Mail Fee $3.30 — 0205 21

Extra Services & Fees (check box, add fee as appropriate)
- Return Receipt (hardcopy) $0.00
- Return Receipt (electronic) $0.00
- Certified Mail Restricted Delivery $0.00
- Adult Signature Required $0.00
- Adult Signature Restricted Delivery $0.00

Postage $1.57

Total Postage and Fees $4.87

Postmark Here

01/19/2017

7016 2140 0001 1523 7828

Sent To
VFW POST NO. 8724

Street and
c/o ARLENE WILT

City, State
P.O. BOX 128
DUNCANSVILLE, PA 16635

PS Form ctions

USPS.COM

USPS Tracking®

Still Have Questions?
Browse our FAQs ›

Get Easy Tracking Updates ›
Sign up for My USPS.

Tracking Number: 70162140000115237828

Product & Tracking Information

Postal Product:
First-Class Mail®

Features:
Certified Mail™

DATE & TIME	STATUS OF ITEM	LOCATION
January 27, 2017 , 9:14 am	**Delivered, Individual Picked Up at Post Office**	**DUNCANSVILLE, PA 16635**
Your item was picked up at the post office at 9:14 am on January 27, 2017 in DUNCANSVILLE, PA 16635.		
January 21, 2017 , 8:41 am	Available for Pickup	DUNCANSVILLE, PA 16635
January 20, 2017 , 11:49 pm	Arrived at USPS Destination Facility	DUNCANSVILLE, PA 16635
January 20, 2017 , 11:44 am	Arrived at USPS Destination Facility	JOHNSTOWN, PA 15904
January 19, 2017 , 9:27 pm	Arrived at USPS Origin Facility	BUFFALO, NY 14240
January 19, 2017 , 7:24 pm	Departed Post Office	BUFFALO, NY 14203
January 19, 2017 , 2:39 pm	Acceptance	BUFFALO, NY 14203

Available Actions

Text Updates

Email Updates

Track Another Package

Tracking (or receipt) number

Track It

Manage Incoming Packages

Track all your packages from a dashboard.
No tracking numbers necessary.

Sign up for My USPS ›

HELPFUL LINKS
Contact Us
Site Index
FAQs

ON ABOUT.USPS.COM
About USPS Home
Newsroom
USPS Service Updates
Forms & Publications
Government Services
Careers

OTHER USPS SITES
Business Customer Gateway
Postal Inspectors
Inspector General
Postal Explorer
National Postal Museum
Resources for Developers

LEGAL INFORMATION
Privacy Policy
Terms of Use
FOIA
No FEAR Act EEO Data

Copyright © 2017 USPS. All Rights Reserved.

TETRA TECH

January 18th, 2017

VFW POST NO 8724
c/o Arlene Wilt
P.O. Box 128
Duncansville, PA 16635

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Vinemont Comm Luth Ch Telephone: 610-670-1141
Contact name:	John Frankhauser
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to John Frankhauser at Vinemont Comm Luth Ch on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

My Profile | Support | Locations | English Search or tracking number Subı

FedEx Shipping | Tracking | Manage | Learn | FedEx Office ®

Carrie Laviolette

IMPORTANT!
Winter storms are causing unavoidable service delays in the Northwest, Midwest, and Northeast areas. Learn More

FedEx ® Tracking

778205781625

Ship date:
Wed 1/18/2017

TETRA TECH - HOME
JOSH BAIRD
301 ELLICOTT STREET
Buffalo, NY US 14203
716 849-9419

Delivery exception
LANCASTER, PA

Scheduled delivery:
Pending

Vinemont Comm Luth Ch
c/o John Frankhauser
1278 Fritztown Rd
REINHOLDS, PA US 17569
716 849-9419

Unable to deliver shipment, returned to shipper

Recommended action:
No action is required. The package is being returned to the shipper.

Travel History

Date/Time	Activity	Location
- 1/27/2017 - Friday		
12:15 pm	Returning package to shipper Return tracking number 778290756068	LANCASTER, PA
- 1/25/2017 - Wednesday		
8:21 pm	At local FedEx facility	LANCASTER, PA
- 1/24/2017 - Tuesday		
3:57 pm	At local FedEx facility	LANCASTER, PA
11:27 am	Delivery exception Customer not available or business closed	LANCASTER, PA
8:56 am	On FedEx vehicle for delivery	LANCASTER, PA
8:10 am	At local FedEx facility	LANCASTER, PA
- 1/23/2017 - Monday		
4:55 pm	At local FedEx facility	LANCASTER, PA
10:55 am	Delivery exception Customer not available or business closed	LANCASTER, PA
8:05 am	On FedEx vehicle for delivery	LANCASTER, PA
7:54 am	At local FedEx facility	LANCASTER, PA
- 1/21/2017 - Saturday		
4:49 pm	At local FedEx facility	LANCASTER, PA
- 1/20/2017 - Friday		
2:47 pm	At local FedEx facility	LANCASTER, PA
10:55 am	Delivery exception Customer not available or business closed	LANCASTER, PA
8:57 am	On FedEx vehicle for delivery	LANCASTER, PA
7:34 am	At local FedEx facility	LANCASTER, PA
- 1/19/2017 - Thursday		
4:06 pm	At local FedEx facility	LANCASTER, PA
11:33 am	Delivery exception Customer not available or business closed	LANCASTER, PA
8:50 am	On FedEx vehicle for delivery	LANCASTER, PA
8:20 am	At local FedEx facility	LANCASTER, PA
3:30 am	Departed FedEx location	NEWARK, NJ
12:18 am	Arrived at FedEx location	NEWARK, NJ
- 1/18/2017 - Wednesday		
5:12 pm	Picked up	CHEEKTOWAGA, NY
3:07 pm	Shipment information sent to FedEx	

Shipment Facts

Tracking number	778205781625	**Service**	FedEx Priority Overnight
Door tag number	DT104524556083	**Weight**	0.5 lbs / 0.23 kgs
Delivery attempts	4	**Total pieces**	1
Total shipment weight	0.5 lbs / 0.23 kgs	**Terms**	Not Available
Shipper reference	112IC05958, 16	**Packaging**	FedEx Envelope
Special handling section	Deliver Weekday	**Standard transit**	1/19/2017 by 12:00 pm

Ask FedEx

Submi

TETRA TECH

January 18th, 2017

VINEMONT COMM LUTH CH
c/o John Frankhauser
1278 Fritztown Rd
Reinholds, PA 19569

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Wernersville Muni Water Auth	Telephone: 610-678-4711
Contact name:	Mike Drobeck	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Mike Drobeck at Wernersville Muni Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received email on 9/26/16 from Nick Johnson stating no impact anticipated.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Monday, October 17, 2016 12:44 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777474177290 Delivered

Your package has been delivered

Tracking # 777474177290

Ship date:
Fri, 10/14/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Mon, 10/17/2016 12:38 pm

Wernersville Muni. Water Authority
250 N. Elm Street
WERNERSVILLE, PA 19565
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777474177290
Status:	Delivered: 10/17/2016 12:38 PM Signed for By: B.DIBIEC
Reference:	112IC05958, 16
Signed for by:	B.DIBIEC
Delivery location:	WERNERSVILLE, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.
Special handling/Services:	Adult Signature Required

	Deliver Weekday
Standard transit:	10/17/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:43 AM CDT on 10/17/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

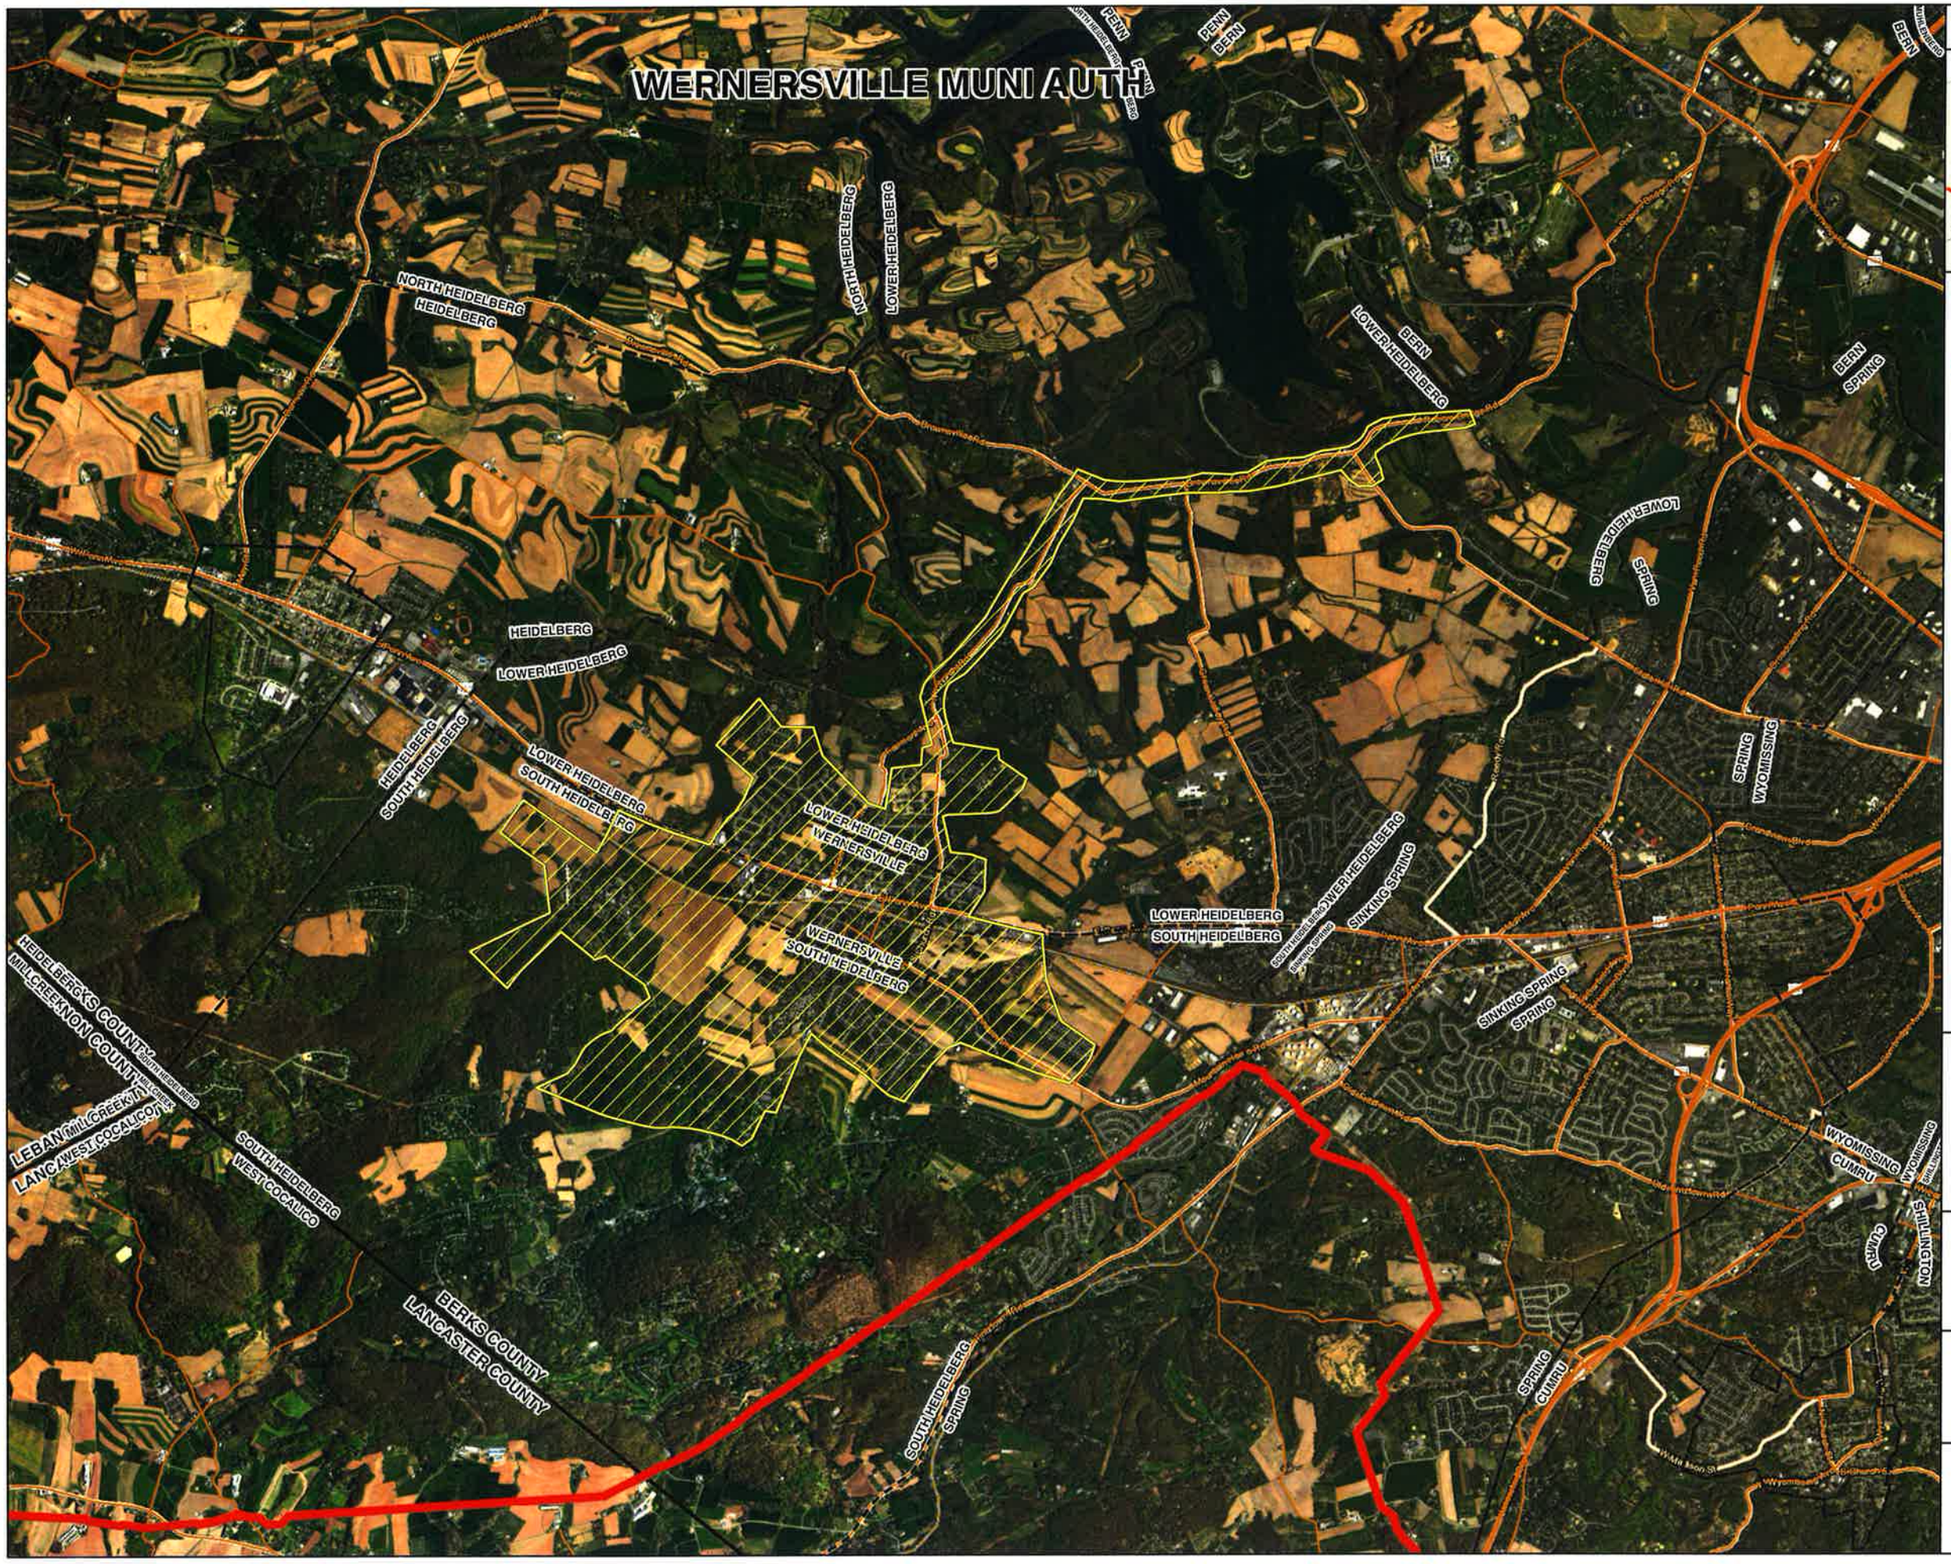

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 6,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	West Cocalico Twp Water Auth	Telephone: 717-336-8720
Contact name:	Henry Freed	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Henry Freed at West Cocalico Twp Water Auth on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Received an email on 10/5/16 stating a Letter of No Objection was signed. Received email with PDF on 10/18/16.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Tuesday, October 18, 2016 12:38 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777482333972 Delivered

Your package has been delivered

Tracking # 777482333972

Ship date:
Mon, 10/17/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Tue, 10/18/2016 12:35 pm

Henry Freed
West Cocalico Township
156 B. West Main Street PO Box 244
REINHOLDS, PA 17569
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777482333972
Status:	Delivered: 10/18/2016 12:35 PM Signed for By: T.EMERICH
Reference:	112IC05958 Task 16
Signed for by:	T.EMERICH
Delivery location:	REINHOLDS, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
Standard transit:	10/18/2016 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:38 AM CDT on 10/18/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

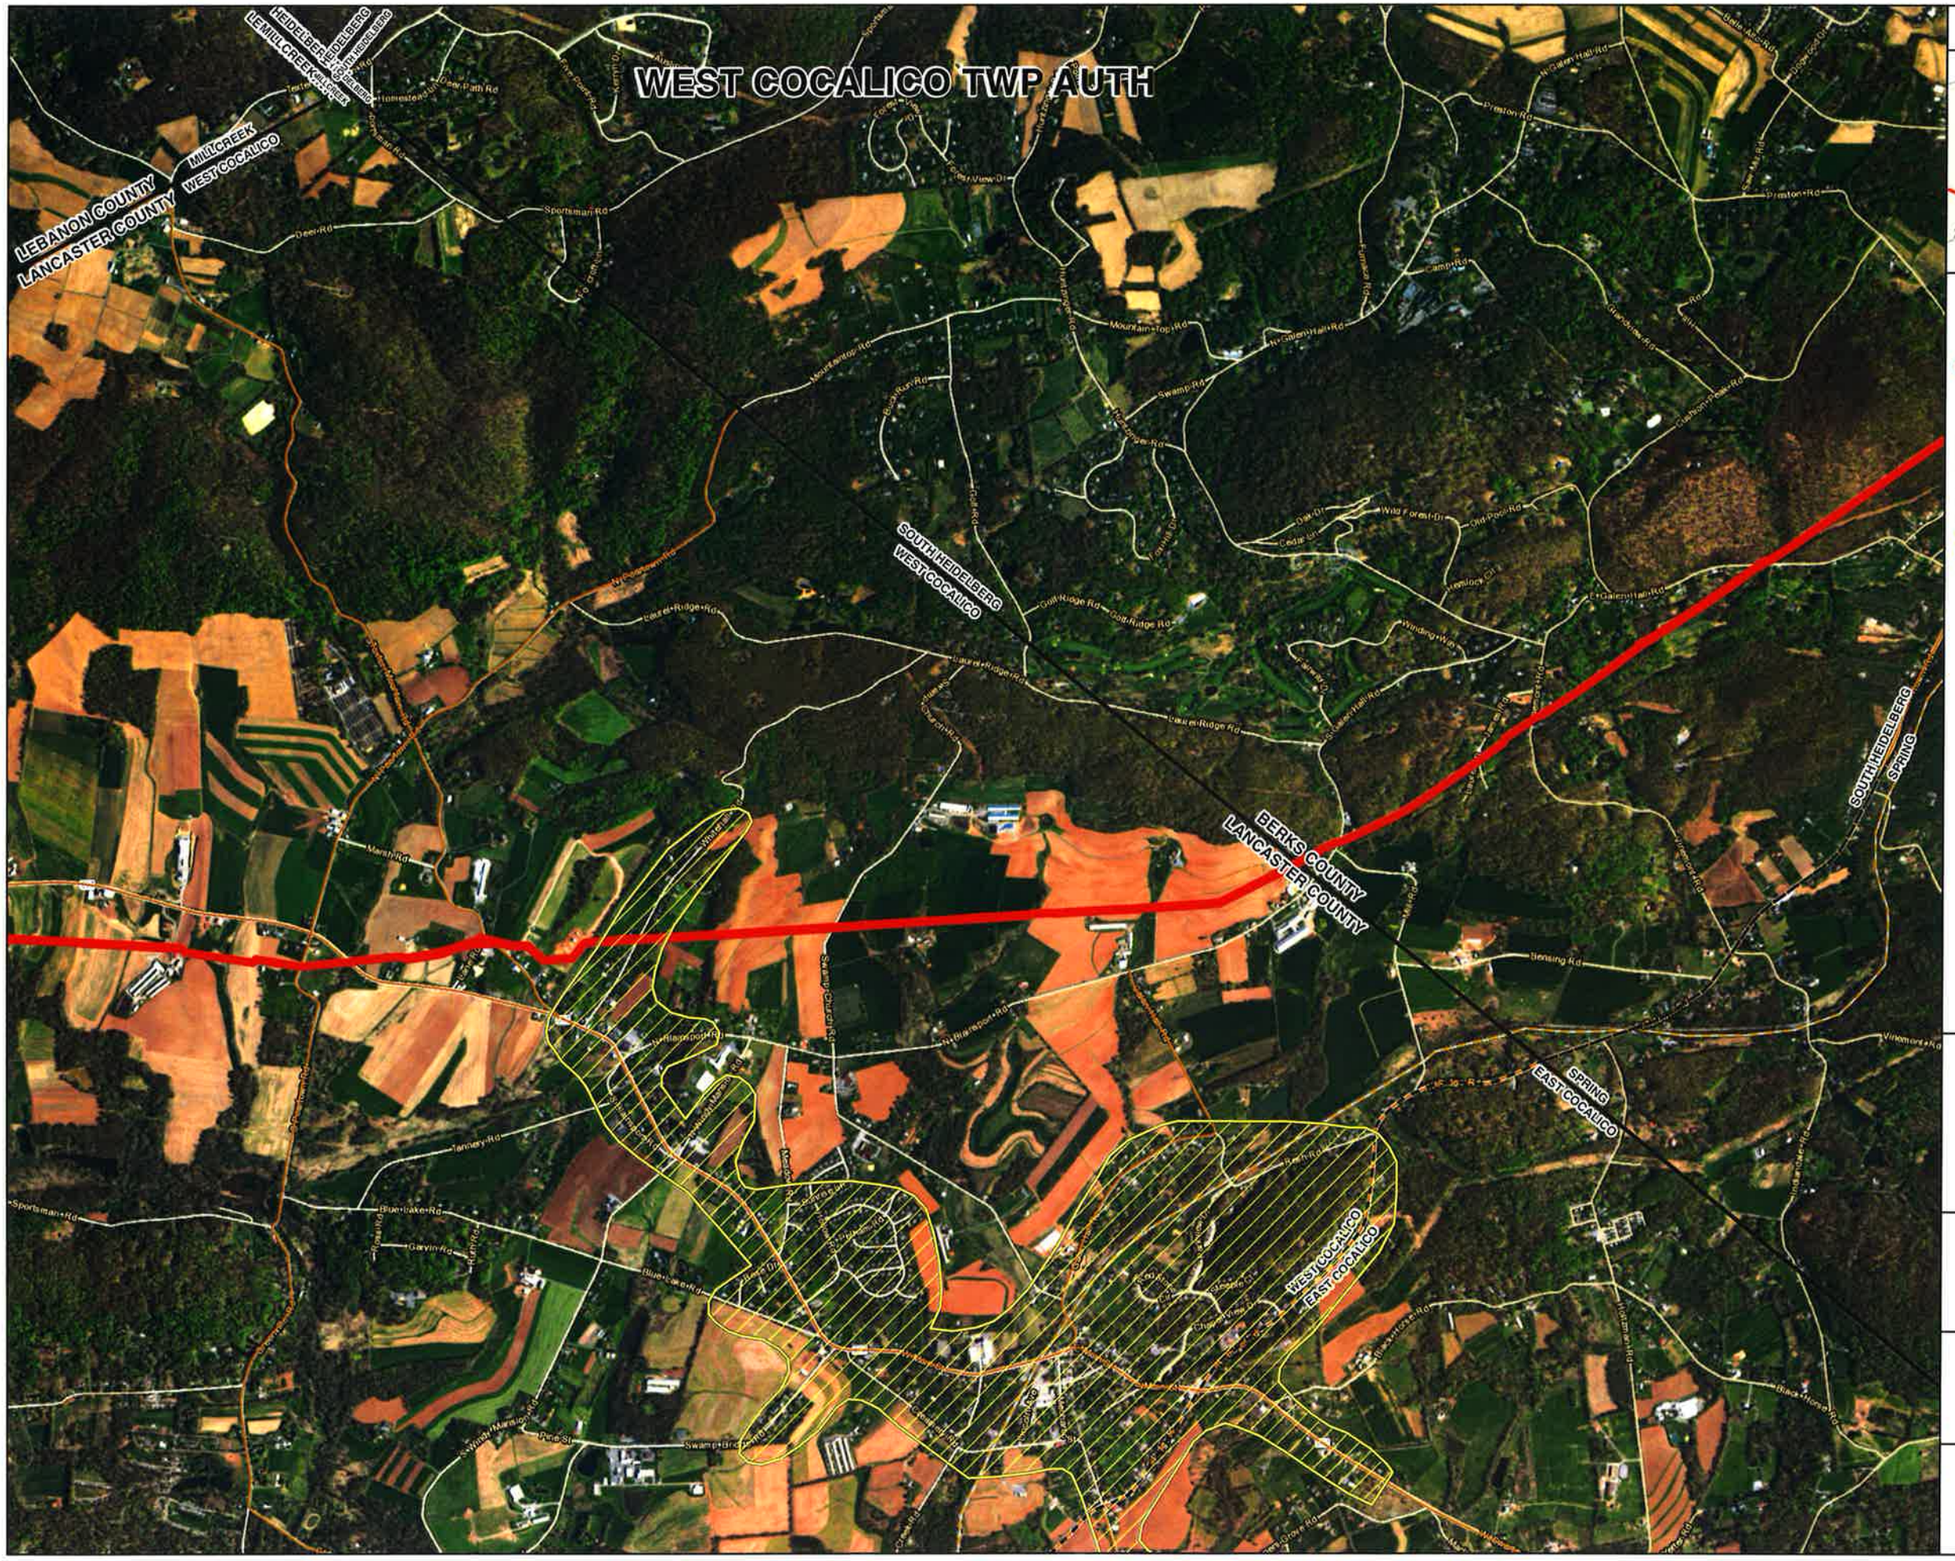

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 — 3,000 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Westmoreland Ma-Truxall Sys	Telephone: 724-727-2300
Contact name:	Chris Kerr	
From:	Josh Baird (Tt)	
Date:	September 20, 2016	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Chris Kerr at Westmoreland Ma-Truxall Sys on September 20, 2016 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question. The letter indicated that if further consultation was not initiated by October 18, SPLP will deem the Project in good standing as it relates to the PWS, and will proceed as planned.

Delivery confirmation indicated the letter was received on September 21, 2016.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: trackingupdates@fedex.com
Sent: Tuesday, October 18, 2016 12:05 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 777482405324 Delivered

Your package has been delivered

Tracking # 777482405324

Ship date:
Mon, 10/17/2016

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivery date:
Tue, 10/18/2016 11:54 am

Chris Kerr
Westmoreland Municipal Authority
124 Park and Pool Road
NEW STANTON, PA 15672
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	777482405324
Status:	Delivered: 10/18/2016 11:54 AM Signed for By: K.MOONEY
Reference:	112IC05958 Task 16
Signed for by:	K.MOONEY
Delivery location:	NEW STANTON, PA
Delivered to:	Receptionist/Front Desk
Service type:	FedEx Standard Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Adult Signature Required
	Deliver Weekday
Standard transit:	10/18/2016 by 3:00 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 11:04 AM CDT on 10/18/2016.


All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.


Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2016 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

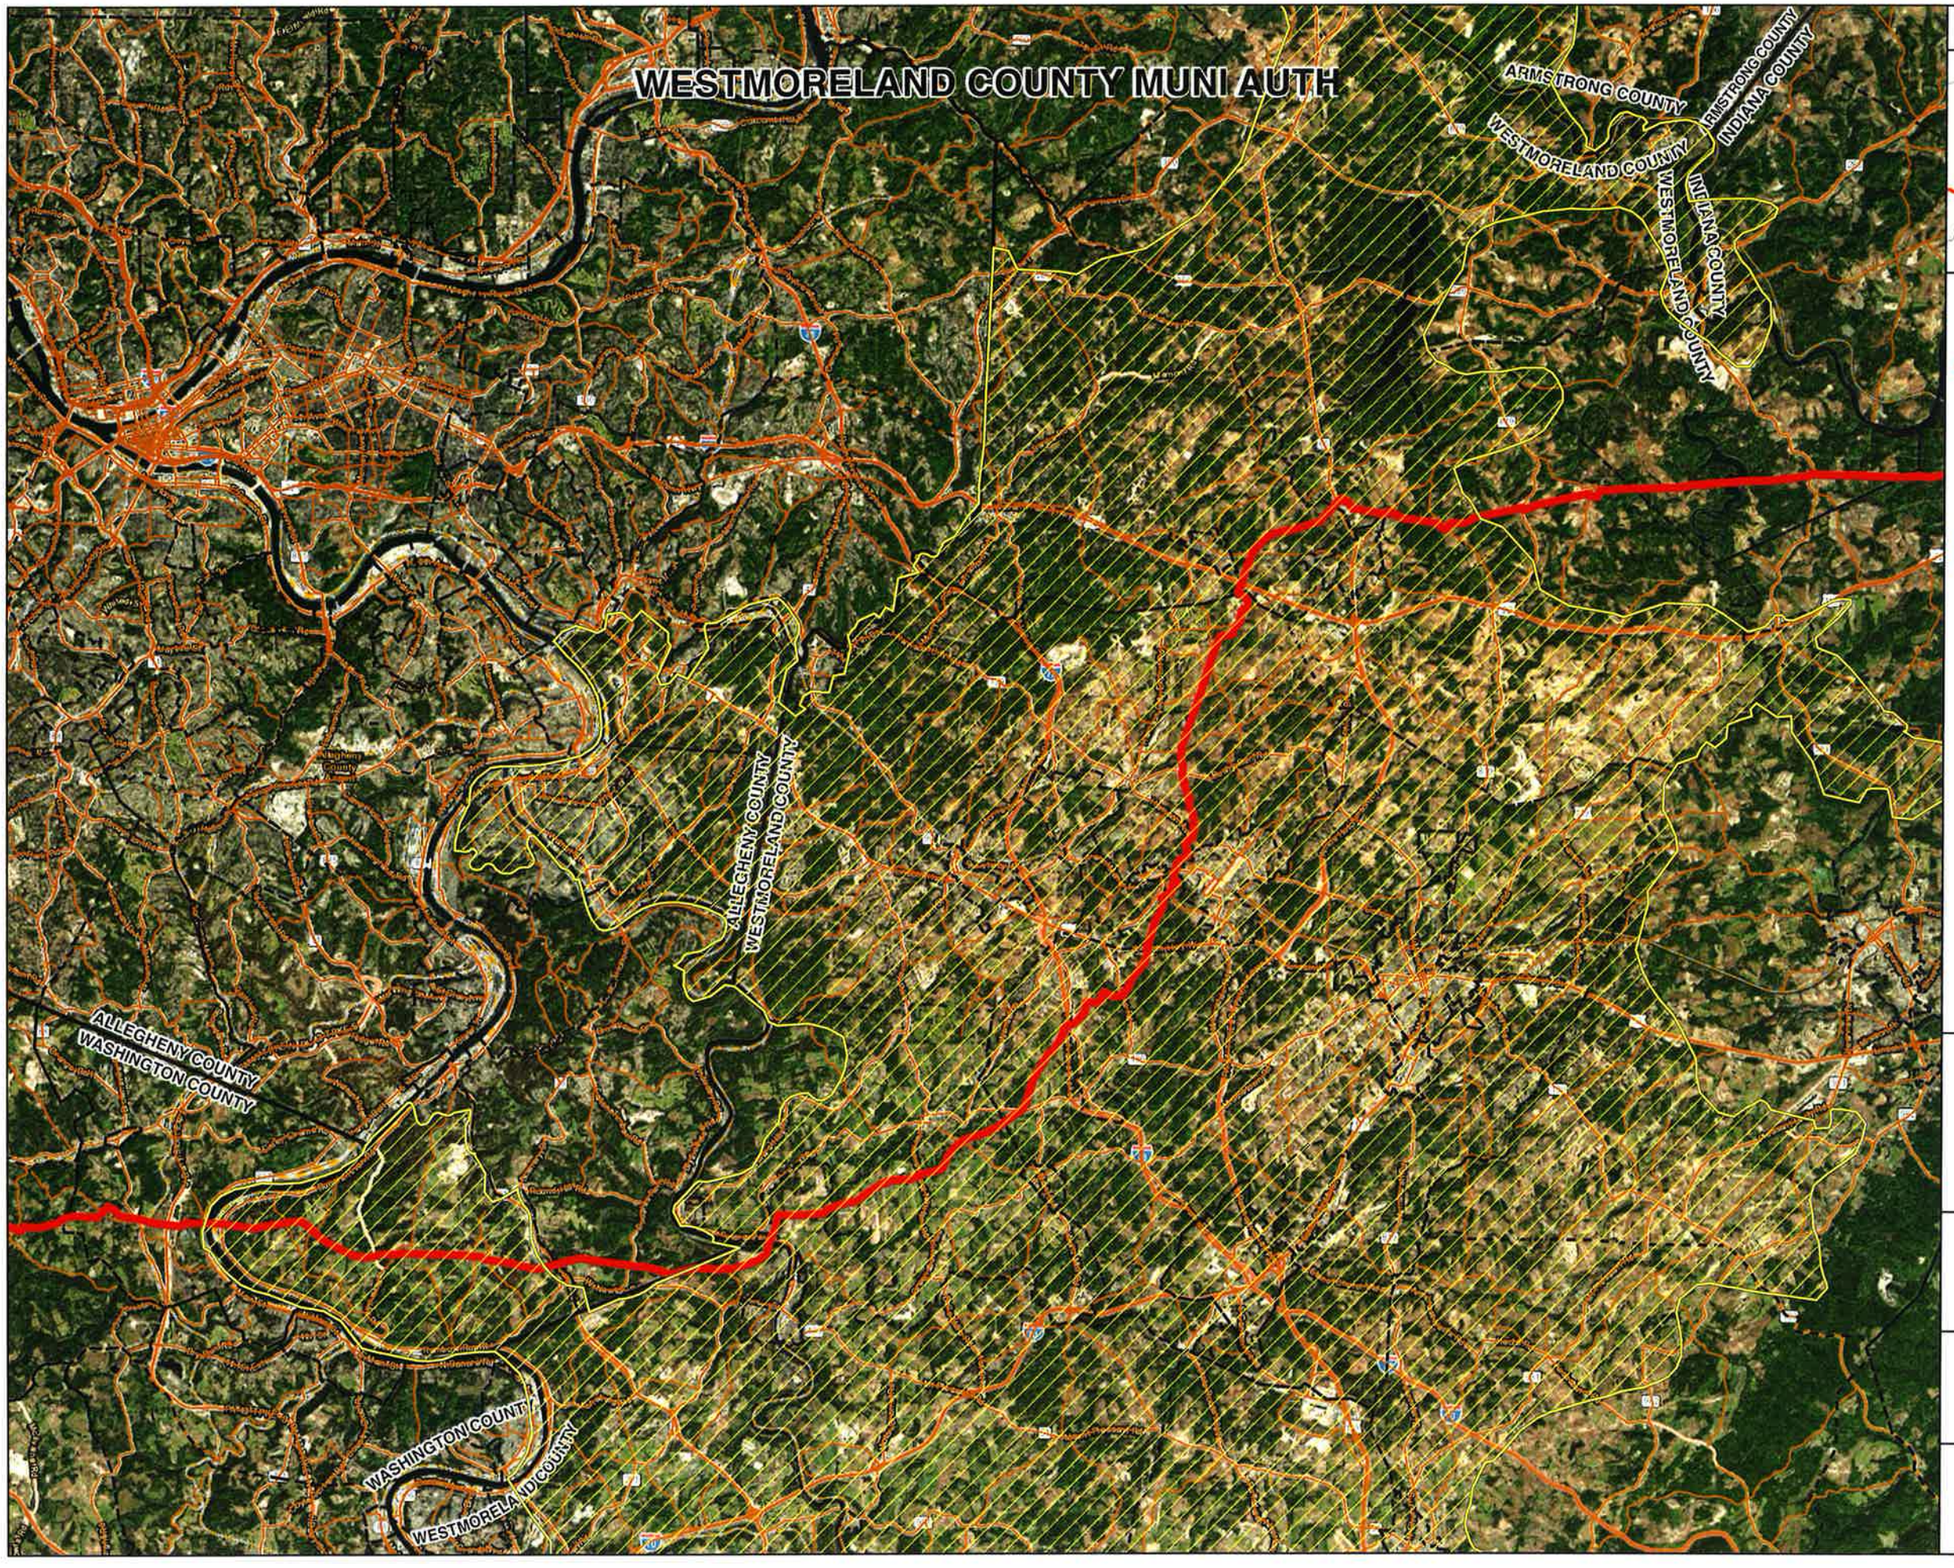

Global Indicator



Legend

- Proposed Pipeline
- PA State Roads
- PA County
- PA Municipality
- Public Water Supply Area

Sunoco PA Pipeline Project
Public Water Supply Area

0 19,500 Feet

Prepared For:

Sunoco Pipeline L.P.

Prepared By:

TETRA TECH

Date:

9/2016

Base Map;
ESRI World Imagery, October 2011
Coordinate System NAD 83
Stateplane, PA South, Feet

N

TETRA TECH

Contact Report

To:	Wildwood Family CG Telephone: 724-734-3656
Contact name:	Ammon and Katie Stoltzfus
From:	Josh Baird (Tt)
Date:	January 18, 2017
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination

A letter was sent to Ammon and Katie Stoltzfus at Wildwood Family CG on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

A phone call with Wildwood Family CG on January 19, 2017 confirmed that they are not concerned with the Project.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 3:34 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778206802417 Delivered

Your package has been delivered

Tracking # 778206802417

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 3:32 pm

c/o Ammon and Katie Stoltzfus
Wildwood Family Cg
1901 Luxemburg Rd
LYKENS, PA 17048
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778206802417
Status:	Delivered: 01/19/2017 3:32 PM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	LYKENS, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1
Weight:	0.50 lb.

Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 2:34 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

TETRA TECH

January 18th, 2017

WILDWOOD FAMILY CG
c/o Ammon And Katie Stoltzfus
1901 Luxemburg Rd Rd
Lykens, PA 17048

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,



Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

TETRA TECH

Contact Report

To:	Woodland Park Campground	Telephone: 814-472-9857
Contact name:	Edward Vorhauer	
From:	Josh Baird (Tt)	
Date:	January 18, 2017	
Subject:	Sunoco Pipeline L.P. – Pennsylvania Pipeline Project Public Water Supply Coordination	

A letter was sent to Edward Vorhauer at Woodland Park Campground on January 18, 2017 requesting information regarding Public Water Supply (PWS) source(s) and/or facility(s) in location to the Pennsylvania Pipeline Project (Project) in order to assess any potential impacts to the PWS. A brief description of the Project was included as well a Site Map related to the location of the PWS in question.

Delivery confirmation indicated the letter was received on January 19, 2017.

Tetra Tech, Inc.
285 Ellicott Street, Buffalo, New York 14203
Tel (716) 849-9419 tetratech.com

TETRA TECH

January 18th, 2017

WOODLAND PARK CAMPGROUND
c/o Edward Vorhauer
153 Rorabaugh Rd
Summerhill, PA 15958

Reference: **Sunoco Pipeline L.P. – Pennsylvania Pipeline Project**
Public Water Supply Coordination

Dear Sir or Madam,

SPLP proposes to construct and operate the Project that would expand existing pipeline systems to provide natural gas liquid (NGL) transportation. The Project involves the installation of two parallel pipelines within an approximately 306.8-mile, 50-foot-wide right-of-way from Houston, Washington County, Pennsylvania to SPLP's Marcus Hook facility in Delaware County, Pennsylvania with the purpose of interconnecting with existing SPLP Mariner East pipelines. A 20-inch diameter pipeline will be installed within the right-of-way from Houston to Marcus Hook (306.8 miles) and a second, 16-inch diameter pipeline, will also be installed in the same right-of-way. The second line is proposed to be installed from SPLP's Delmont Station, Westmoreland County, Pennsylvania to the Marcus Hook facility, paralleling the initial line for approximately 255.8 miles.

The Project includes one new 20-inch and one new 16-inch diameter pipelines installed within or adjacent to 306.8 miles of existing or new right-of-way. The majority of the new right-of-way will be co-located adjacent to existing utility corridors, including approximately 230 miles of pipeline that will be co-located in the existing SPLP Mariner East pipeline system that is currently used for the transportation of NGLs.

As part of the PADEP permit requirements, we and Sunoco respectfully request your review of the Project's location as it relates to your Public Water Supply (PWS) source(s) and/or facility(s), and assess any potential impacts to the PWS. SPLP also requests the approximate location and/or name of the waterbody that is the water supply. If you require additional information and/or consultation pertaining to the Project, please contact Joshua Baird using the contact info listed below. **If further consultation is not initiated by January 31st, SPLP will deem the Project in good standing as it relates to your PWS, and will proceed as planned**.

The following attachments are included for your review:

- Site Map showing the location of the proposed pipeline Project ROW

If you have further questions or require additional information, please do not hesitate to contact me at (716) 849-9419 or via email at Josh.Baird@TetraTech.com

Thank you for your timely response to this matter.

Sincerely,

Joshua S. Baird
Tetra Tech, Inc.

Enclosures: Site Map

301 Ellicott St, Buffalo, New York 14203
Tel 716.849.9419 Fax 716.849.9420 www.tetratech.com

Laviolette, Carrie

From: TrackingUpdates@fedex.com
Sent: Thursday, January 19, 2017 1:46 PM
To: Laviolette, Carrie
Subject: FedEx Shipment 778205905548 Delivered

Your package has been delivered

Tracking # 778205905548

Ship date:
Wed, 1/18/2017

JOSH BAIRD
TETRA TECH - HOME
Buffalo, NY 14203
US



Delivered

Delivery date:
Thu, 1/19/2017 1:41 pm

c/o Edward Vorhauer
Woodland Park Campground
153 Rorabaugh Rd
SUMMERHILL, PA 15958
US

Shipment Facts

Our records indicate that the following package has been delivered.

Tracking number:	778205905548
Status:	Delivered: 01/19/2017 1:41 PM Signed for By: Signature not required
Reference:	112IC05958, 16
Signed for by:	Signature not required
Delivery location:	SUMMERHILL, PA
Delivered to:	Residence
Service type:	FedEx Priority Overnight
Packaging type:	FedEx Envelope
Number of pieces:	1

Weight:	0.50 lb.
Special handling/Services:	Deliver Weekday
	Residential Delivery
Standard transit:	1/19/2017 by 4:30 pm

Please do not respond to this message. This email was sent from an unattended mailbox. This report was generated at approximately 12:46 PM CST on 01/19/2017.

All weights are estimated.

To track the latest status of your shipment, click on the tracking number above.

Standard transit is the date and time the package is scheduled to be delivered by, based on the selected service, destination and ship date. Limitations and exceptions may apply. Please see the FedEx Service Guide for terms and conditions of service, including the FedEx Money-Back Guarantee, or contact your FedEx Customer Support representative.

© 2017 Federal Express Corporation. The content of this message is protected by copyright and trademark laws under U.S. and international law. Review our privacy policy. All rights reserved.

Thank you for your business.

Appendix B
Well Test Plan

Pre-Construction (Baseline) Potable Well Sampling and Well Yield Testing Scope

The general scope of work and execution is provided below to document pre construction conditions at domestic wells, proximal to HDD borings, and provide a data base on water quality and well yield. This data base can be used to inspect any post HDD construction claims of suspected well impact.

WELL YIELD TESTING

If given permission from the landowner, GES shall conduct well yield testing to measure the yield of the well. These activities will be completed prior to collecting the water sample. Well yield, or specific capacity is commonly used to describe the yield capacity (performance) of a well at a given time and discharge rate. Specific capacity cannot be obtained without invasive monitoring of drawdown during pumping, discharge rate, and time or duration of pumping. For this scope, the test will be conducted for a half hour (30 minutes).

When completing a yield testing, GES shall first ask permission from the landowner to open their well at the wellhead and assess whether a water level meter can be used to measure drawdown in the well during testing. The flow volume can be determined using an outside spigot using a calibrated five-gallon bucket, a time keeping device, and a water level meter. GES will ask the property owner to not use their water during the test and will gather information about the estimated gallons of water used prior to the test. The data gathered is as follows:

- During testing, take readings at five minute intervals. The first reading should be taken upon starting the test (within the first 30 seconds). The following parameters should be recorded at each five minute interval: discharge (gallons per minute [gpm]), drawdown (feet), pH (standard units), temperature (degrees Celsius), turbidity (Nephelometric Turbidity Units [NTU]), specific conductivity (microSiemens per centimeters [µs/cm]). The time should also be recorded at each interval, as well as any additional observations that the field team makes.
- Stop the test before one hour if there is a visual change in the turbidity of the water or if the water starts to surge. If the test is stopped before one hour, record the time that the test was stopped, why the test was stopped, and take a final set of readings. Turbidity increases may indicate the well is overstressed due to excessive drawdown. Surging may indicate that the drawdown in the well may be excessive, causing the pump to suck air.
- The specific capacity will be calculated by dividing the discharge rate by the drawdown.

If a landowner does not provide permission to access the well, or a water level meter cannot be placed in the well, the test can be completed, but drawdown will not be measured and specific capacity will not be calculated; however the discharge rate and the field-measured parameters can be monitored and recorded. If a landowner does not provide permission to complete well yield testing, this will be documented and the test will not be completed.

If a property owner wants flow testing to be completed, but does not agree to a full 30 minute test, a shorter test can be completed and the reason for completing a shorter test will be documented.

FIELD SAMPLING/TESTING ITEMS

Water samples will be collected in accordance with standard industry sampling techniques. For the purposes of this scope it will be assumed that water samples will be collected preferably from the pressure

tank, but if that location is not available or accessible, then the samples will be collected from an alternate location such as an indoor tap, outdoor spigot, or free flowing pipe. Where water treatment systems are present, GES will make all reasonable attempts to collect the water sample prior to any treatment system. If unable to collect a pre-treatment sample, GES will document the conditions and collect post-treatment.

If well yield testing is completed, then additional purging of the water source is not needed before the water sample is collected. If well yield testing is not completed, then the well will be purged before sample collection. Purge volumes will be two times the pressure tank volume. If there is no pressure tank, approximately 60 gallons will be purged. If a reduced purge is requested by the landowner, a minimum of ten gallons will be purged and the reason for a reduced purge will be documented. After purging, GES will collect one sample at each well location and submit to an SXL-approved laboratory for analysis of the following:

	Parameters
Inorganics	pH
	Specific Conductance
	Turbidity
	Total Dissolved Solids (TDS)
	Total Suspended Solids (TSS)
	Hardness
	Anions: Bromide, Chloride, Sulfate
	Total Alkalinity
Trace Metals	Metals Analysis: (Ba, Ca, Fe, K, Mg, Mn, Na)
Organics	BTEX
	Light Gas Analysis [Methane, ethane, Propane]

Field equipment will consist of a YSI water-quality meter, turbidity meter, photo-ionization detector (PID), digital camera, hand-held GPS unit, laboratory-supplied bottleware, calibrated five-gallon bucket, tubing, hand tools, water level meter, plastic sheeting, and decontamination materials. The following items will be documented on the Field Data Survey form.

- Sketch of parcel boundaries, parcel features, and water source location
- Water use (domestic or livestock)
- Well information (if known)
    - Vented
    - Depth
    - Diameter
    - Pump Depth
    - Water Level
    - Year Well Installed
    - Seasonal Information
- GPS location of source in decimal degrees format
- Pressure tank size
- Treatment system description and photographs

- Sample collected pre- or post-treatment
- Purge volume (at a minimum twice the pressure tank size)
- Water quality data (pH, conductivity, temperature, turbidity, and VOCs)
- Well yield testing measurements (as detailed above)
- Photographs
- Observations related to well integrity and/or the condition of the environment surrounding the well

Appendix C
Hydrogeological Review and Aquifer Assessment

Hydrogeologic Review and Aquifer Assessment

Groundwater & Environmental Services, Inc. (GES) reviewed certain information described below to identify potential Inadvertent Return (IR) problem areas. GES assembled information related to certain parameters associated with aquifers to assess the relative risk of IRs at HDDs. Of the 17 counties that the proposed Pennsylvania Pipeline Project (PPP) crosses, GES reviewed HDD profiles and supplemental information for nine of the counties where geologies representative of all HDD crossings were evaluated, which are, from west to east: Washington, Allegheny, Westmoreland, Cumberland, Huntingdon, Lebanon, Lancaster, Chester, and Delaware.

For this assignment, GES reviewed the following information:

- HDD locations from the pipeline map
- Identification of geology (i.e., underlying formation) at each HDD location, including:
    - Soils Types and Thicknesses
    - Bedrock type, thickness
    - Structural features (i.e., faults, dikes)
    - Groundwater depth, yield
    - Topography
- Identification of surface water features and classifications
    - Streams (i.e., High Quality, Exception Value, etc.)
    - Wetlands
- Identification of Water Supplies within 200 feet of the HDDs
    - Private Water Supply Wells and Springs
    - Public Water Supply Well Source Water Protection Areas

Concurrently, GES had conversations with the TetraTech design team members and with the HDD drilling contractor to ascertain the risks of potential IRs in aquifers. GES provided resources consisting of Professional Registered Geologists and geologic specialists to conduct a hydrogeologic review of pertinent project files that were made available to GES, which also included the Water Supply Plan, the Void Mitigation Plan for Karst Terrain and Underground Mining and the HDD Inadvertent Return Assessment, Preparedness, Prevention and Contingency Plan (IR Plan).

Based on previous drilling and installation experience with the ME1 pipeline, the IR risk for many of the HDDs required for the PPP was assigned as “low.” GES recommended that the IR risk be elevated to “medium” in circumstances where HDDs are advanced in karst terrain, through faulted bedrock, and in areas where ME1 experienced problematic IRs. None of the HDDs were assigned a “high” risk for an inadvertent return.

In addition to the planning undertaken to locate and design the HDDs, aquifer resources will be further protected through the implementation of the measures described in the IR Plan, the Water Supply Plan and the Void Mitigation Plan.
